

Phezukomoya

PHEZ · 145.6 MW installed


Full History

Phezukomoya: the plant produced 35.0 GWh, significantly below P50 and P90 targets. Contractual availability averaged 99.5%, while technical availability was lower at 94.2%. The negative delta in production was visible in the wind resource deviation of -18%.


FULL KPI MATRIX

CATEGORY	2026	FEB	MAR	APR	MAY	JUN	JUL	TOTAL
A. Production								
Measured (MWh)	203,288	31,758	34,015	41,027	29,164	32,348	34,975	203,288
Deviation Historical	–	–	–	–	–	–	–	–
Deviation P50	-33.8%	-18.7%	-29.5%	-13.8%	-46.7%	-44.7%	-40.9%	-33.8%
Deviation P90	-26.7%	-9.9%	-21.9%	-4.5%	-40.9%	-38.8%	-34.5%	-26.7%
Capacity Factor	32.6%	32.8%	31.9%	39.7%	27.3%	31.3%	32.8%	32.6%
Electrical Losses	1.4%	1.2%	1.5%	1.5%	1.3%	1.4%	1.4%	1.4%
B. Consumption								
Measured (MWh)	138	38	15	15	14	31	25	138
Ratio to Production	0.1%	0.1%	0.0%	0.0%	0.0%	0.1%	0.1%	0.1%
C. Availability								
TBA - Contractual	99.8%	–	100.0%	100.0%	99.8%	99.9%	99.5%	99.8%
TBA - Technical	97.3%	97.3%	99.1%	98.7%	97.1%	97.3%	94.2%	97.3%
PBA - Technical	97.7%	94.5%	98.8%	97.9%	96.5%	99.0%	99.4%	97.7%
D. OLF - Losses								
Manufacturer	13.2%	5.9%	5.2%	14.0%	33.5%	15.0%	5.3%	13.2%
Owner	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.2%	0.0%
Environmental	1.3%	0.0%	0.0%	1.1%	3.7%	1.2%	1.9%	1.3%
Utility	4.5%	0.0%	0.0%	0.1%	0.3%	9.6%	17.0%	4.5%
Bat Curtailment	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%
E. Wind								
Forecasted WS (m/s)	8.5	8	8	8	8.7	9.3	9.1	8.5
Measured WS (m/s)	7.5	7.3	6.8	8	8.1	7.4	7.4	7.5
WindSpeed Deviation	-11.4%	-8.3%	-15.1%	0.4%	-6.2%	-20.6%	-18.4%	-11.4%


PLANT PRODUCTION

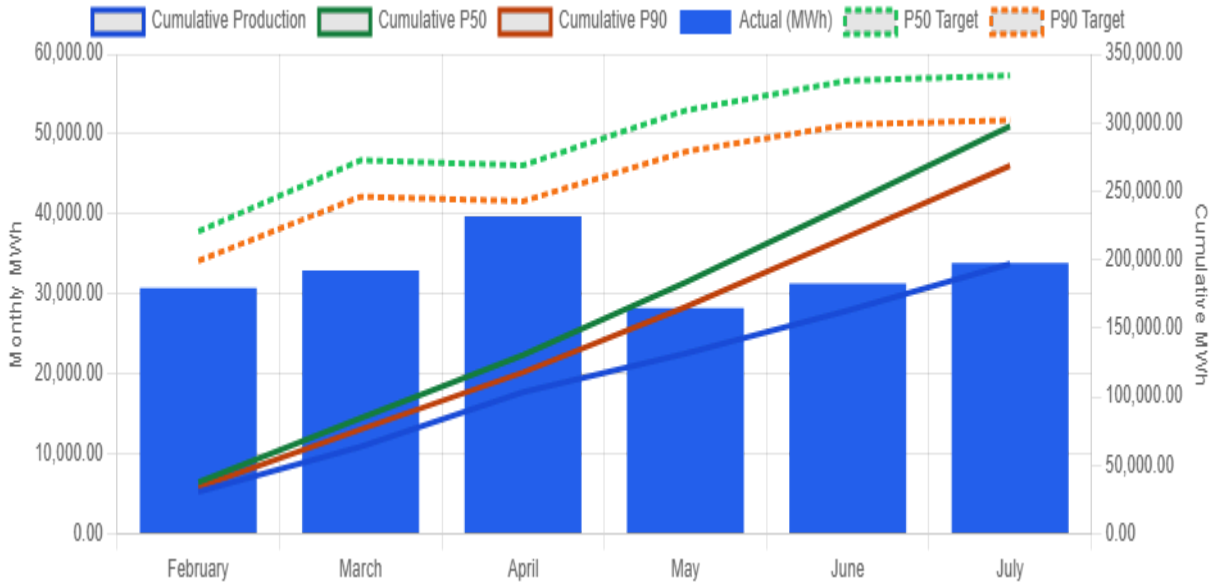


ANNUAL PRODUCTION AND AVAILABILITY PER WT

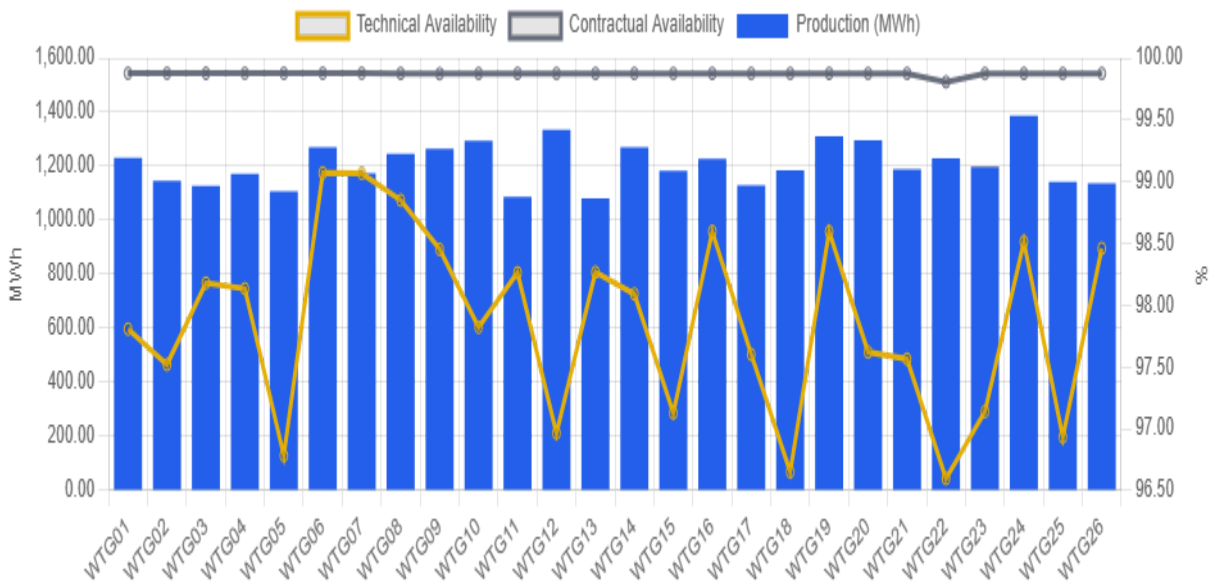

PLANT AVAILABILITY

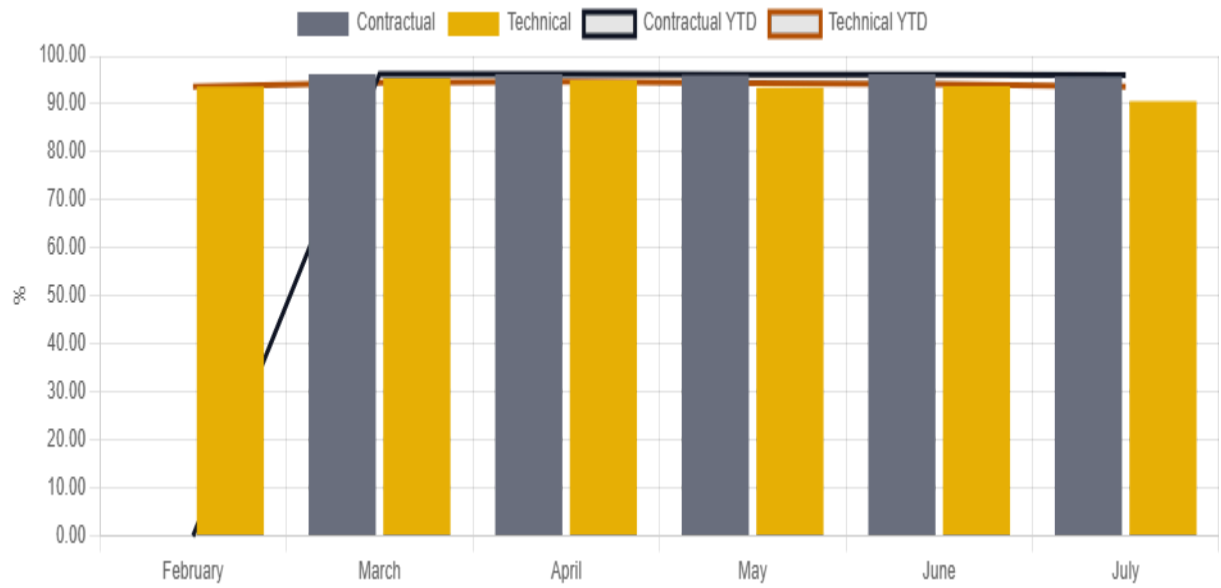

OPERATIONAL LOSS FACTORS

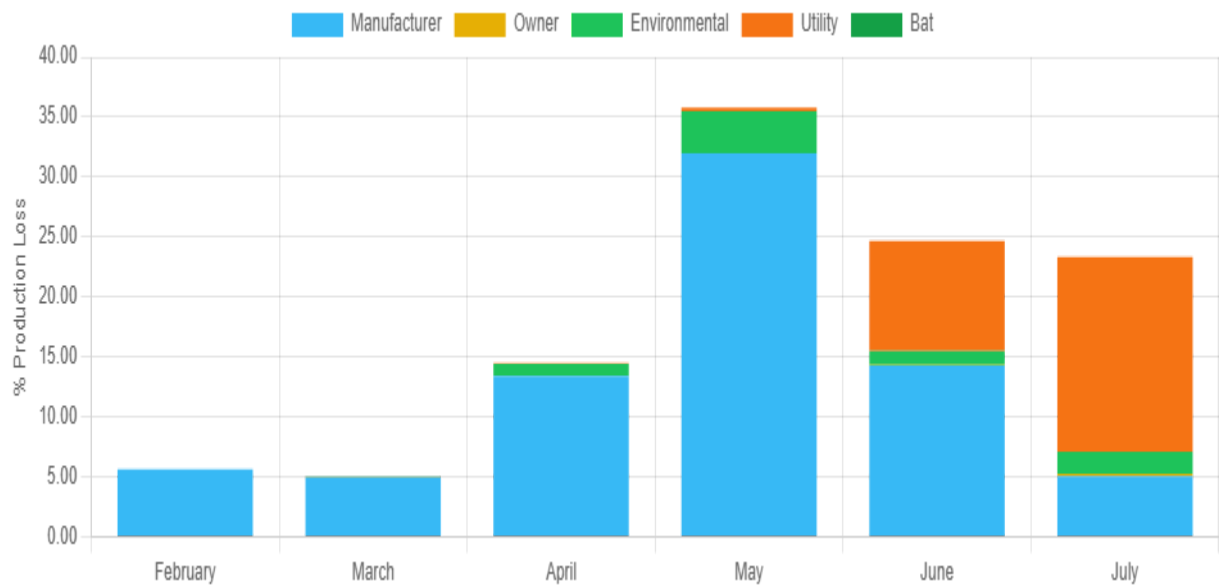

WIND SPEED

