


Phezukomoya: the plant produced 27.6 GWh, significantly below P50 and P90 targets. Contractual availability averaged 85.9%, while technical availability was lower at 80.1%. The negative delta in production was visible in the wind resource deviation of -21%.


FULL KPI MATRIX

CATEGORY	2026	FEB	MAR	APR	MAY	JUN	JUL	AUG	TOTAL
A. Production									
Measured (MWh)	230,848	31,758	34,015	41,027	29,164	32,348	34,975	27,560	230,848
Deviation Historical	-	-	-	-	-	-	-	-	-
Deviation P50	-37.3%	-18.7%	-29.5%	-13.8%	-46.7%	-44.7%	-40.9%	-54.9%	-37.3%
Deviation P90	-30.6%	-9.9%	-21.9%	-4.5%	-40.9%	-38.8%	-34.5%	-50.0%	-30.6%
Capacity Factor	31.6%	32.8%	31.9%	39.7%	27.3%	31.3%	32.8%	25.8%	31.6%
B. Consumption									
Measured (MWh)	177	38	15	15	14	31	25	39	177
Ratio to Production	0.1%	0.1%	0.0%	0.0%	0.0%	0.1%	0.1%	0.1%	0.1%
C. Availability									
TBA - Contractual	97.5%	-	100.0%	100.0%	99.8%	99.9%	99.5%	85.9%	97.5%
TBA - Technical	94.8%	97.3%	99.1%	98.7%	97.1%	97.3%	94.2%	80.1%	94.8%
PBA - Technical	78.5%	94.3%	95.0%	84.9%	62.2%	74.0%	75.8%	63.3%	78.5%
D. Losses Breakdown									
Grid	8.2%	-	0.0%	0.1%	0.4%	9.6%	16.6%	22.2%	8.2%
Breakdown	3.2%	-	-	-	0.1%	0.1%	0.1%	12.6%	3.2%
Maintenance	0.1%	-	-	-	0.1%	-	0.2%	0.1%	0.1%
Partial Perf.	9.4%	0.7%	4.0%	12.0%	30.2%	14.1%	4.8%	0.1%	9.4%
Environmental	0.3%	0.3%	0.3%	0.1%	0.2%	0.7%	0.4%	0.1%	0.3%
Data Quality	2.2%	5.5%	1.2%	2.1%	3.2%	0.8%	0.2%	-	2.2%
Requested Shutdown	0.1%	-	-	0.1%	0.0%	0.0%	0.2%	0.0%	0.1%
Electrical Losses	1.1%	1.1%	1.3%	1.2%	0.8%	1.0%	1.1%	1.0%	1.1%
BoP	0.1%	-	-	-	-	0.0%	0.1%	0.1%	0.1%
Bird	1.0%	-	-	-	0.2%	0.7%	1.4%	1.6%	1.0%
Icing	1.2%	-	-	1.1%	3.5%	0.0%	0.1%	-	1.2%
E. Wind									
Forecasted WS (m/s)	8.6	8	8	8	8.7	9.3	9.1	9.4	8.6
Measured WS (m/s)	7.5	7.3	6.8	8	8.1	7.4	7.4	7.4	7.5
WindSpeed Deviation	-12.8%	-8.3%	-15.1%	0.4%	-6.2%	-20.6%	-18.4%	-21.3%	-12.8%


PLANT PRODUCTION

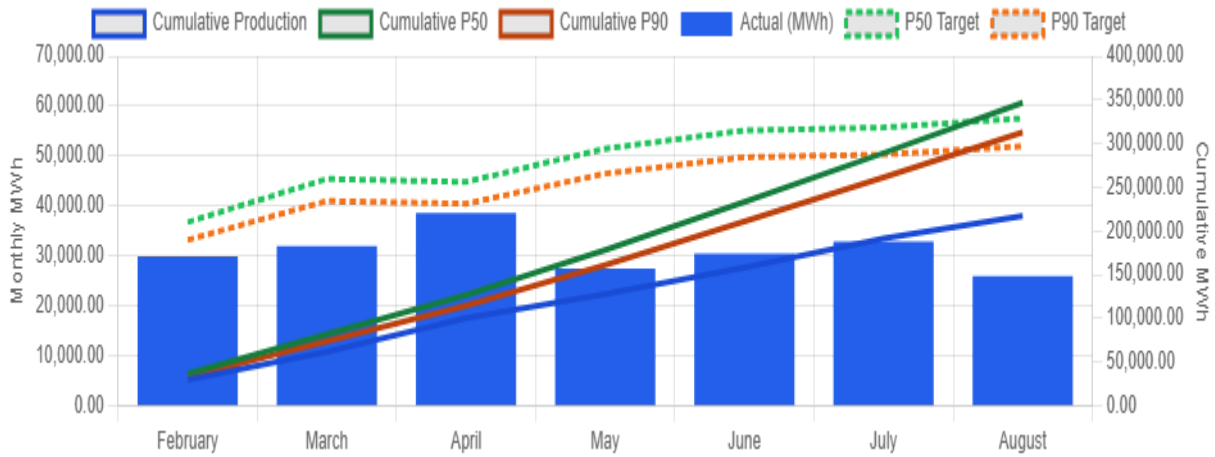


PLANT AVAILABILITY

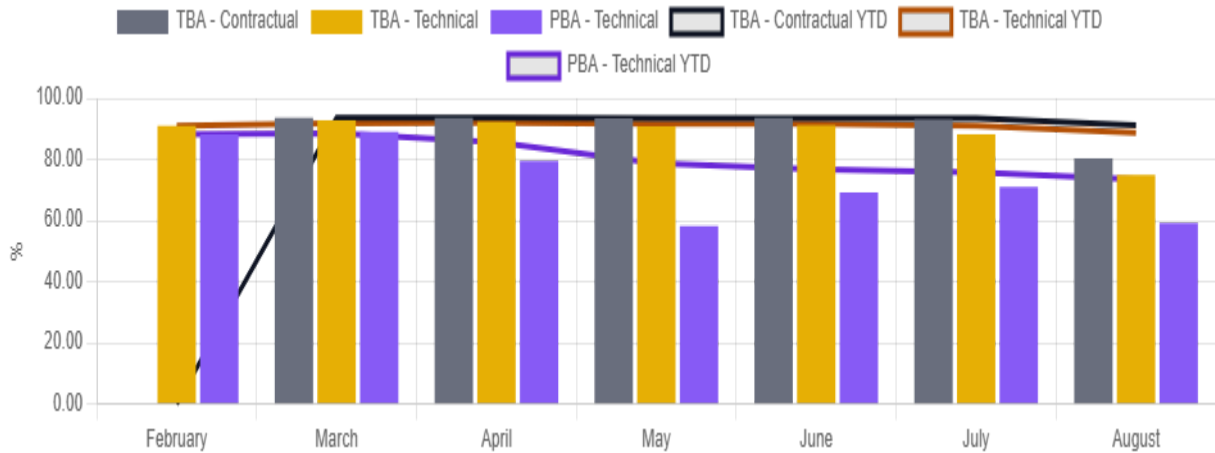

WIND SPEED

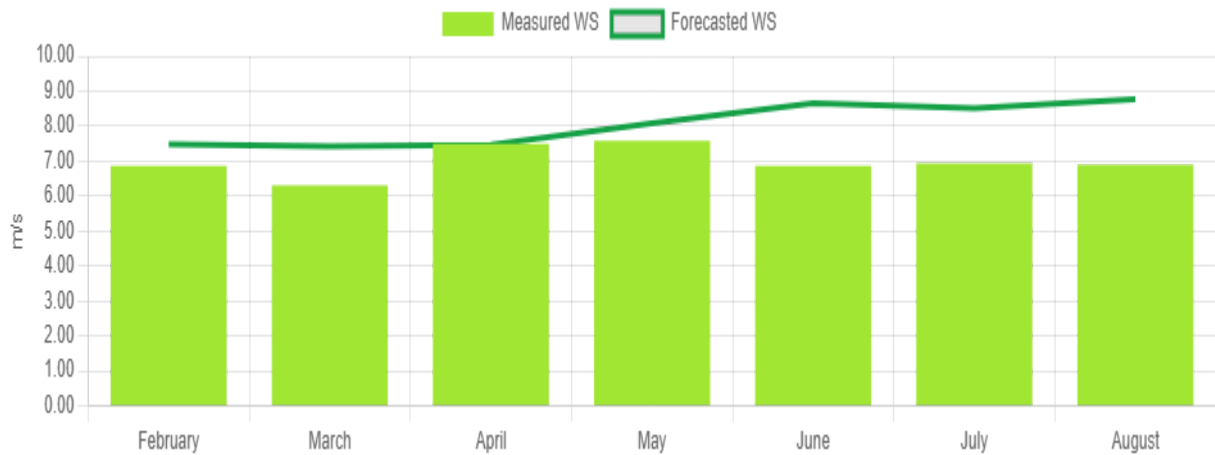

ANNUAL PRODUCTION AND AVAILABILITY PER WT

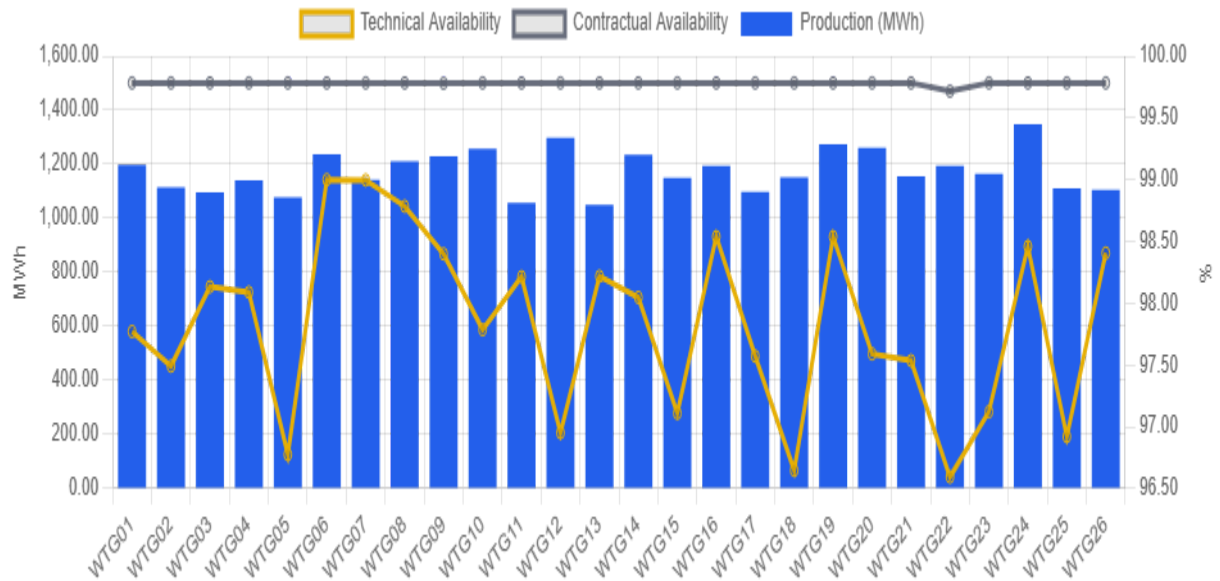

LOSSES BREAKDOWN

