


Coleskop: the plant produced 38.7 GWh, significantly below P50 and P90 targets. Contractual availability averaged 99.4%, while technical availability was lower at 96.0%. The negative delta in production was visible in the wind resource deviation of -8%.


FULL KPI MATRIX

CATEGORY	2026	FEB	MAR	APR	MAY	JUN	JUL	TOTAL
A. Production								
Measured (MWh)	197,370	8,096	36,822	44,460	33,537	35,741	38,713	197,370
Deviation Historical	-	-	-	-	-	-	-	-
Deviation P50	-31.0%	-33.2%	-22.6%	-6.6%	-40.1%	-40.9%	-37.9%	-31.0%
Deviation P90	-22.2%	-24.7%	-12.7%	5.4%	-32.4%	-33.3%	-30.0%	-22.2%
Capacity Factor	31.1%	8.1%	34.3%	42.4%	31.1%	34.4%	36.2%	31.1%
Electrical Losses	0.3%	-1.8%	0.9%	-0.1%	0.5%	0.9%	1.4%	0.3%
B. Consumption								
Measured (MWh)	78	0	28	9	12	29	0	78
Ratio to Production	0.0%	0.0%	0.1%	0.0%	0.0%	0.1%	0.0%	0.0%
C. Availability								
TBA - Contractual	99.0%	96.7%	99.8%	99.3%	99.7%	99.4%	99.4%	99.0%
TBA - Technical	96.0%	95.0%	95.5%	95.6%	97.2%	96.5%	96.0%	96.0%
PBA - Technical	96.7%	88.2%	98.8%	98.4%	97.6%	98.9%	98.6%	96.7%
D. OLF - Losses								
Manufacturer	6.4%	10.8%	3.2%	4.1%	10.7%	5.4%	4.5%	6.4%
Owner	0.5%	0.3%	0.7%	0.8%	0.2%	0.2%	0.9%	0.5%
Environmental	1.0%	0.8%	0.4%	2.0%	0.8%	1.0%	1.2%	1.0%
Utility	13.0%	0.2%	5.5%	9.1%	25.1%	20.7%	17.3%	13.0%
Bat Curtailment	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%
E. Wind								
Forecasted WS (m/s)	8	7.5	7.5	7.5	8.1	8.7	8.5	8
Measured WS (m/s)	7.9	6.9	7.1	8.6	8.9	8	7.8	7.9
WindSpeed Deviation	-0.8%	-9.0%	-4.6%	14.2%	10.1%	-7.8%	-7.6%	-0.8%


PLANT PRODUCTION

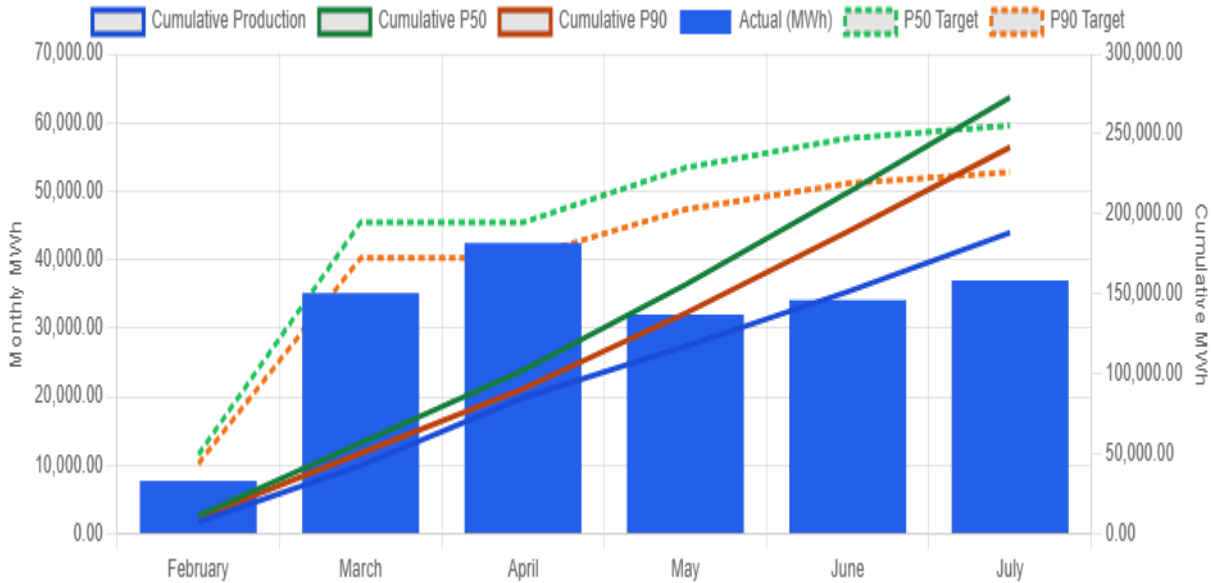


ANNUAL PRODUCTION AND AVAILABILITY PER WT

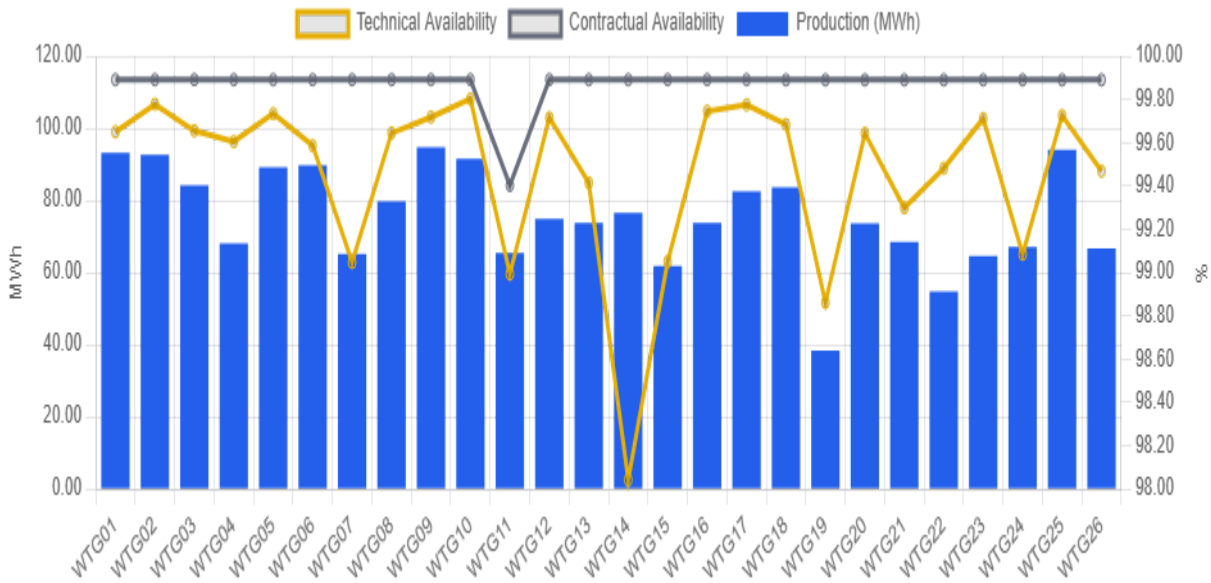

PLANT AVAILABILITY

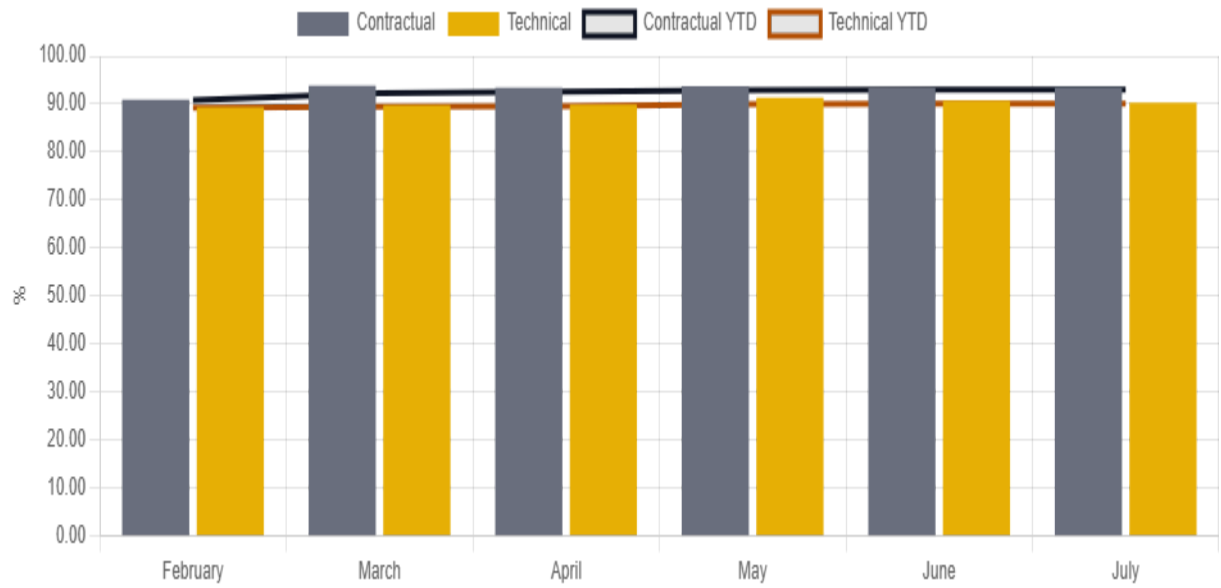

OPERATIONAL LOSS FACTORS

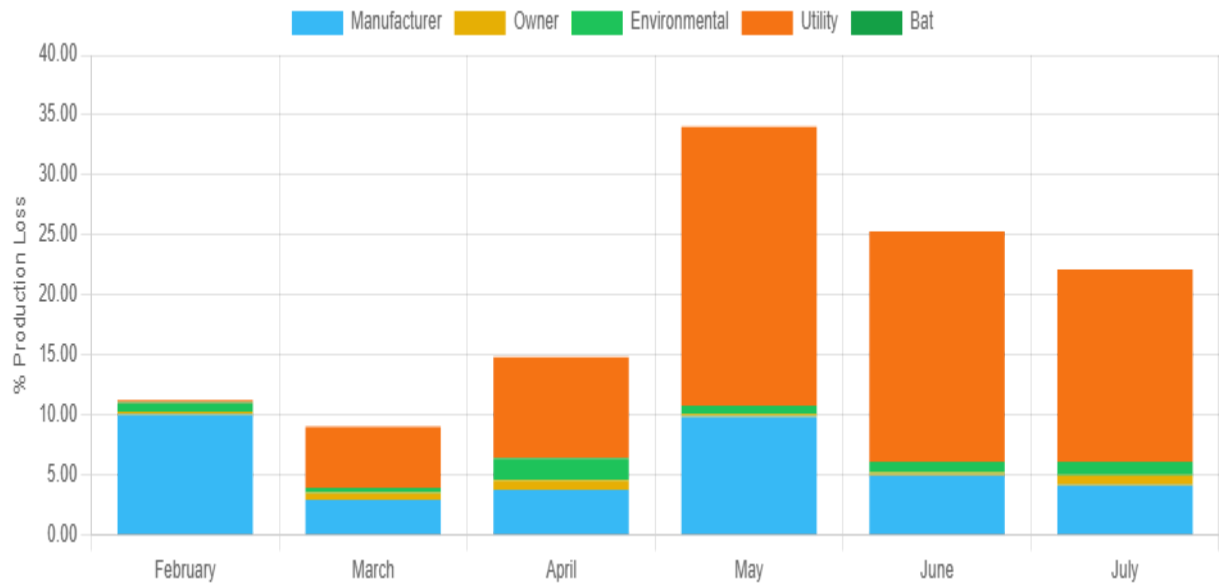

WIND SPEED

