


**Coleskop:** the plant produced 39.6 GWh, significantly below P50 and P90 targets. Contractual availability averaged 97.9%, while technical availability was lower at 92.0%. The negative delta in production was visible in the wind resource deviation of -4%.


FULL KPI MATRIX

| CATEGORY             | 2026    | FEB    | MAR    | APR    | MAY    | JUN    | JUL    | AUG    | TOTAL   |
|----------------------|---------|--------|--------|--------|--------|--------|--------|--------|---------|
| A. Production        |         |        |        |        |        |        |        |        |         |
| Measured (MWh)       | 236,998 | 8,096  | 36,822 | 44,460 | 33,537 | 35,741 | 38,713 | 39,628 | 236,998 |
| Deviation Historical | -       | -      | -      | -      | -      | -      | -      | -      | -       |
| Deviation P50        | -32.0%  | -33.2% | -22.6% | -6.6%  | -40.1% | -40.9% | -37.9% | -36.5% | -32.0%  |
| Deviation P90        | -23.3%  | -24.7% | -12.7% | 5.4%   | -32.4% | -33.3% | -30.0% | -28.3% | -23.3%  |
| Capacity Factor      | 32.0%   | 8.1%   | 34.3%  | 42.4%  | 31.1%  | 34.4%  | 36.2%  | 37.1%  | 32.0%   |
| Electrical Losses    | 0.5%    | -1.8%  | 0.9%   | -0.1%  | 0.5%   | 0.9%   | 1.4%   | 1.5%   | 0.5%    |
| B. Consumption       |         |        |        |        |        |        |        |        |         |
| Measured (MWh)       | 138     | 0      | 28     | 9      | 12     | 29     | 30     | 30     | 138     |
| Ratio to Production  | 0.1%    | 0.0%   | 0.1%   | 0.0%   | 0.0%   | 0.1%   | 0.1%   | 0.1%   | 0.1%    |
| C. Availability      |         |        |        |        |        |        |        |        |         |
| TBA - Contractual    | 98.9%   | 96.7%  | 99.8%  | 99.3%  | 99.7%  | 99.4%  | 99.4%  | 97.9%  | 98.9%   |
| TBA - Technical      | 95.4%   | 95.0%  | 95.5%  | 95.6%  | 97.2%  | 96.5%  | 96.0%  | 92.0%  | 95.4%   |
| PBA - Technical      | 78.5%   | 88.5%  | 91.7%  | 83.3%  | 62.5%  | 71.8%  | 76.0%  | 75.5%  | 78.5%   |
| D. Losses Breakdown  |         |        |        |        |        |        |        |        |         |
| Grid                 | 14.7%   | 0.2%   | 6.6%   | 11.2%  | 27.5%  | 24.2%  | 17.8%  | 15.3%  | 14.7%   |
| Breakdown            | 2.1%    | 9.3%   | 0.3%   | 1.2%   | 0.5%   | 0.3%   | 0.3%   | 2.8%   | 2.1%    |
| Maintenance          | 0.1%    | 0.0%   | 0.0%   | 0.0%   | 0.1%   | 0.5%   | 0.1%   | 0.3%   | 0.1%    |
| Partial Perf.        | 2.5%    | -      | 0.1%   | 0.6%   | 7.5%   | 1.1%   | 2.6%   | 3.4%   | 2.5%    |
| BoP                  | 0.3%    | 0.8%   | 0.3%   | 0.3%   | 0.4%   | 0.1%   | 0.1%   | 0.1%   | 0.3%    |
| Environmental        | 0.9%    | -      | -      | 1.7%   | 0.0%   | -      | -      | -      | 0.9%    |
| Bird                 | 0.7%    | -      | 0.2%   | 0.3%   | 0.1%   | 0.9%   | 1.4%   | 1.1%   | 0.7%    |
| Data Quality         | 0.6%    | 0.7%   | -      | 0.0%   | 1.0%   | 0.2%   | 0.4%   | 1.0%   | 0.6%    |
| Icing                | 0.1%    | -      | -      | 0.0%   | 0.1%   | 0.3%   | 0.0%   | 0.0%   | 0.1%    |
| Requested Shutdown   | 0.7%    | 0.5%   | 0.7%   | 1.2%   | 0.3%   | 0.4%   | 1.4%   | 0.5%   | 0.7%    |
| E. Wind              |         |        |        |        |        |        |        |        |         |
| Forecasted WS (m/s)  | 8.1     | 7.5    | 7.5    | 7.5    | 8.1    | 8.7    | 8.5    | 8.8    | 8.1     |
| Measured WS (m/s)    | 8       | 6.9    | 7.1    | 8.6    | 8.9    | 8      | 7.8    | 8.4    | 8       |
| WindSpeed Deviation  | -1.3%   | -9.0%  | -4.6%  | 14.2%  | 10.1%  | -7.8%  | -7.6%  | -4.1%  | -1.3%   |


LOSSES BREAKDOWN WATERFALL — AUGUST 2026

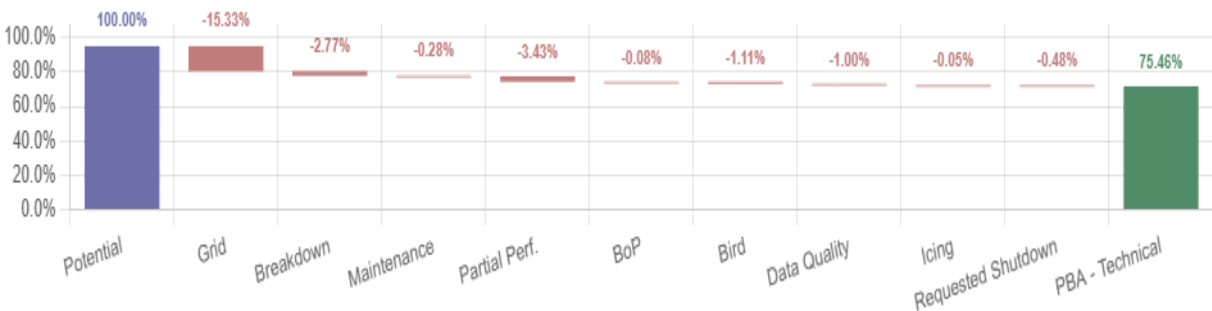


PLANT PRODUCTION

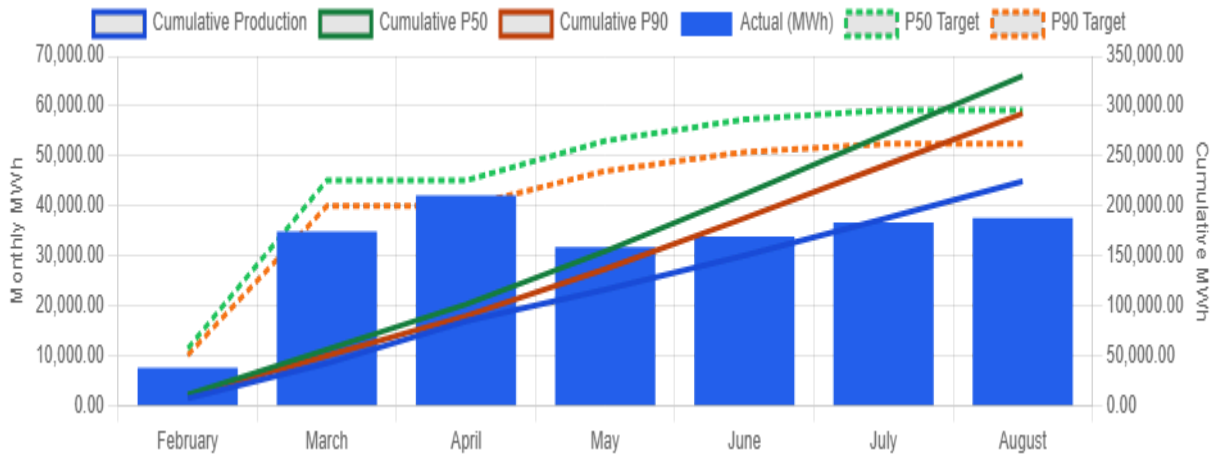


PLANT AVAILABILITY

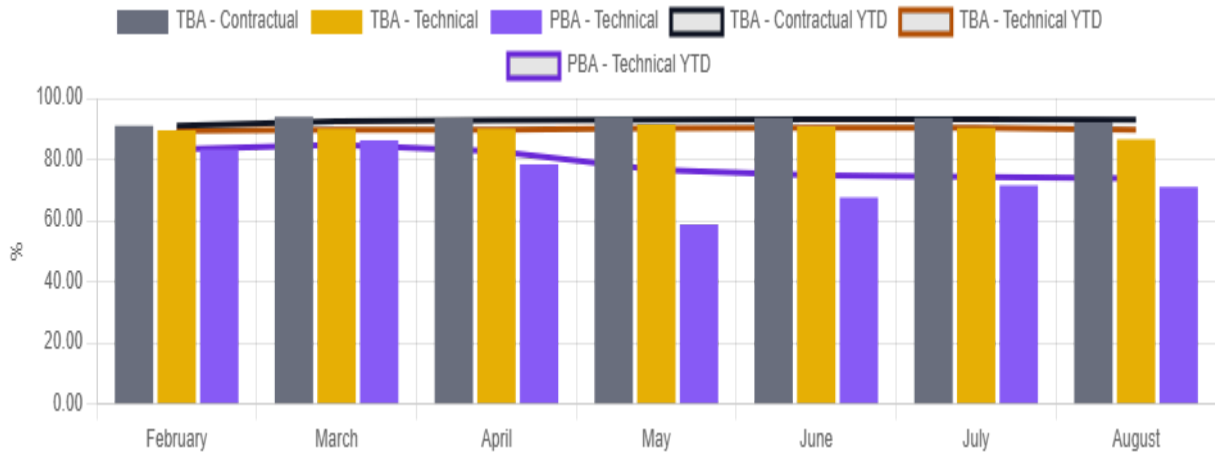

WIND SPEED

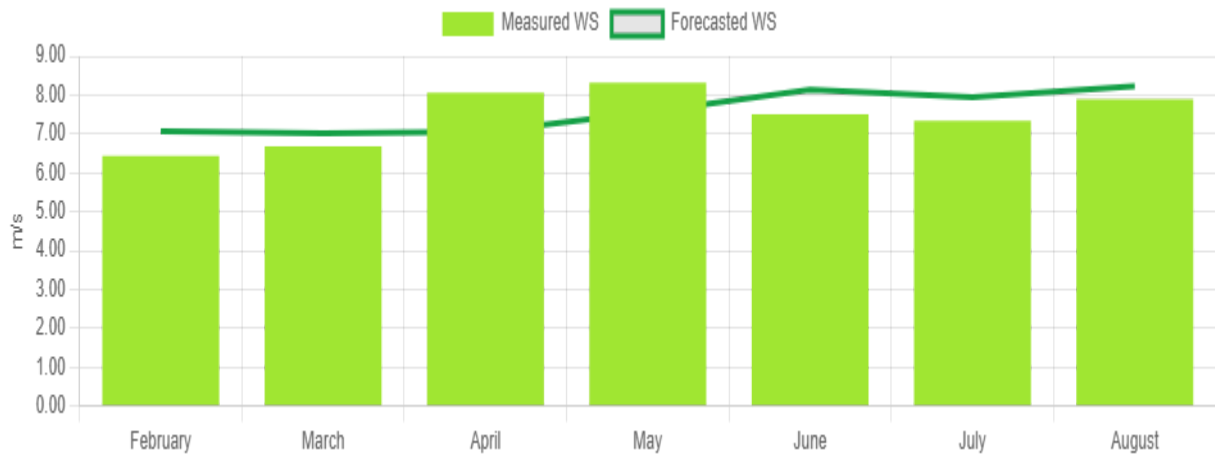

## ANNUAL PRODUCTION AND AVAILABILITY PER WT

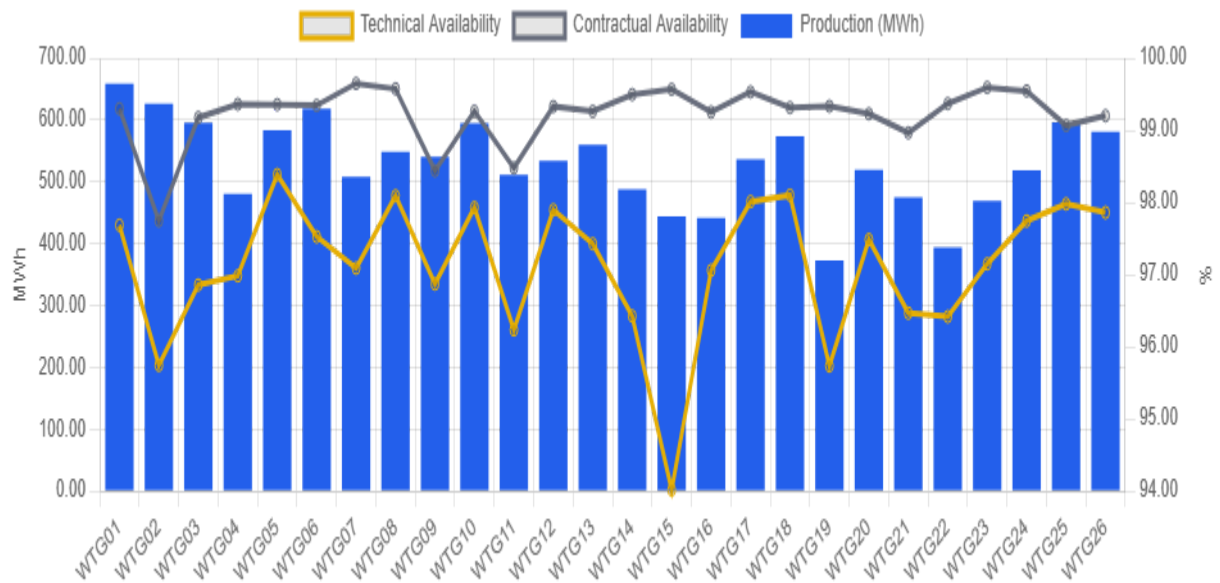

## LOSSES BREAKDOWN

