


**Waainek:** the plant produced 6.4 GWh, significantly below historical, P50 and P90 targets. Contractual availability averaged 87.1%, while technical availability was 85.1%. The negative delta in production was visible in the wind resource deviation of -16%.


FULL KPI MATRIX

| CATEGORY             | 2022   | 2023   | 2024   | 2025   | 2026   | JAN    | FEB    | MAR    | APR   | MAY    | JUN    | JUL    | AUG    | TOTAL   |
|----------------------|--------|--------|--------|--------|--------|--------|--------|--------|-------|--------|--------|--------|--------|---------|
| A. Production        |        |        |        |        |        |        |        |        |       |        |        |        |        |         |
| Measured (MWh)       | 90,260 | 92,833 | 92,112 | 87,117 | 51,466 | 6,386  | 5,427  | 5,675  | 7,217 | 6,864  | 7,770  | 5,726  | 6,403  | 413,788 |
| Deviation Historical | –      | 2.9%   | 0.6%   | -5.0%  | -16.0% | 2.1%   | -5.2%  | -17.1% | 5.3%  | 1.8%   | -20.8% | -44.3% | -26.7% | -3.4%   |
| Deviation P50        | -11.7% | -9.2%  | -9.9%  | -14.8% | -23.2% | -21.0% | -19.6% | -20.7% | -8.4% | -22.9% | -24.8% | -32.5% | -32.0% | -13.1%  |
| Deviation P90        | 1.4%   | 4.3%   | 3.5%   | -2.1%  | -11.7% | -9.2%  | -7.6%  | -8.9%  | 5.3%  | -11.4% | -13.6% | -22.5% | -21.8% | -0.2%   |
| Capacity Factor      | 42.4%  | 43.4%  | 43.1%  | 40.6%  | 36.3%  | 35.3%  | 33.2%  | 31.4%  | 41.2% | 38.0%  | 44.4%  | 31.7%  | 35.4%  | 41.5%   |
| B. Consumption       |        |        |        |        |        |        |        |        |       |        |        |        |        |         |
| Measured (MWh)       | 100    | 83     | 117    | 118    | 113    | 15     | 12     | 19     | 19    | 17     | 8      | 9      | 13     | 531     |
| Ratio to Production  | 0.1%   | 0.1%   | 0.1%   | 0.1%   | 0.2%   | 0.2%   | 0.2%   | 0.3%   | 0.3%  | 0.3%   | 0.1%   | 0.2%   | 0.2%   | 0.1%    |
| C. Availability      |        |        |        |        |        |        |        |        |       |        |        |        |        |         |
| TBA - Contractual    | 93.9%  | 88.5%  | 96.3%  | 96.9%  | 95.3%  | 96.9%  | 90.2%  | 92.8%  | 98.0% | 99.5%  | 99.3%  | 98.6%  | 87.1%  | 94.1%   |
| TBA - Technical      | 93.7%  | 88.7%  | 92.9%  | 92.3%  | 89.9%  | 93.0%  | 86.8%  | 86.6%  | 92.1% | 92.6%  | 97.1%  | 85.9%  | 85.1%  | 91.6%   |
| PBA - Technical      | 97.1%  | 95.5%  | 95.0%  | 93.2%  | 89.4%  | 93.6%  | 88.1%  | 89.2%  | 88.0% | 90.3%  | 96.7%  | 83.6%  | 85.8%  | 94.4%   |
| D. Losses Breakdown  |        |        |        |        |        |        |        |        |       |        |        |        |        |         |
| Grid                 | 0.2%   | 0.1%   | 0.9%   | 1.8%   | 5.1%   | 2.5%   | 0.1%   | 1.4%   | 10.0% | 8.0%   | 2.9%   | 14.9%  | 1.4%   | 2.1%    |
| Breakdown            | 2.3%   | 3.9%   | 1.6%   | 1.1%   | 4.2%   | 1.0%   | 10.1%  | 6.7%   | 1.3%  | 1.2%   | 0.1%   | 1.3%   | 11.9%  | 2.5%    |
| Maintenance          | 0.4%   | 0.4%   | 0.9%   | 0.6%   | 0.2%   | 0.6%   | 0.3%   | 0.5%   | 0.4%  | 0.0%   | 0.0%   | 0.0%   | 0.1%   | 0.5%    |
| Partial Perf.        | 0.2%   | 0.1%   | 0.1%   | 0.2%   | 0.3%   | 0.5%   | 0.2%   | 0.1%   | 0.0%  | –      | 0.3%   | 0.0%   | 0.7%   | 0.2%    |
| Environmental        | 0.0%   | 0.0%   | 0.2%   | 0.1%   | 1.3%   | 1.6%   | 1.1%   | 1.7%   | –     | 0.7%   | –      | –      | –      | 0.3%    |
| Data Quality         | 0.1%   | –      | –      | –      | 0.0%   | –      | –      | –      | –     | –      | –      | –      | 0.0%   | 0.1%    |
| Requested Shutdown   | 0.1%   | 0.0%   | 0.1%   | 0.0%   | 0.1%   | 0.0%   | –      | 0.2%   | –     | 0.0%   | –      | –      | –      | 0.0%    |
| Electrical Losses    | 1.1%   | 0.9%   | 1.1%   | 0.5%   | 1.0%   | 1.0%   | 1.0%   | 1.0%   | 1.0%  | 1.1%   | 1.1%   | 1.1%   | 1.0%   | 0.9%    |
| BoP                  | 0.0%   | 0.0%   | 0.0%   | 0.1%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%  | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%    |
| Bat                  | –      | –      | 0.3%   | 1.1%   | 0.2%   | 0.1%   | 0.2%   | 0.2%   | 0.3%  | 0.3%   | –      | –      | –      | 0.6%    |
| MCR                  | –      | –      | 11.5%  | 10.5%  | –      | –      | –      | –      | –     | –      | –      | –      | –      | 10.9%   |
| Other                | –      | –      | –      | –      | 0.1%   | –      | –      | 0.1%   | –     | –      | –      | –      | –      | 0.1%    |
| E. Wind              |        |        |        |        |        |        |        |        |       |        |        |        |        |         |
| Forecasted WS (m/s)  | 8.2    | 8.2    | 8.2    | 8.2    | 8.2    | 7.9    | 7.8    | 7.6    | 7.4   | 8.4    | 9.3    | 8.7    | 8.8    | 8.2     |
| Measured WS (m/s)    | 7.6    | 8      | 7.8    | 7.7    | 7.3    | 6.9    | 7      | 6.7    | 7.9   | 7.9    | 7.8    | 7.1    | 7.4    | 7.7     |
| WindSpeed Deviation  | -7.2%  | -3.1%  | -4.7%  | -6.8%  | -10.6% | -12.8% | -10.1% | -11.7% | 6.3%  | -5.6%  | -16.5% | -18.5% | -15.9% | -6.2%   |


PLANT PRODUCTION

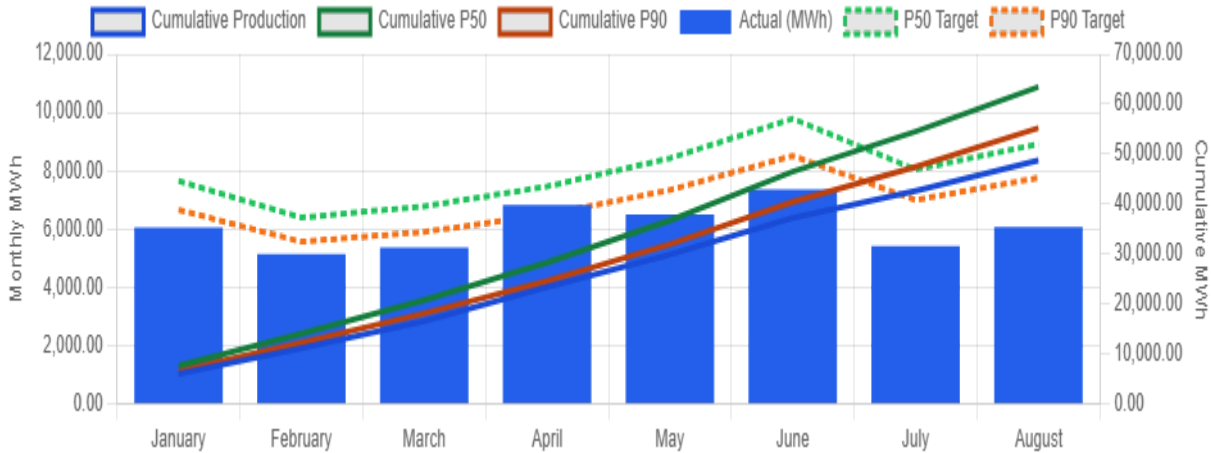

PLANT AVAILABILITY

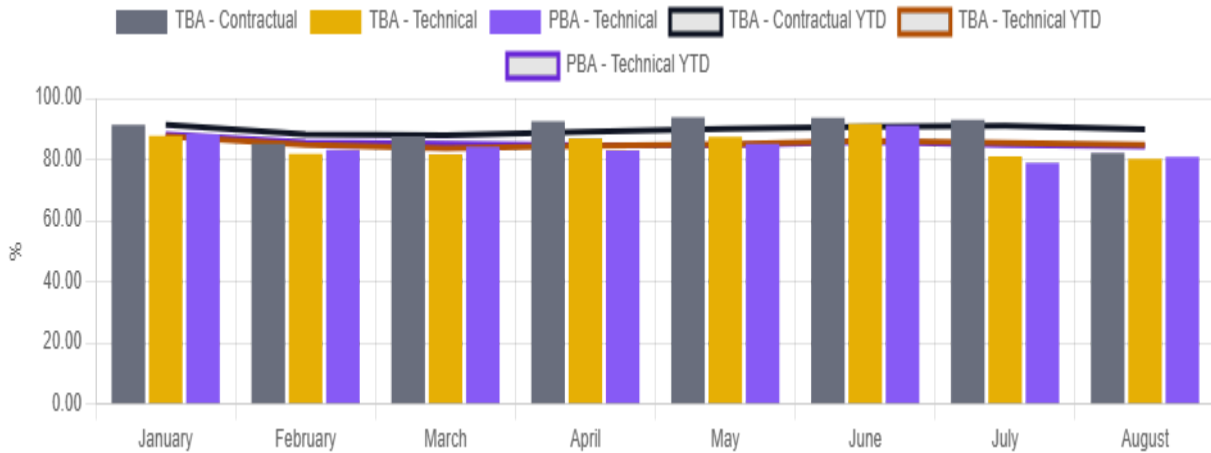

WIND SPEED

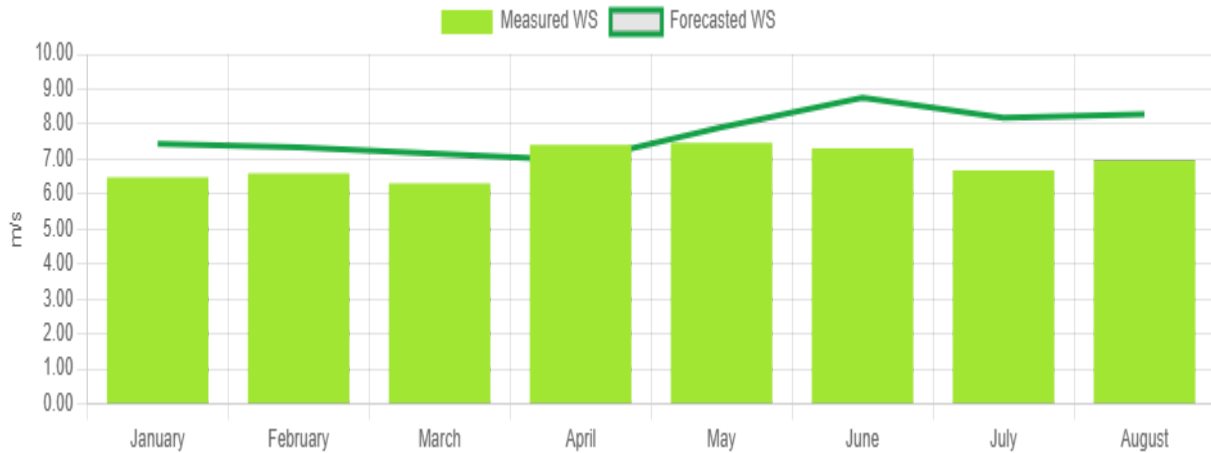

## ANNUAL PRODUCTION AND AVAILABILITY PER WT



## LOSSES BREAKDOWN

