


Coleskop: the plant produced 39.6 GWh, significantly below P50 and P90 targets. Contractual availability averaged 97.9%, while technical availability was lower at 92.0%. The negative delta in production was visible in the wind resource deviation of -4%.


FULL KPI MATRIX

CATEGORY	2026	FEB	MAR	APR	MAY	JUN	JUL	AUG	TOTAL
A. Production									
Measured (MWh)	236,998	8,096	36,822	44,460	33,537	35,741	38,713	39,628	236,998
Deviation Historical	-	-	-	-	-	-	-	-	-
Deviation P50	-32.0%	-33.2%	-22.6%	-6.6%	-40.1%	-40.9%	-37.9%	-36.5%	-32.0%
Deviation P90	-23.3%	-24.7%	-12.7%	5.4%	-32.4%	-33.3%	-30.0%	-28.3%	-23.3%
Capacity Factor	32.0%	8.1%	34.3%	42.4%	31.1%	34.4%	36.2%	37.1%	32.0%
Electrical Losses	0.5%	-1.8%	0.9%	-0.1%	0.5%	0.9%	1.4%	1.5%	0.5%
B. Consumption									
Measured (MWh)	138	0	28	9	12	29	30	30	138
Ratio to Production	0.1%	0.0%	0.1%	0.0%	0.0%	0.1%	0.1%	0.1%	0.1%
C. Availability									
TBA - Contractual	98.9%	96.7%	99.8%	99.3%	99.7%	99.4%	99.4%	97.9%	98.9%
TBA - Technical	95.4%	95.0%	95.5%	95.6%	97.2%	96.5%	96.0%	92.0%	95.4%
PBA - Technical	96.6%	88.2%	98.8%	98.4%	97.6%	98.9%	98.6%	95.9%	96.6%
D. OLF - Losses									
Manufacturer	6.5%	10.8%	3.2%	4.1%	10.7%	5.4%	4.5%	7.1%	6.5%
Owner	0.5%	0.3%	0.7%	0.8%	0.2%	0.2%	0.9%	0.5%	0.5%
Environmental	1.1%	0.8%	0.4%	2.0%	0.8%	1.0%	1.2%	1.2%	1.1%
Utility	13.4%	0.2%	5.5%	9.1%	25.1%	20.7%	17.3%	15.5%	13.4%
Bat Curtailment	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%
E. Wind									
Forecasted WS (m/s)	8.1	7.5	7.5	7.5	8.1	8.7	8.5	8.8	8.1
Measured WS (m/s)	8	6.9	7.1	8.6	8.9	8	7.8	8.4	8
WindSpeed Deviation	-1.3%	-9.0%	-4.6%	14.2%	10.1%	-7.8%	-7.6%	-4.1%	-1.3%


PLANT PRODUCTION

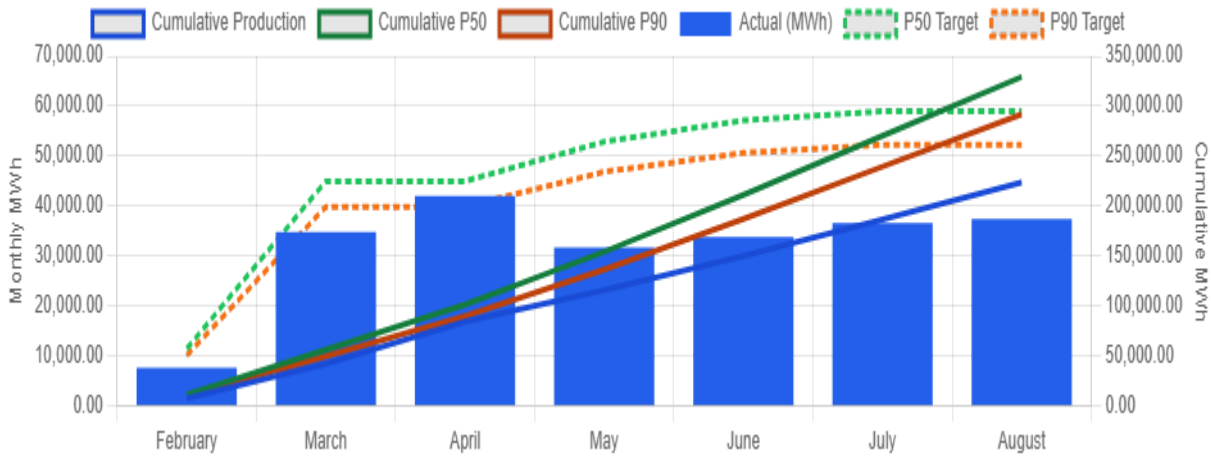


PLANT AVAILABILITY

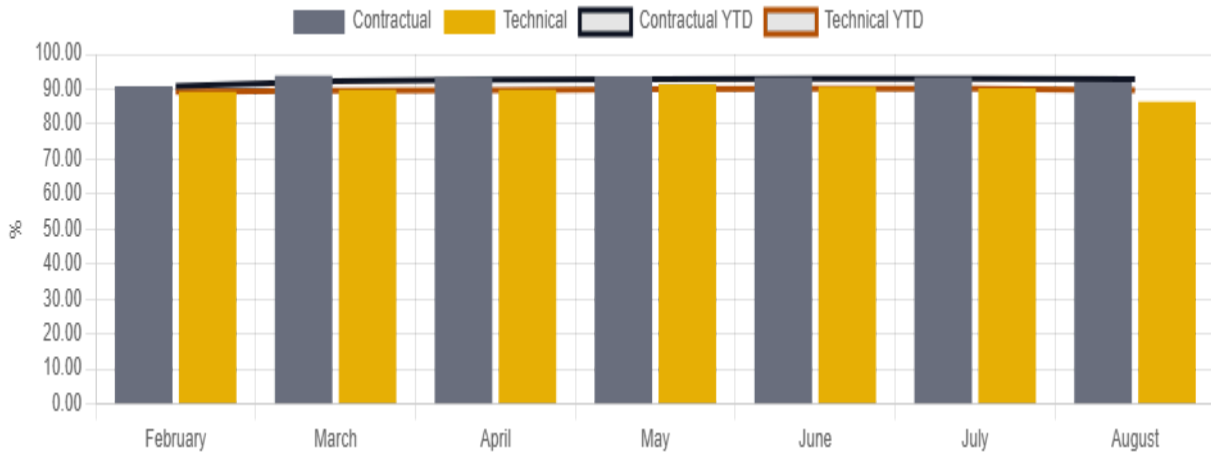

WIND SPEED

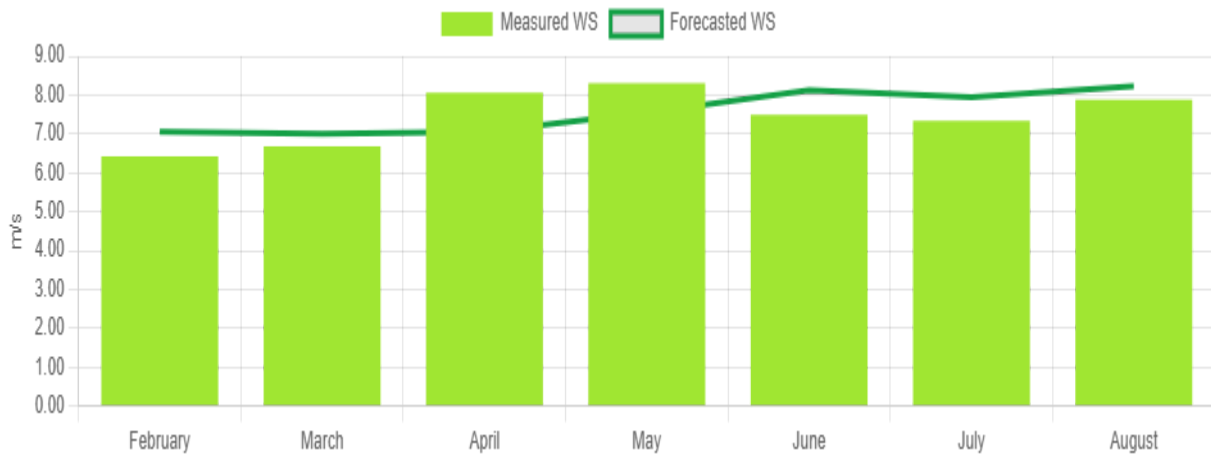

ANNUAL PRODUCTION AND AVAILABILITY PER WT

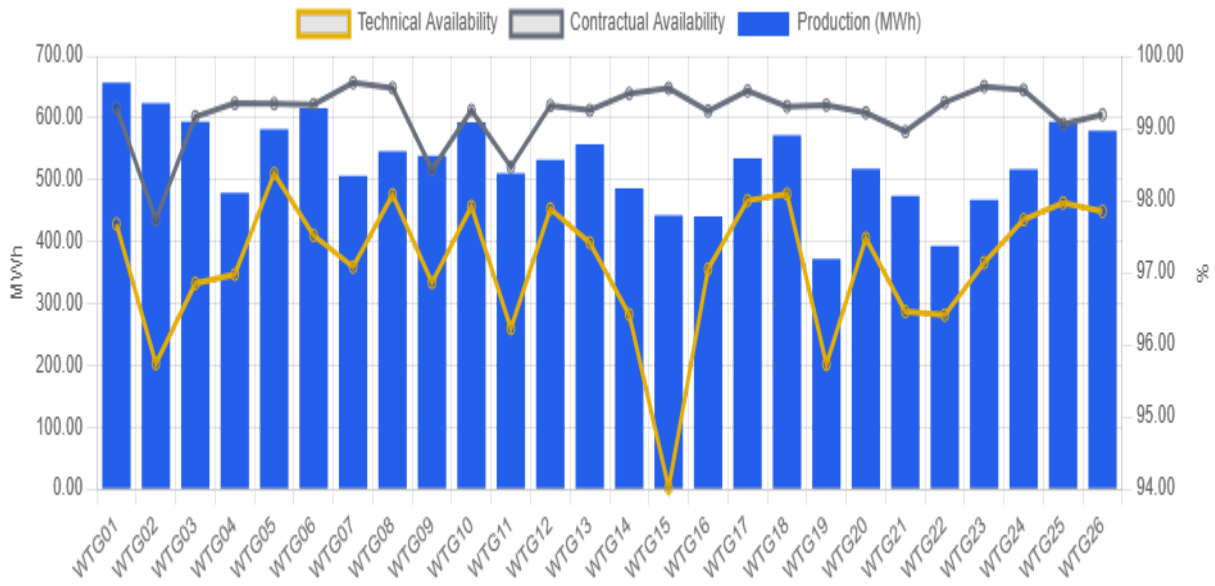

OPERATIONAL LOSS FACTORS

