


Dassiesridge: the plant produced 13.9 GWh, significantly below P50 and P90 targets. Contractual availability averaged 98.5%, while technical availability was 96.0%. The negative delta in production was visible in the wind resource deviation of -17%.


FULL KPI MATRIX

CATEGORY	2025	2026	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	TOTAL
A. Production											
Measured (MWh)	14,944	101,155	14,780	11,841	10,471	15,782	12,522	11,098	10,735	13,926	116,099
Deviation Historical	-	-	-	-	-	-	-	-	-	-	-
Deviation P50	-	-26.9%	-14.9%	-20.1%	-36.5%	8.2%	-26.3%	-44.7%	-44.5%	-25.7%	-26.9%
Deviation P90	-	-16.1%	-2.2%	-8.2%	-27.1%	24.2%	-15.4%	-36.5%	-36.3%	-14.6%	-16.1%
Capacity Factor	29.5%	28.1%	32.1%	28.5%	22.9%	35.5%	27.3%	25.1%	23.5%	30.3%	28.3%
Electrical Losses	-7.3%	2.2%	1.8%	2.1%	2.3%	2.1%	2.2%	2.4%	2.5%	2.1%	1.1%
B. Consumption											
Measured (MWh)	70	482	68	39	43	42	85	94	72	39	552
Ratio to Production	0.5%	0.5%	0.5%	0.3%	0.4%	0.3%	0.7%	0.8%	0.7%	0.3%	0.5%
C. Availability											
TBA - Contractual	98.4%	93.9%	98.3%	98.5%	98.1%	98.6%	92.9%	66.7%	99.2%	98.5%	94.4%
TBA - Technical	95.1%	89.8%	93.7%	95.2%	94.7%	97.5%	80.7%	68.1%	92.4%	96.0%	90.4%
PBA - Technical	97.9%	93.7%	98.1%	98.2%	98.4%	98.5%	92.7%	66.2%	99.0%	98.6%	94.2%
D. OLF - Losses											
Manufacturer	2.6%	7.9%	4.6%	7.7%	3.2%	2.1%	6.4%	36.4%	1.0%	1.4%	7.3%
Owner	0.0%	0.2%	0.0%	0.0%	0.0%	0.0%	1.4%	0.0%	0.2%	0.0%	0.2%
Environmental	0.1%	0.1%	0.0%	0.1%	0.1%	0.1%	0.1%	0.0%	0.1%	0.3%	0.1%
Utility	2.0%	2.4%	4.2%	2.1%	0.9%	0.3%	4.4%	0.2%	3.3%	3.8%	2.4%
Bat Curtailment	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%
E. Wind											
Forecasted WS (m/s)	7.1	7.2	6.9	6.6	6.5	6.5	7.3	8.5	7.8	7.5	7.2
Measured WS (m/s)	6.6	6.4	6.6	6.3	5.6	6.7	6.9	7.2	5.6	6.2	6.4
WindSpeed Deviation	-5.9%	-10.6%	-3.7%	-4.8%	-14.1%	3.6%	-5.1%	-14.8%	-28.4%	-17.2%	-10.0%


PLANT PRODUCTION

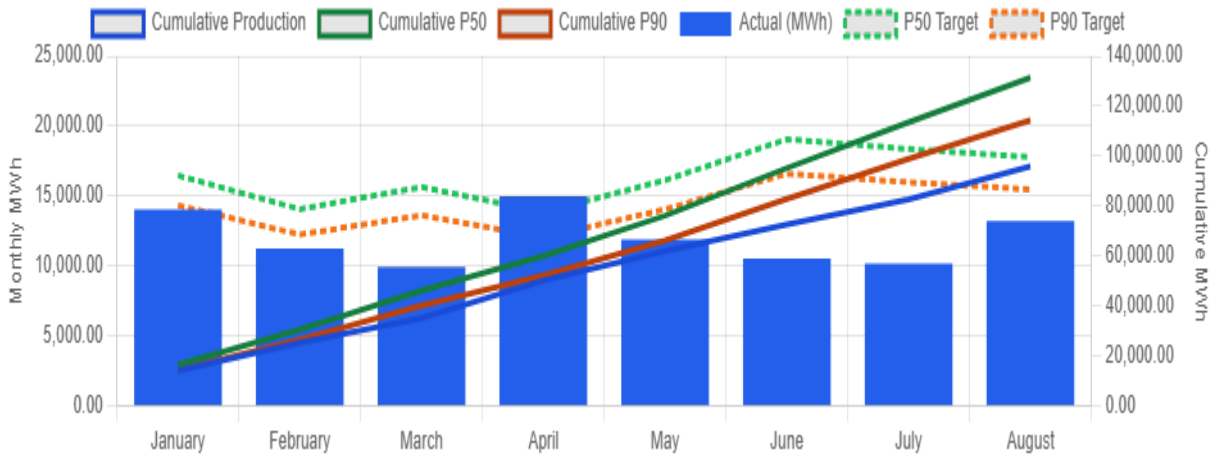


PLANT AVAILABILITY

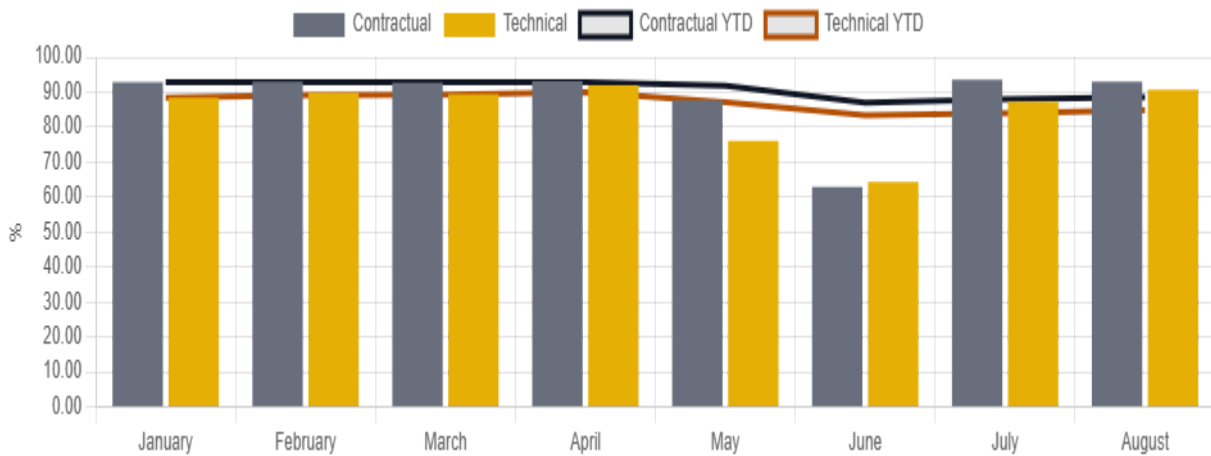

WIND SPEED

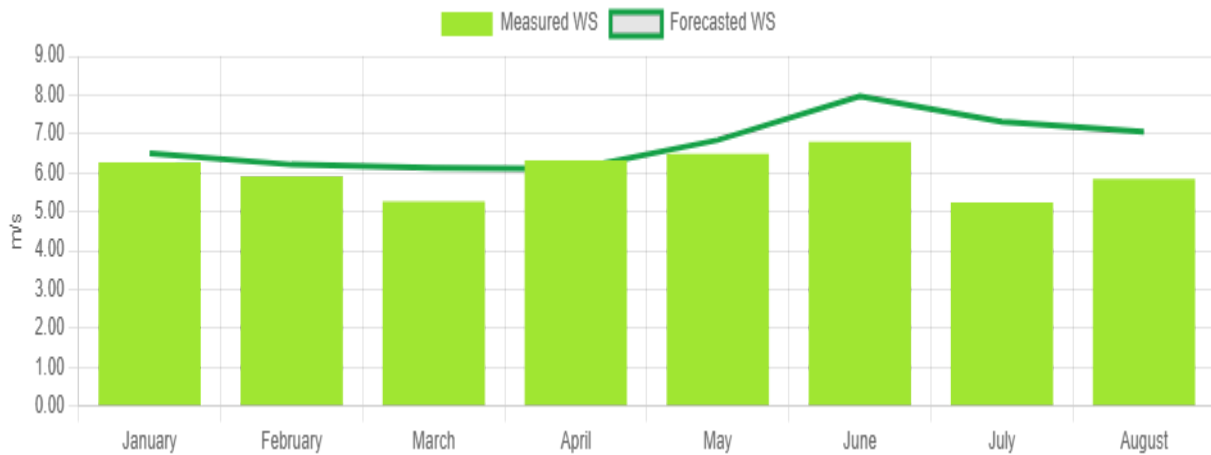

ANNUAL PRODUCTION AND AVAILABILITY PER WT

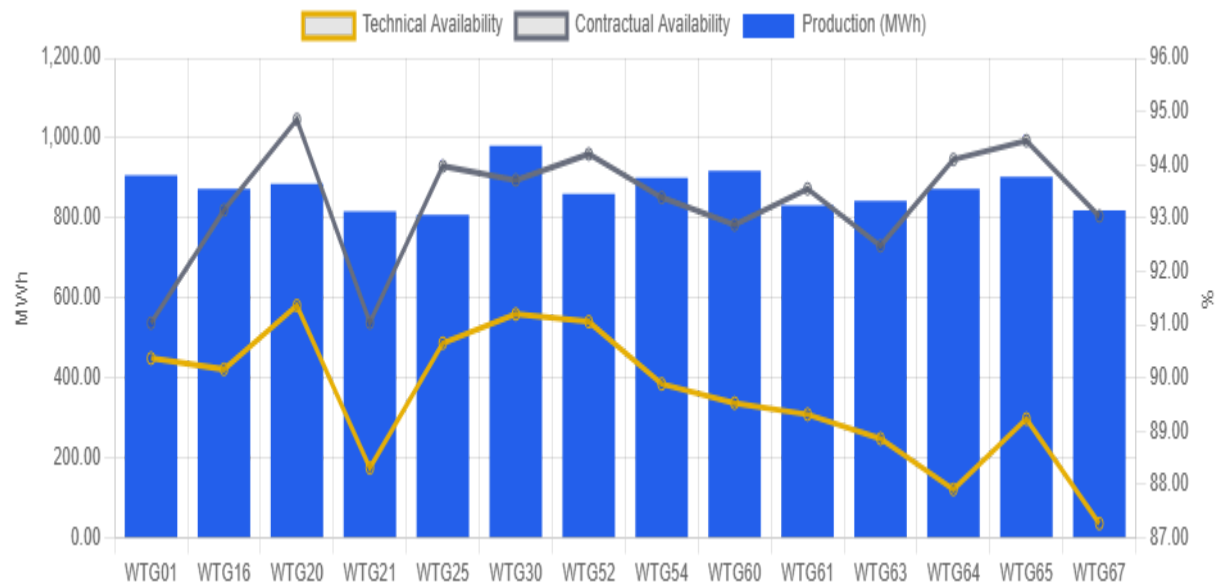

OPERATIONAL LOSS FACTORS

