


**Phezukomoya:** the plant produced 27.6 GWh, significantly below P50 and P90 targets. Contractual availability averaged 85.9%, while technical availability was lower at 80.1%. The negative delta in production was visible in the wind resource deviation of -21%.


FULL KPI MATRIX

| CATEGORY             | 2026    | FEB    | MAR    | APR    | MAY    | JUN    | JUL    | AUG    | TOTAL   |
|----------------------|---------|--------|--------|--------|--------|--------|--------|--------|---------|
| A. Production        |         |        |        |        |        |        |        |        |         |
| Measured (MWh)       | 230,848 | 31,758 | 34,015 | 41,027 | 29,164 | 32,348 | 34,975 | 27,560 | 230,848 |
| Deviation Historical | -       | -      | -      | -      | -      | -      | -      | -      | -       |
| Deviation P50        | -37.3%  | -18.7% | -29.5% | -13.8% | -46.7% | -44.7% | -40.9% | -54.9% | -37.3%  |
| Deviation P90        | -30.6%  | -9.9%  | -21.9% | -4.5%  | -40.9% | -38.8% | -34.5% | -50.0% | -30.6%  |
| Capacity Factor      | 31.6%   | 32.8%  | 31.9%  | 39.7%  | 27.3%  | 31.3%  | 32.8%  | 25.8%  | 31.6%   |
| Electrical Losses    | 1.4%    | 1.2%   | 1.5%   | 1.5%   | 1.3%   | 1.4%   | 1.4%   | 1.5%   | 1.4%    |
| B. Consumption       |         |        |        |        |        |        |        |        |         |
| Measured (MWh)       | 177     | 38     | 15     | 15     | 14     | 31     | 25     | 39     | 177     |
| Ratio to Production  | 0.1%    | 0.1%   | 0.0%   | 0.0%   | 0.0%   | 0.1%   | 0.1%   | 0.1%   | 0.1%    |
| C. Availability      |         |        |        |        |        |        |        |        |         |
| TBA - Contractual    | 97.5%   | -      | 100.0% | 100.0% | 99.8%  | 99.9%  | 99.5%  | 85.9%  | 97.5%   |
| TBA - Technical      | 94.8%   | 97.3%  | 99.1%  | 98.7%  | 97.1%  | 97.3%  | 94.2%  | 80.1%  | 94.8%   |
| PBA - Technical      | 96.2%   | 94.5%  | 98.8%  | 97.9%  | 96.5%  | 99.0%  | 99.4%  | 87.3%  | 96.2%   |
| D. OLF - Losses      |         |        |        |        |        |        |        |        |         |
| Manufacturer         | 13.1%   | 5.9%   | 5.2%   | 14.0%  | 33.5%  | 15.0%  | 5.3%   | 12.6%  | 13.1%   |
| Owner                | 0.0%    | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.2%   | 0.0%   | 0.0%    |
| Environmental        | 1.4%    | 0.0%   | 0.0%   | 1.1%   | 3.7%   | 1.2%   | 1.9%   | 2.0%   | 1.4%    |
| Utility              | 7.1%    | 0.0%   | 0.0%   | 0.1%   | 0.3%   | 9.6%   | 17.0%  | 22.9%  | 7.1%    |
| Bat Curtailment      | 0.0%    | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%    |
| E. Wind              |         |        |        |        |        |        |        |        |         |
| Forecasted WS (m/s)  | 8.6     | 8      | 8      | 8      | 8.7    | 9.3    | 9.1    | 9.4    | 8.6     |
| Measured WS (m/s)    | 7.5     | 7.3    | 6.8    | 8      | 8.1    | 7.4    | 7.4    | 7.4    | 7.5     |
| WindSpeed Deviation  | -12.8%  | -8.3%  | -15.1% | 0.4%   | -6.2%  | -20.6% | -18.4% | -21.3% | -12.8%  |


PLANT PRODUCTION

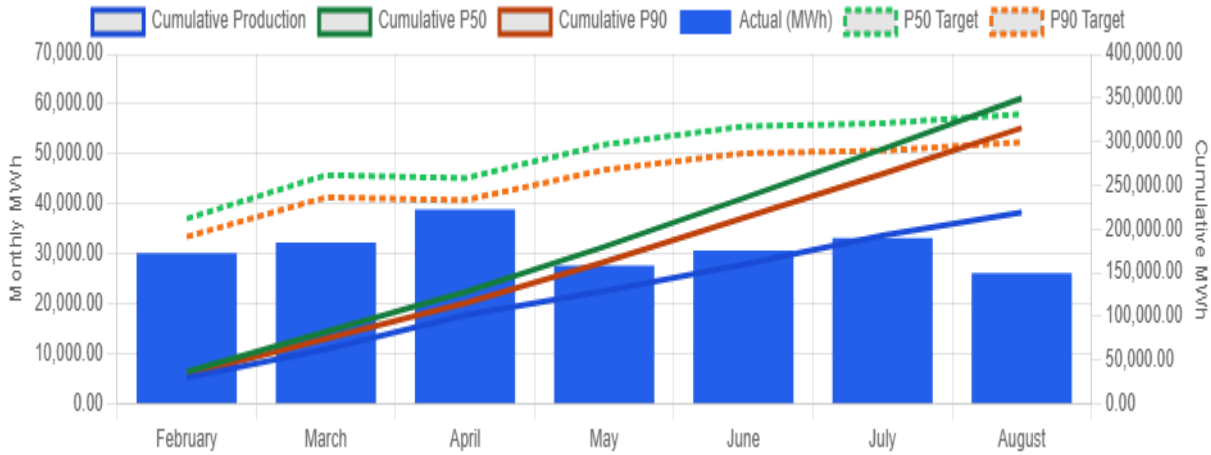


PLANT AVAILABILITY

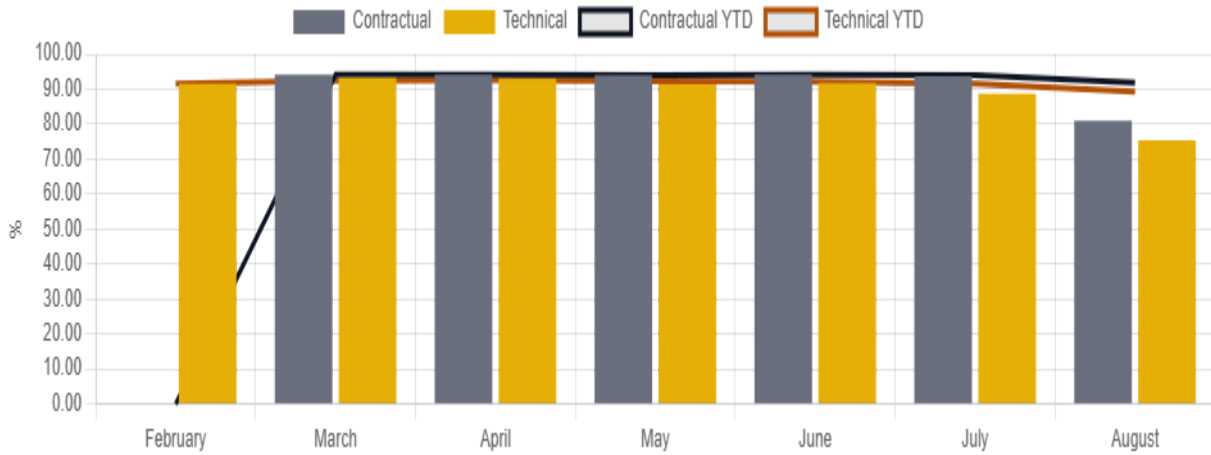

WIND SPEED

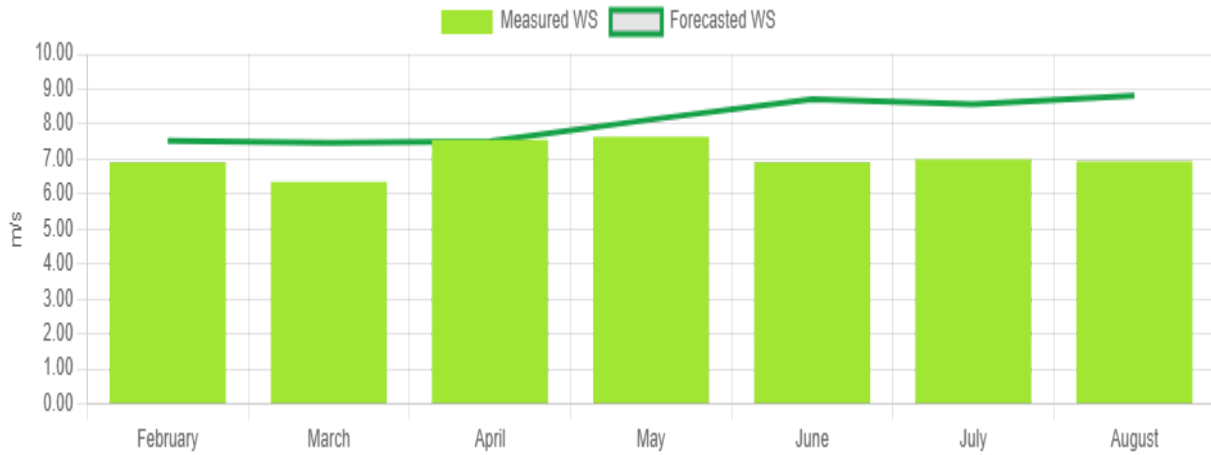

## ANNUAL PRODUCTION AND AVAILABILITY PER WT

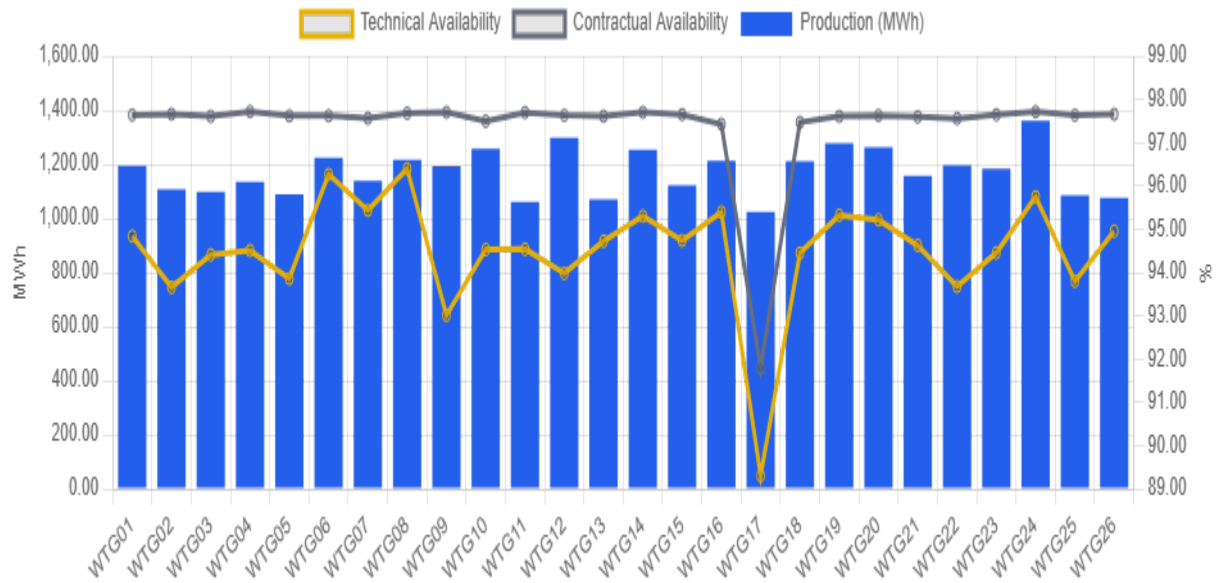

## OPERATIONAL LOSS FACTORS

