


**Wesley:** the plant produced 9.1 GWh, significantly below historical, P50 and P90 targets. Contractual availability averaged 98.0%, while technical availability was 97.7%. The negative delta in production was visible in the wind resource deviation of -24%.


FULL KPI MATRIX

| CATEGORY             | 2022    | 2023    | 2024    | 2025    | 2026   | JAN    | FEB    | MAR    | APR    | MAY    | JUN    | JUL    | AUG    | TOTAL   |
|----------------------|---------|---------|---------|---------|--------|--------|--------|--------|--------|--------|--------|--------|--------|---------|
| A. Production        |         |         |         |         |        |        |        |        |        |        |        |        |        |         |
| Measured (MWh)       | 129,047 | 132,295 | 132,220 | 127,062 | 74,037 | 10,049 | 10,554 | 10,719 | 9,132  | 8,946  | 7,787  | 7,787  | 9,064  | 594,662 |
| Deviation Historical | -       | 2.5%    | 1.2%    | -3.1%   | -13.2% | -7.8%  | 6.7%   | -3.7%  | -10.9% | 2.7%   | -32.9% | -33.4% | -18.1% | -2.2%   |
| Deviation P50        | -8.6%   | -6.3%   | -6.3%   | -10.0%  | -18.9% | -12.2% | 2.3%   | -6.3%  | -15.0% | -19.9% | -32.8% | -32.8% | -30.3% | -9.3%   |
| Deviation P90        | 2.7%    | 5.3%    | 5.2%    | 1.1%    | -8.9%  | -1.4%  | 14.9%  | 5.2%   | -4.5%  | -10.0% | -24.5% | -24.5% | -21.7% | 1.8%    |
| Capacity Factor      | 1.8%    | 36.8%   | 44.4%   | 42.5%   | 36.7%  | 39.7%  | 45.6%  | 42.4%  | 37.4%  | 33.2%  | 31.5%  | 28.0%  | 35.9%  | 32.1%   |
| Electrical Losses    | -95.8%  | -15.5%  | 1.6%    | 0.9%    | -0.7%  | 1.4%   | 0.1%   | 1.6%   | 1.7%   | -4.6%  | 0.5%   | -7.8%  | 1.7%   | -23.4%  |
| B. Consumption       |         |         |         |         |        |        |        |        |        |        |        |        |        |         |
| Measured (MWh)       | 172     | 174     | 186     | 166     | 163    | 17     | 16     | 19     | 16     | 20     | 23     | 25     | 27     | 860     |
| Ratio to Production  | 0.1%    | 0.1%    | 0.1%    | 0.1%    | 0.2%   | 0.2%   | 0.1%   | 0.2%   | 0.2%   | 0.2%   | 0.3%   | 0.3%   | 0.3%   | 0.2%    |
| C. Availability      |         |         |         |         |        |        |        |        |        |        |        |        |        |         |
| TBA - Contractual    | -       | 97.3%   | 96.5%   | 97.9%   | 98.3%  | 99.1%  | 97.4%  | 99.3%  | 98.7%  | 98.1%  | 97.9%  | 97.6%  | 98.0%  | 97.4%   |
| TBA - Technical      | -       | 96.6%   | 95.5%   | 97.3%   | 97.5%  | 99.0%  | 97.3%  | 99.0%  | 94.5%  | 97.9%  | 97.1%  | 97.5%  | 97.7%  | 96.7%   |
| PBA - Technical      | 4.3%    | 96.0%   | 96.6%   | 98.2%   | 98.3%  | 99.0%  | 97.1%  | 99.7%  | 97.7%  | 98.3%  | 98.7%  | 97.4%  | 98.9%  | 77.3%   |
| D. OLF - Losses      |         |         |         |         |        |        |        |        |        |        |        |        |        |         |
| Manufacturer         | 0.0%    | 4.2%    | 4.2%    | 2.1%    | 1.7%   | 1.0%   | 2.9%   | 0.4%   | 2.3%   | 1.7%   | 1.4%   | 2.9%   | 1.3%   | 2.5%    |
| Owner                | 0.0%    | 0.0%    | 0.0%    | 0.0%    | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%    |
| Environmental        | 0.0%    | 0.0%    | 0.0%    | 0.0%    | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%    |
| Utility              | 0.0%    | 0.4%    | 1.0%    | 3.4%    | 7.1%   | 0.8%   | 0.7%   | 7.2%   | 15.0%  | 9.7%   | 10.8%  | 5.5%   | 7.2%   | 2.1%    |
| Bat Curtailment      | 0.0%    | 0.0%    | 0.0%    | 0.0%    | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%    |
| E. Wind              |         |         |         |         |        |        |        |        |        |        |        |        |        |         |
| Forecasted WS (m/s)  | 8.3     | 8.3     | 8.3     | 8.3     | 8.1    | 8.1    | 7.3    | 8.1    | 7.6    | 7.9    | 8.2    | 8.2    | 9.2    | 8.3     |
| Measured WS (m/s)    | 7.8     | 7.9     | 8       | 7.8     | 7.3    | 7.3    | 7.9    | 7.9    | 7.7    | 7.4    | 6.8    | 6.4    | 7      | 7.8     |
| WindSpeed Deviation  | -6.3%   | -5.3%   | -3.7%   | -6.0%   | -8.9%  | -9.4%  | 8.8%   | -2.0%  | 0.9%   | -6.4%  | -17.0% | -22.5% | -23.6% | -5.8%   |


PLANT PRODUCTION

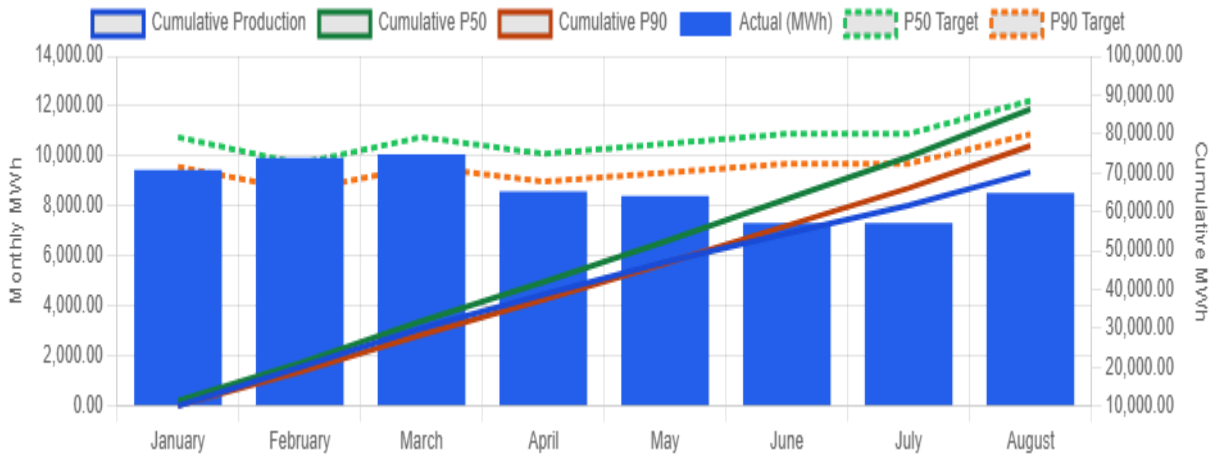


PLANT AVAILABILITY

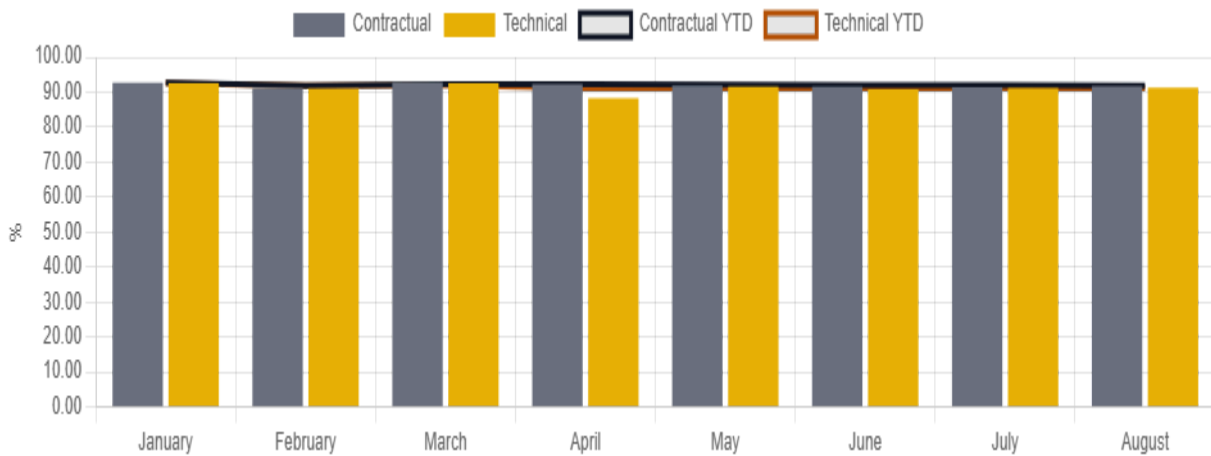

WIND SPEED

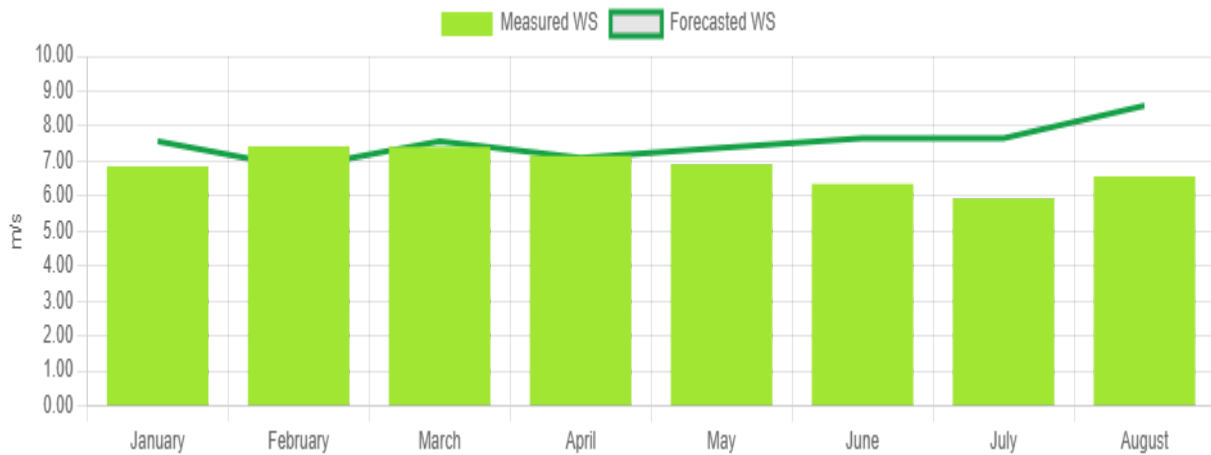

## ANNUAL PRODUCTION AND AVAILABILITY PER WT

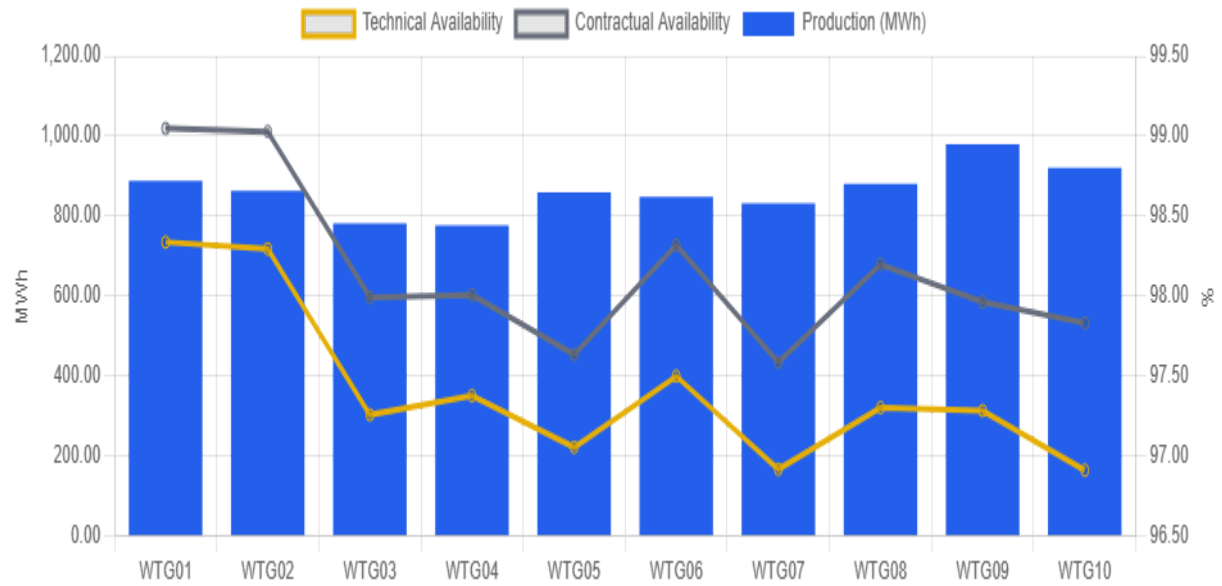

## OPERATIONAL LOSS FACTORS

