


Coleskop: the plant produced 38.7 GWh, significantly below P50 and P90 targets. Contractual availability averaged 99.4%, while technical availability was lower at 96.0%. The negative delta in production was visible in the wind resource deviation of -8%.


FULL KPI MATRIX

CATEGORY	2026	FEB	MAR	APR	MAY	JUN	JUL	TOTAL
A. Production								
Measured (MWh)	197,370	8,096	36,822	44,460	33,537	35,741	38,713	197,370
Deviation Historical	–	–	–	–	–	–	–	–
Deviation P50	-31.0%	-33.2%	-22.6%	-6.6%	-40.1%	-40.9%	-37.9%	-31.0%
Deviation P90	-22.2%	-24.7%	-12.7%	5.4%	-32.4%	-33.3%	-30.0%	-22.2%
Capacity Factor	31.1%	8.1%	34.3%	42.4%	31.1%	34.4%	36.2%	31.1%
B. Consumption								
Measured (MWh)	78	0	28	9	12	29	0	78
Ratio to Production	0.0%	0.0%	0.1%	0.0%	0.0%	0.1%	0.0%	0.0%
C. Availability								
TBA - Contractual	99.0%	96.7%	99.8%	99.3%	99.7%	99.4%	99.4%	99.0%
TBA - Technical	96.0%	95.0%	95.5%	95.6%	97.2%	96.5%	96.0%	96.0%
PBA - Technical	78.8%	86.8%	90.7%	83.7%	62.8%	72.6%	76.3%	78.8%
D. Losses Breakdown								
Grid	13.2%	0.2%	5.5%	9.3%	25.4%	21.3%	17.1%	13.2%
Breakdown	1.6%	7.8%	0.2%	0.6%	0.4%	0.3%	0.3%	1.6%
Maintenance	0.1%	–	–	0.0%	0.0%	0.3%	0.1%	0.1%
Partial Perf.	3.3%	0.0%	2.0%	2.4%	8.7%	3.8%	3.1%	3.3%
BoP	0.3%	0.9%	0.3%	0.2%	0.1%	0.2%	0.1%	0.3%
Environmental	0.5%	0.2%	0.2%	1.9%	0.2%	0.2%	0.1%	0.5%
Bird	0.4%	–	0.1%	0.1%	0.1%	0.5%	1.2%	0.4%
Data Quality	1.5%	4.0%	1.0%	1.0%	1.8%	0.6%	0.7%	1.5%
Icing	0.3%	–	–	0.2%	0.6%	0.3%	0.0%	0.3%
Requested Shutdown	0.6%	0.3%	0.7%	0.9%	0.4%	0.2%	1.4%	0.6%
Electrical Losses	0.0%	-1.6%	0.8%	-0.1%	0.1%	0.0%	1.0%	0.0%
E. Wind								
Forecasted WS (m/s)	8	7.5	7.5	7.5	8.1	8.7	8.5	8
Measured WS (m/s)	7.9	6.9	7.1	8.6	8.9	8	7.8	7.9
WindSpeed Deviation	-0.8%	-9.0%	-4.6%	14.2%	10.1%	-7.8%	-7.6%	-0.8%


PLANT PRODUCTION

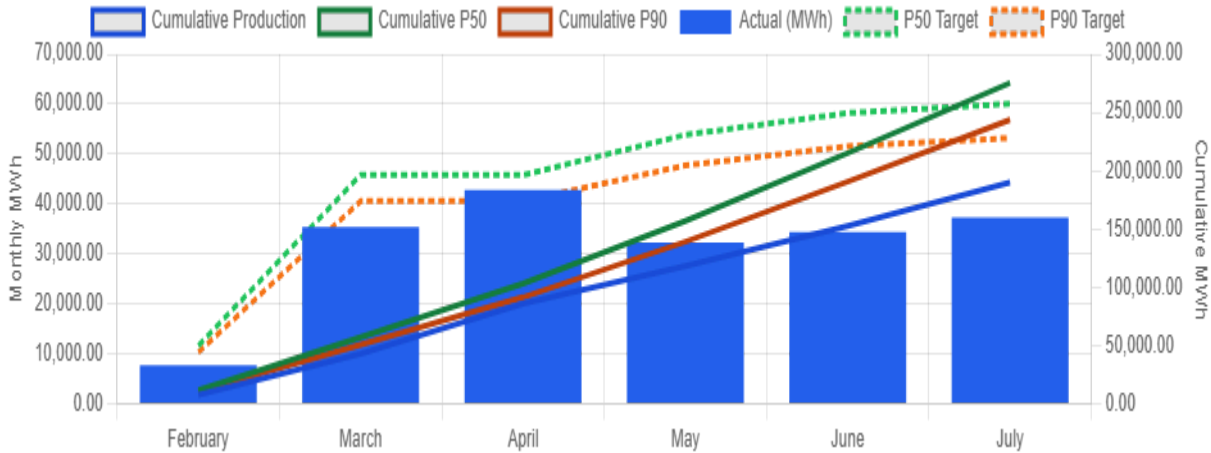


PLANT AVAILABILITY

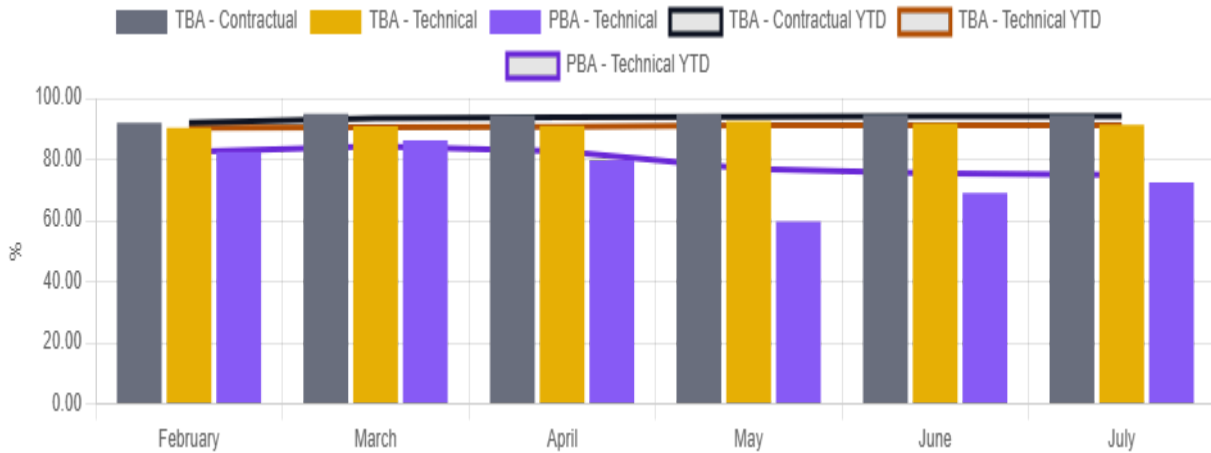

WIND SPEED

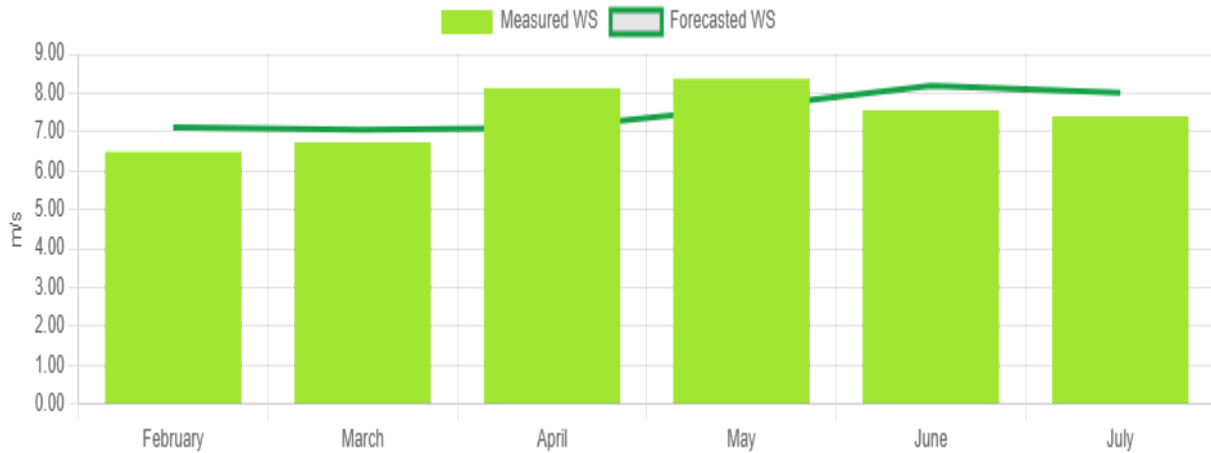

ANNUAL PRODUCTION AND AVAILABILITY PER WT

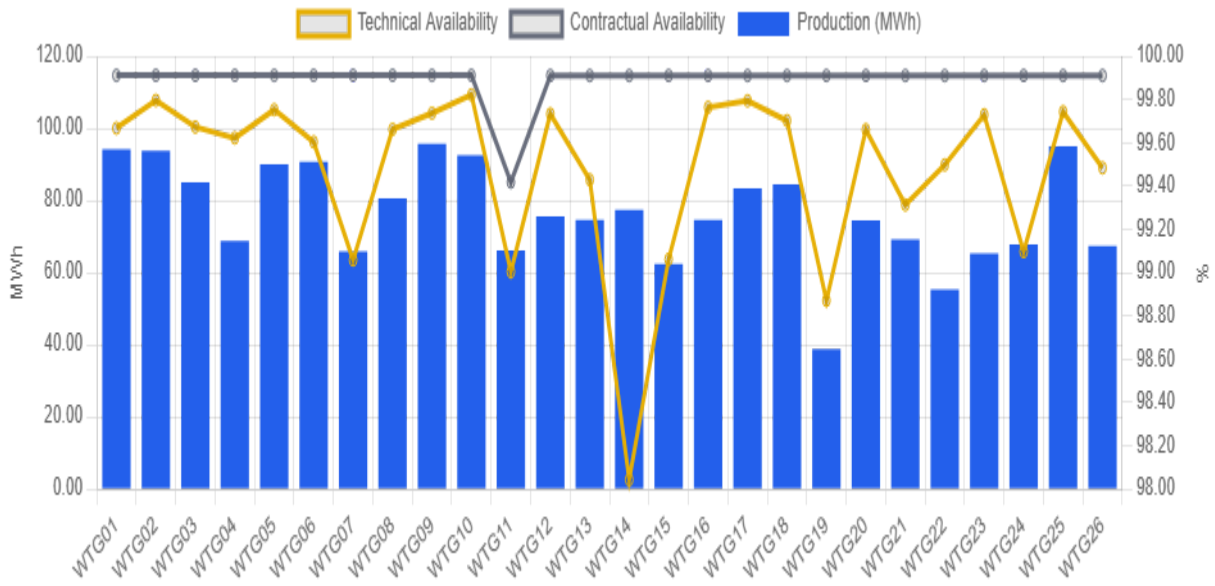

LOSSES BREAKDOWN

