


San Kraal: the plant produced 37.4 GWh, significantly below P50 and P90 targets. Contractual availability averaged 99.5%, while technical availability was lower at 95.6%. The negative delta in production was visible in the wind resource deviation of -19%.


FULL KPI MATRIX

CATEGORY	2025	2026	JAN	FEB	MAR	APR	MAY	JUN	JUL	TOTAL
A. Production										
Measured (MWh)	35,374	274,172	49,138	36,763	35,552	46,951	31,244	37,114	37,409	309,546
Deviation Historical	–	–	–	–	–	–	–	–	–	–
Deviation P50	4.6%	-20.9%	7.8%	-6.8%	-18.7%	5.9%	-41.7%	-37.2%	-38.7%	-18.7%
Deviation P90	17.2%	-11.4%	20.8%	4.5%	-8.9%	18.6%	-34.7%	-29.7%	-31.3%	-8.9%
Capacity Factor	33.1%	37.5%	46.0%	38.1%	33.3%	45.5%	29.0%	35.7%	35.0%	37.0%
Electrical Losses	1.4%	1.2%	1.5%	1.4%	1.5%	1.6%	0.7%	0.9%	1.2%	1.3%
B. Consumption										
Measured (MWh)	0	189	28	26	34	16	16	42	27	189
Ratio to Production	0.0%	0.1%	0.1%	0.1%	0.1%	0.0%	0.1%	0.1%	0.1%	0.1%
C. Availability										
TBA - Contractual	98.9%	98.1%	99.8%	98.2%	99.4%	97.1%	94.0%	98.7%	99.5%	98.2%
TBA - Technical	95.8%	94.8%	97.8%	94.4%	94.5%	94.8%	90.6%	95.7%	95.6%	94.9%
PBA - Technical	97.9%	97.2%	99.3%	97.1%	98.8%	96.1%	91.7%	98.4%	99.4%	97.3%
D. OLF - Losses										
Manufacturer	1.6%	1.8%	0.8%	2.7%	1.1%	2.2%	3.6%	1.4%	0.6%	1.8%
Owner	0.3%	0.6%	0.1%	0.4%	0.5%	0.3%	1.9%	0.3%	0.6%	0.6%
Environmental	0.7%	0.3%	0.1%	0.6%	0.4%	0.2%	0.6%	0.1%	0.1%	0.4%
Utility	0.3%	10.9%	0.0%	0.3%	0.8%	3.6%	32.0%	17.6%	21.8%	9.6%
Bat Curtailment	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%
E. Wind										
Forecasted WS (m/s)	8.4	8.5	8.1	7.8	7.9	8.1	8.9	9.6	9.4	8.5
Measured WS (m/s)	8.3	7.7	8	7.3	6.8	8.3	8.5	7.7	7.6	7.8
WindSpeed Deviation	-1.6%	-8.9%	-0.7%	-5.7%	-14.1%	2.0%	-4.4%	-20.3%	-19.3%	-8.0%


PLANT PRODUCTION

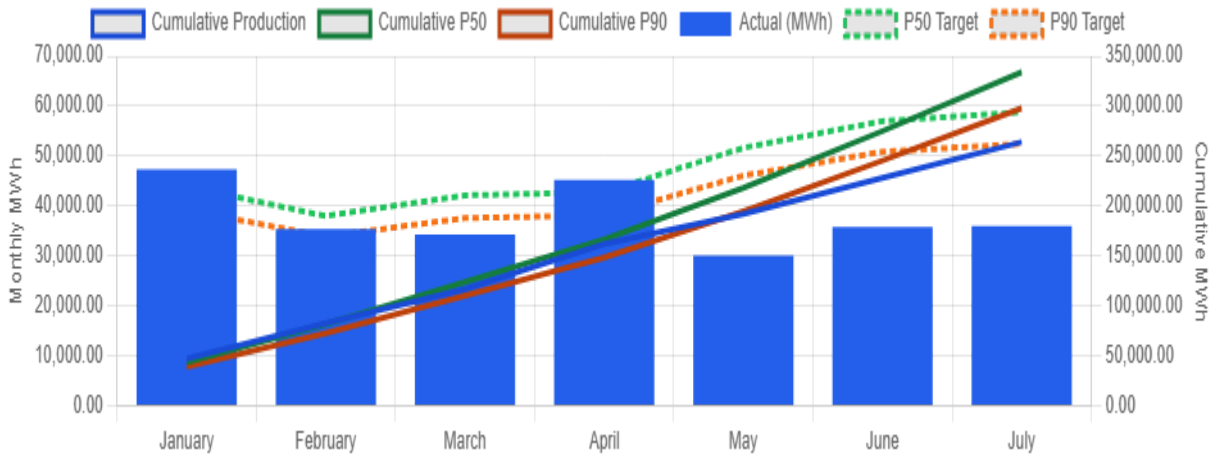


PLANT AVAILABILITY

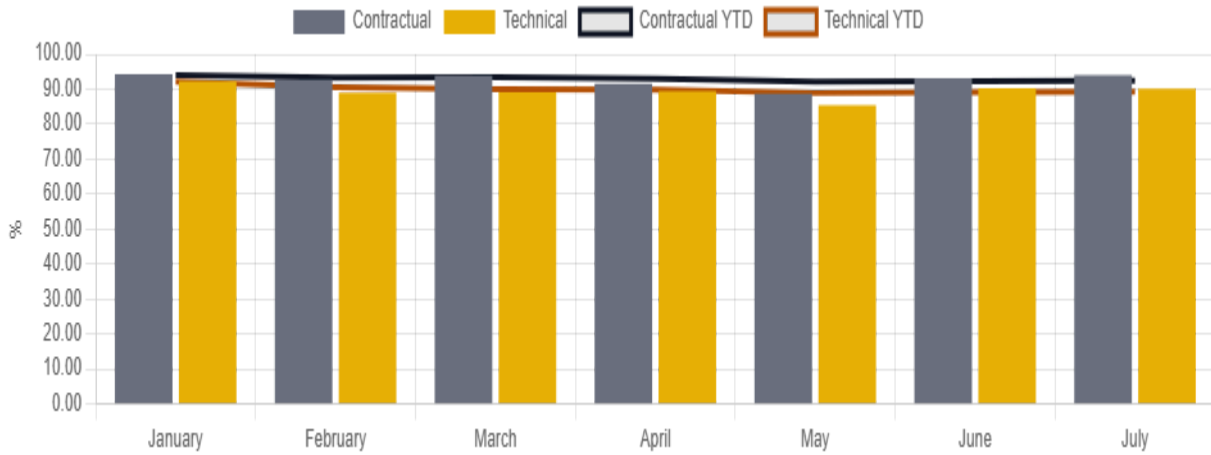

WIND SPEED

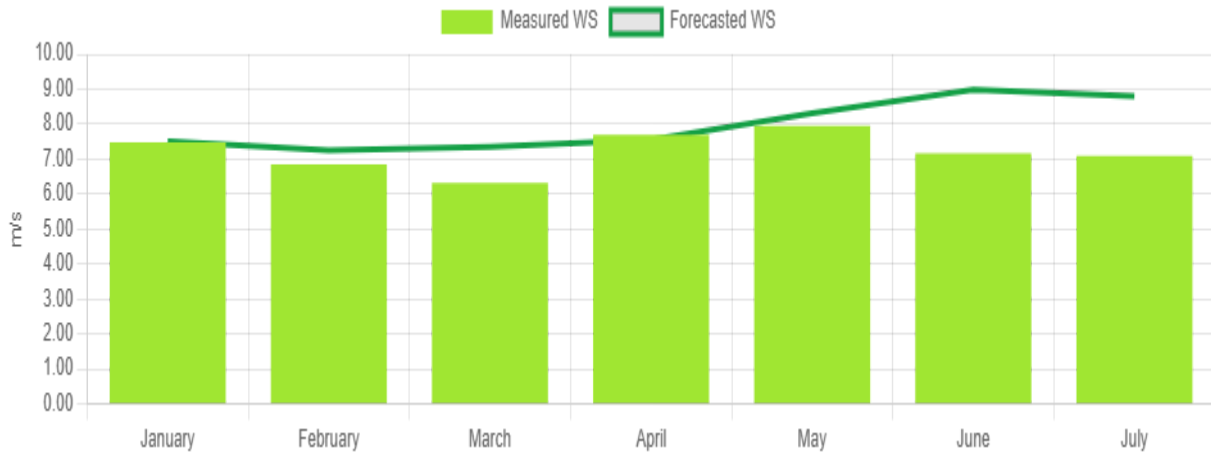

ANNUAL PRODUCTION AND AVAILABILITY PER WT

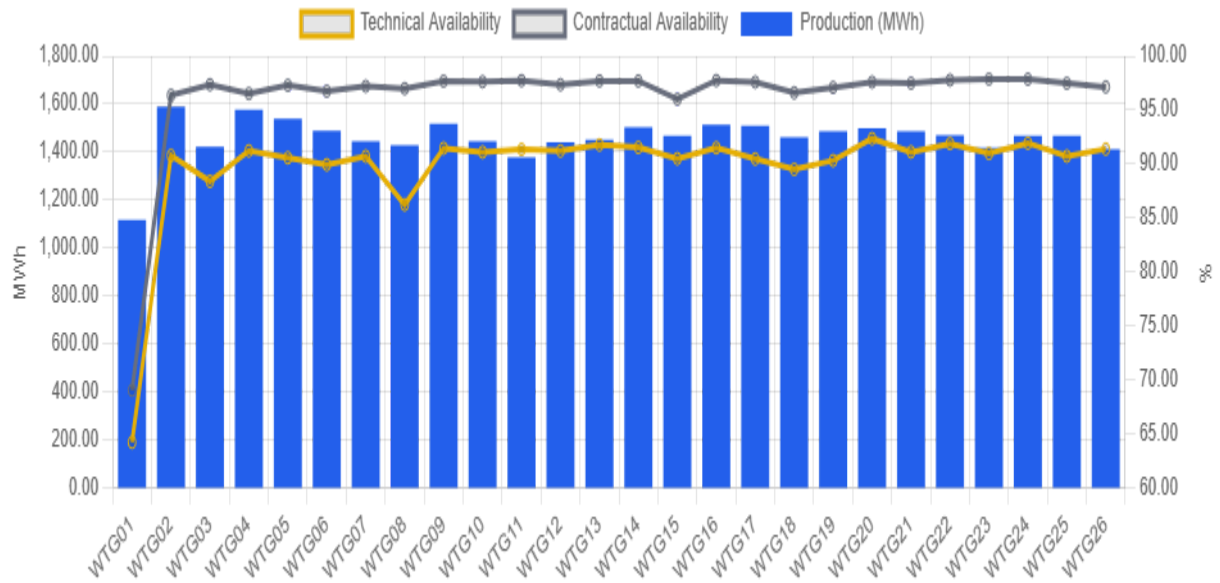

OPERATIONAL LOSS FACTORS

