

Wesley: the plant produced 9.1 GWh, significantly below historical, P50 and P90 targets. Contractual availability averaged 98.0%, while technical availability was 97.7%. The negative delta in production was visible in the wind resource deviation of -24%.


FULL KPI MATRIX

CATEGORY	2022	2023	2024	2025	2026	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	TOTAL
A. Production														
Measured (MWh)	129,047	132,295	132,220	127,062	74,037	10,049	10,554	10,719	9,132	8,946	7,787	7,787	9,064	594,662
Deviation Historical	–	2.5%	1.2%	-3.1%	-13.2%	-7.8%	6.7%	-3.7%	-10.9%	2.7%	-32.9%	-33.4%	-18.1%	-2.2%
Deviation P50	-8.6%	-6.3%	-6.3%	-10.0%	-18.9%	-12.2%	2.3%	-6.3%	-15.0%	-19.9%	-32.8%	-32.8%	-30.3%	-9.3%
Deviation P90	2.7%	5.3%	5.2%	1.1%	-8.9%	-1.4%	14.9%	5.2%	-4.5%	-10.0%	-24.5%	-24.5%	-21.7%	1.8%
Capacity Factor	1.8%	36.8%	44.4%	42.5%	36.7%	39.7%	45.6%	42.4%	37.4%	33.2%	31.5%	28.0%	35.9%	32.1%
Electrical Losses	-95.8%	-15.5%	1.6%	0.9%	-0.7%	1.4%	0.1%	1.6%	1.7%	-4.6%	0.5%	-7.8%	1.7%	-23.4%
B. Consumption														
Measured (MWh)	172	174	186	166	163	17	16	19	16	20	23	25	27	860
Ratio to Production	0.1%	0.1%	0.1%	0.1%	0.2%	0.2%	0.1%	0.2%	0.2%	0.2%	0.3%	0.3%	0.3%	0.2%
C. Availability														
TBA - Contractual	–	97.3%	96.5%	97.9%	98.3%	99.1%	97.4%	99.3%	98.7%	98.1%	97.9%	97.6%	98.0%	97.4%
TBA - Technical	–	96.6%	95.5%	97.3%	97.5%	99.0%	97.3%	99.0%	94.5%	97.9%	97.1%	97.5%	97.7%	96.7%
PBA - Technical	100.0%	96.9%	94.8%	94.5%	91.2%	98.2%	96.9%	92.4%	82.7%	88.9%	87.8%	91.5%	91.4%	95.8%
D. Losses Breakdown														
Grid	–	0.5%	1.1%	3.4%	7.2%	0.8%	0.7%	7.2%	14.9%	9.7%	11.4%	5.5%	7.2%	2.9%
Breakdown	–	1.9%	1.9%	1.2%	0.9%	0.7%	1.0%	0.3%	2.1%	0.6%	0.5%	1.7%	0.3%	1.5%
Maintenance	–	0.4%	0.5%	0.6%	0.6%	0.3%	1.3%	–	0.1%	0.7%	0.2%	0.9%	0.8%	0.5%
Partial Perf.	–	0.2%	0.7%	0.3%	0.1%	0.0%	0.0%	0.0%	0.0%	0.1%	0.1%	0.3%	0.2%	0.4%
BoP	–	0.0%	0.0%	0.1%	0.0%	–	–	0.0%	0.0%	0.0%	0.0%	0.0%	–	0.0%
Environmental	–	0.1%	–	0.0%	–	–	–	–	–	–	–	–	–	0.0%
Data Quality	–	0.2%	0.1%	0.1%	0.1%	–	–	–	–	–	0.1%	–	–	0.1%
MCR	–	–	4.8%	–	–	–	–	–	–	–	–	–	–	4.8%
Requested Shutdown	–	0.1%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.1%	–	–	–	–	0.0%
E. Wind														
Forecasted WS (m/s)	8.3	8.3	8.3	8.3	8.1	8.1	7.3	8.1	7.6	7.9	8.2	8.2	9.2	8.3
Measured WS (m/s)	7.8	7.9	8	7.8	7.3	7.3	7.9	7.9	7.7	7.4	6.8	6.4	7	7.8
WindSpeed Deviation	-6.3%	-5.3%	-3.7%	-6.0%	-8.9%	-9.4%	8.8%	-2.0%	0.9%	-6.4%	-17.0%	-22.5%	-23.6%	-5.8%


LOSSES BREAKDOWN WATERFALL — AUGUST 2026




PLANT PRODUCTION

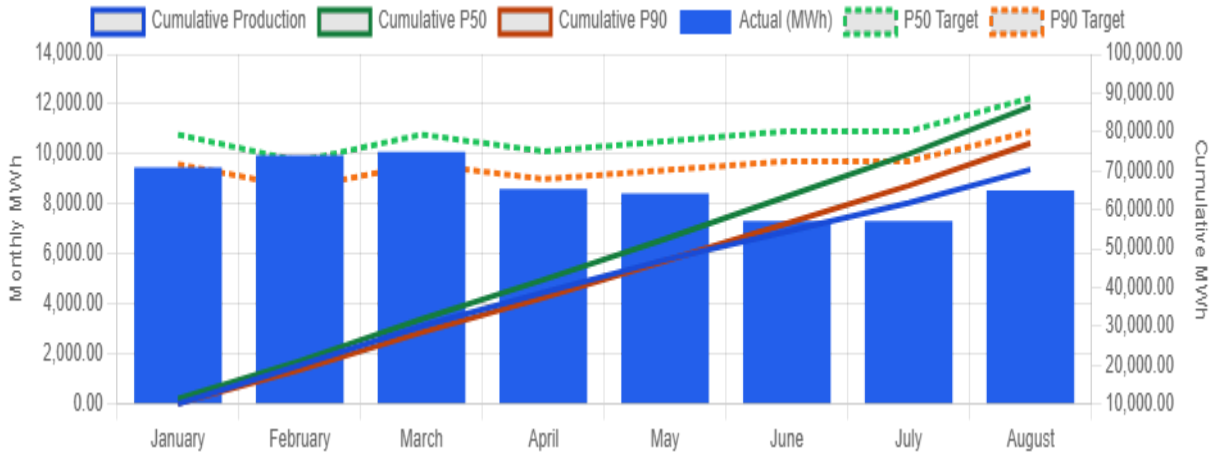


PLANT AVAILABILITY

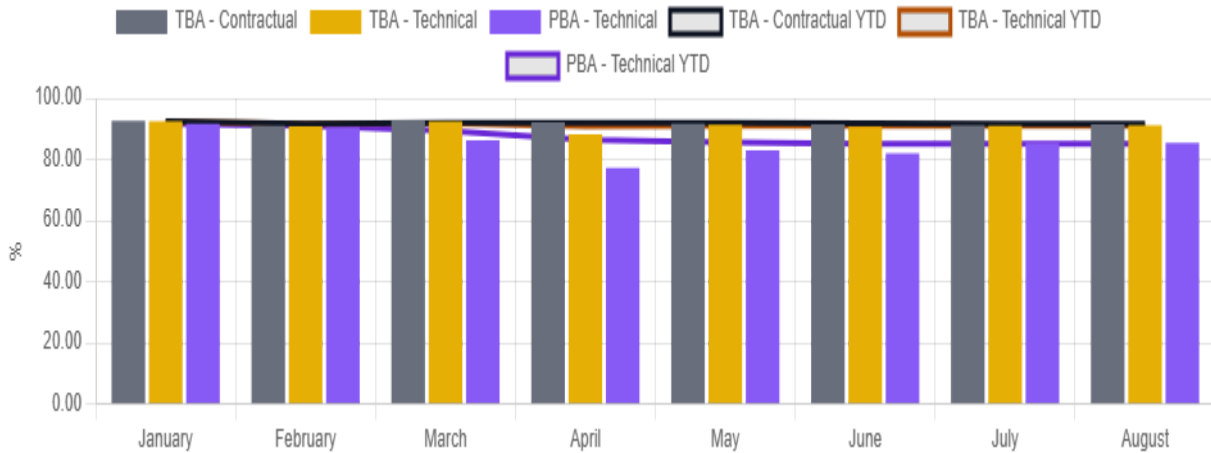

WIND SPEED

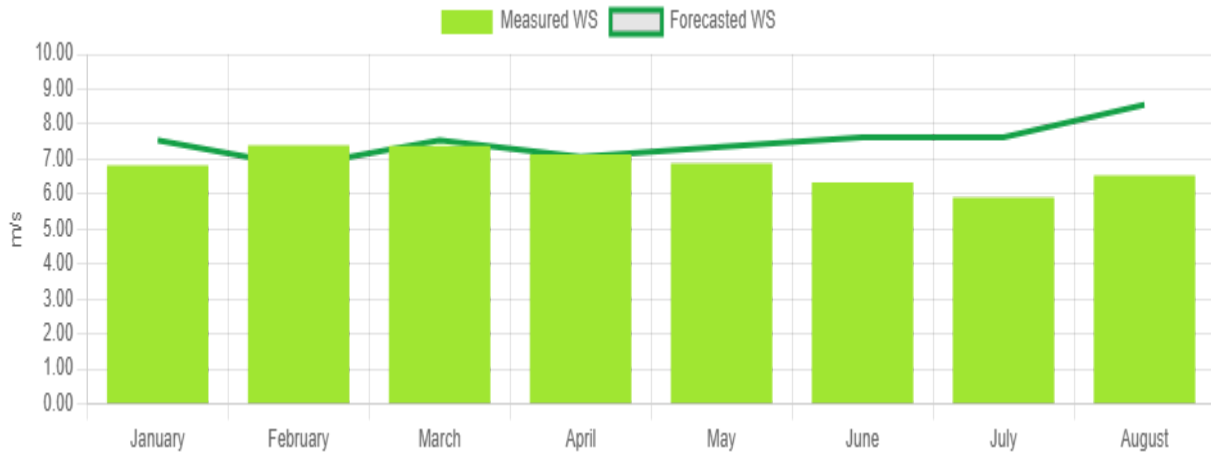

ANNUAL PRODUCTION AND AVAILABILITY PER WT

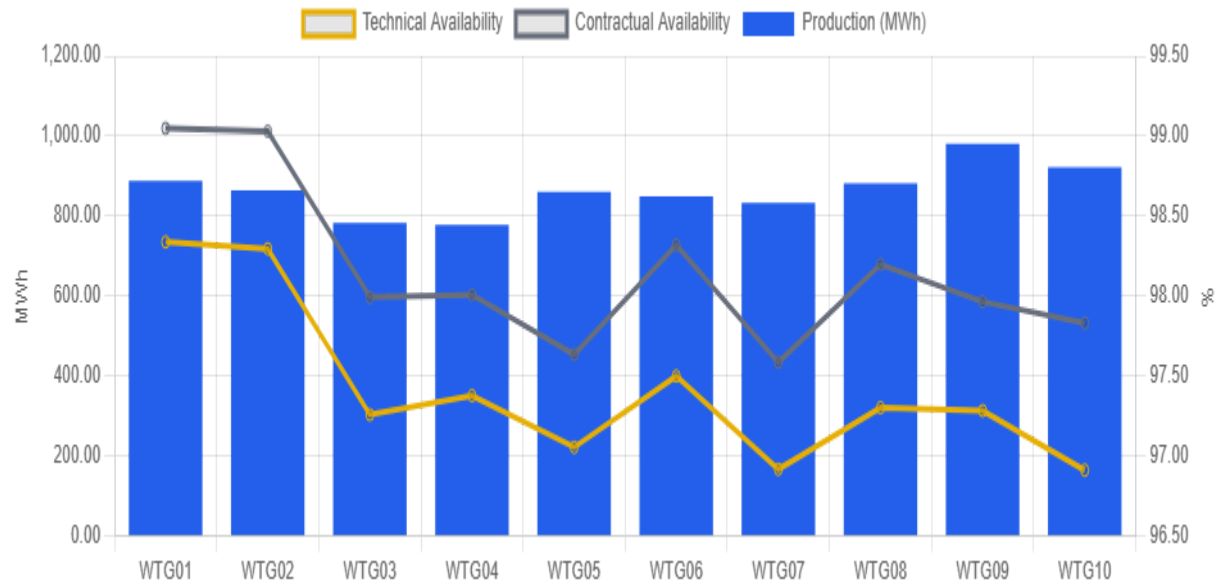

LOSSES BREAKDOWN

