


Wesley: the plant produced 7.8 GWh, significantly below historical, P50 and P90 targets. Contractual availability averaged 97.6%, while technical availability was 97.5%. The negative delta in production was visible in the wind resource deviation of -23%.


FULL KPI MATRIX

CATEGORY	2022	2023	2024	2025	2026	JAN	FEB	MAR	APR	MAY	JUN	JUL	TOTAL
A. Production													
Measured (MWh)	129,047	132,295	132,220	127,062	64,973	10,049	10,554	10,719	9,132	8,946	7,787	7,787	585,597
Deviation Historical	-	2.5%	1.2%	-3.1%	-12.4%	-7.8%	6.7%	-3.7%	-10.9%	2.7%	-32.9%	-33.4%	-1.8%
Deviation P50	-8.6%	-6.3%	-6.3%	-10.0%	-17.0%	-12.2%	2.3%	-6.3%	-15.0%	-19.9%	-32.8%	-32.8%	-8.9%
Deviation P90	2.7%	5.3%	5.2%	1.1%	-6.8%	-1.4%	14.9%	5.2%	-4.5%	-10.0%	-24.5%	-24.5%	2.3%
Capacity Factor	1.8%	36.8%	44.4%	42.5%	36.8%	39.7%	45.6%	42.4%	37.4%	33.2%	31.5%	28.0%	32.1%
B. Consumption													
Measured (MWh)	172	174	186	166	136	17	16	19	16	20	23	25	833
Ratio to Production	0.1%	0.1%	0.1%	0.1%	0.2%	0.2%	0.1%	0.2%	0.2%	0.2%	0.3%	0.3%	0.1%
C. Availability													
TBA - Contractual	-	97.3%	96.5%	97.9%	98.3%	99.1%	97.4%	99.3%	98.7%	98.1%	97.9%	97.6%	97.4%
TBA - Technical	-	96.6%	95.5%	97.3%	97.5%	99.0%	97.3%	99.0%	94.5%	97.9%	97.1%	97.5%	96.6%
PBA - Technical	100.0%	96.9%	94.8%	94.5%	91.2%	98.2%	96.9%	92.4%	82.7%	88.9%	87.8%	91.5%	95.9%
D. Losses Breakdown													
Grid	-	0.6%	1.1%	3.4%	7.2%	0.8%	0.7%	7.2%	14.9%	10.0%	10.9%	5.5%	2.8%
Breakdown	-	2.2%	1.9%	1.2%	1.1%	0.7%	1.0%	0.3%	2.1%	0.6%	1.1%	1.7%	1.7%
Maintenance	-	0.5%	0.5%	0.6%	0.6%	0.3%	1.3%	-	0.1%	0.7%	0.2%	0.9%	0.5%
Partial Perf.	-	0.2%	0.7%	0.3%	0.1%	0.0%	0.0%	0.0%	0.0%	0.1%	0.1%	0.3%	0.4%
Environmental	-	0.1%	0.1%	0.1%	0.0%	0.0%	0.0%	0.0%	-	0.1%	0.0%	-	0.1%
Data Quality	96.1%	2.0%	0.2%	0.1%	0.3%	-	0.5%	-	-	0.4%	0.1%	-	28.8%
Requested Shutdown	-	0.1%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.1%	-	-	-	0.1%
Electrical Losses	-88.9%	-17.7%	1.5%	0.8%	-1.0%	1.4%	0.1%	1.4%	1.4%	-4.2%	0.4%	-7.8%	-22.9%
BoP	-	0.0%	0.0%	0.1%	0.0%	-	-	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%
MCR	-	-	4.8%	-	-	-	-	-	-	-	-	-	4.8%
E. Wind													
Forecasted WS (m/s)	8.3	8.3	8.3	8.3	7.9	8.1	7.3	8.1	7.6	7.9	8.2	8.2	8.3
Measured WS (m/s)	7.8	7.9	8	7.8	7.3	7.3	7.9	7.9	7.7	7.4	6.8	6.4	7.8
WindSpeed Deviation	-6.3%	-5.3%	-3.7%	-6.0%	-6.8%	-9.4%	8.8%	-2.0%	0.9%	-6.4%	-17.0%	-22.5%	-5.5%


PLANT PRODUCTION

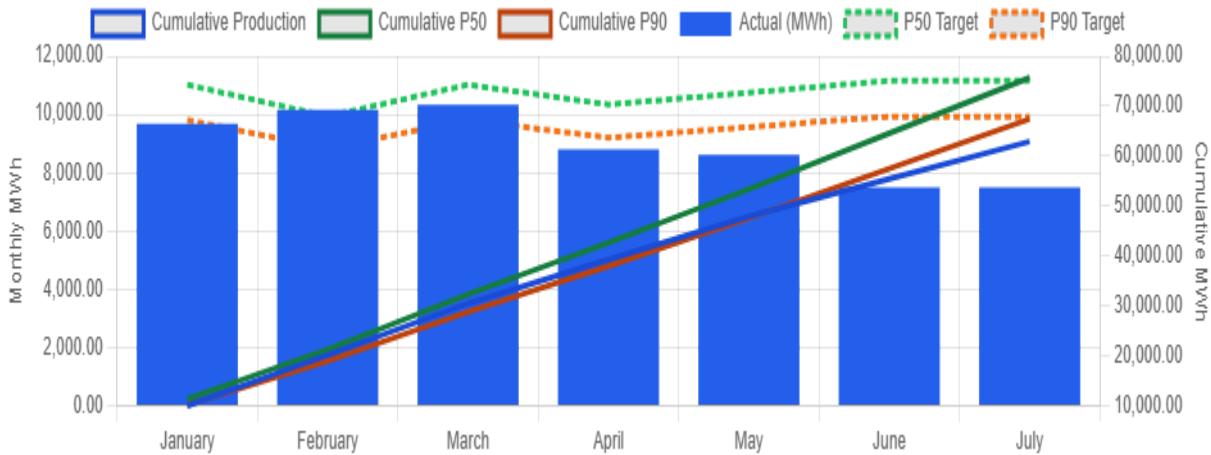


PLANT AVAILABILITY

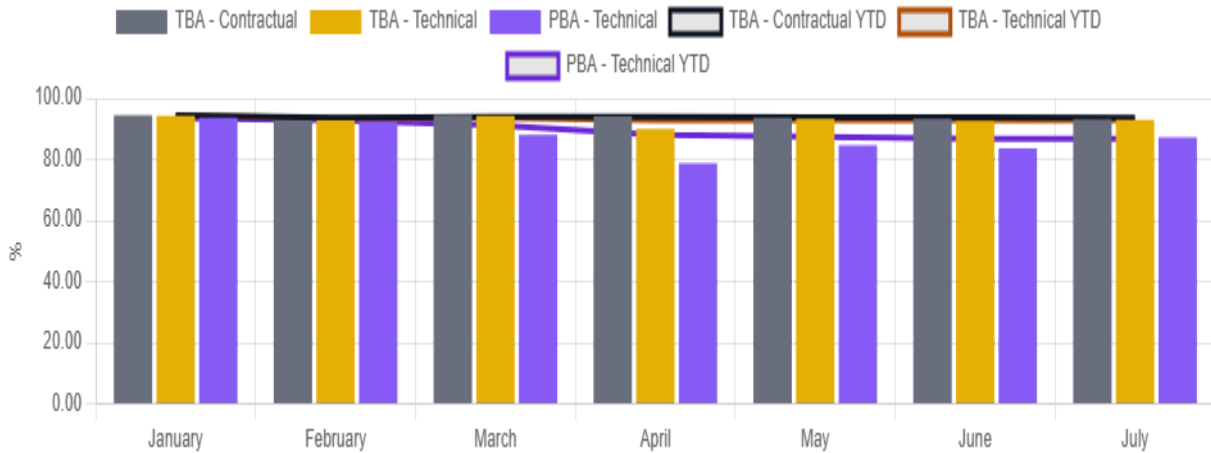

WIND SPEED

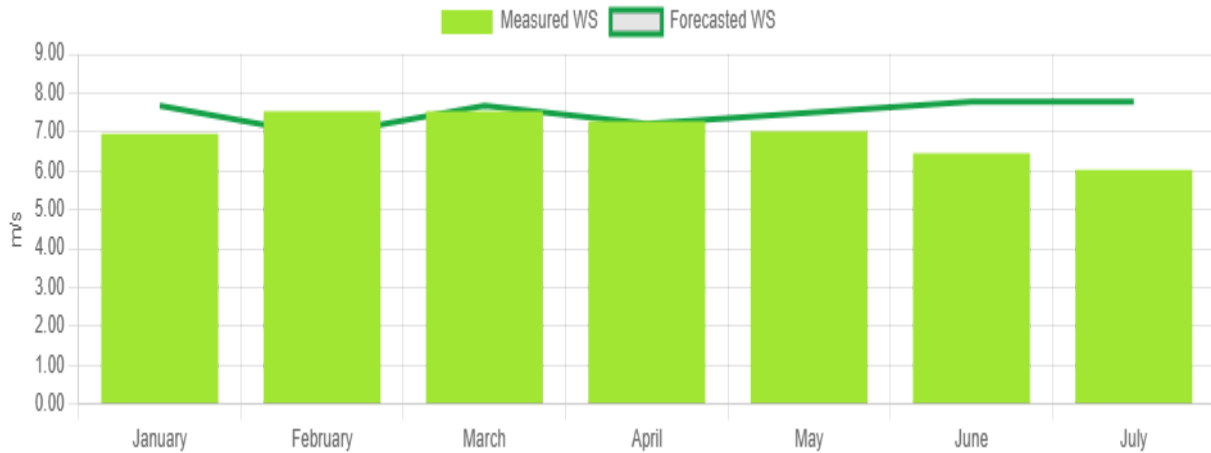

ANNUAL PRODUCTION AND AVAILABILITY PER WT

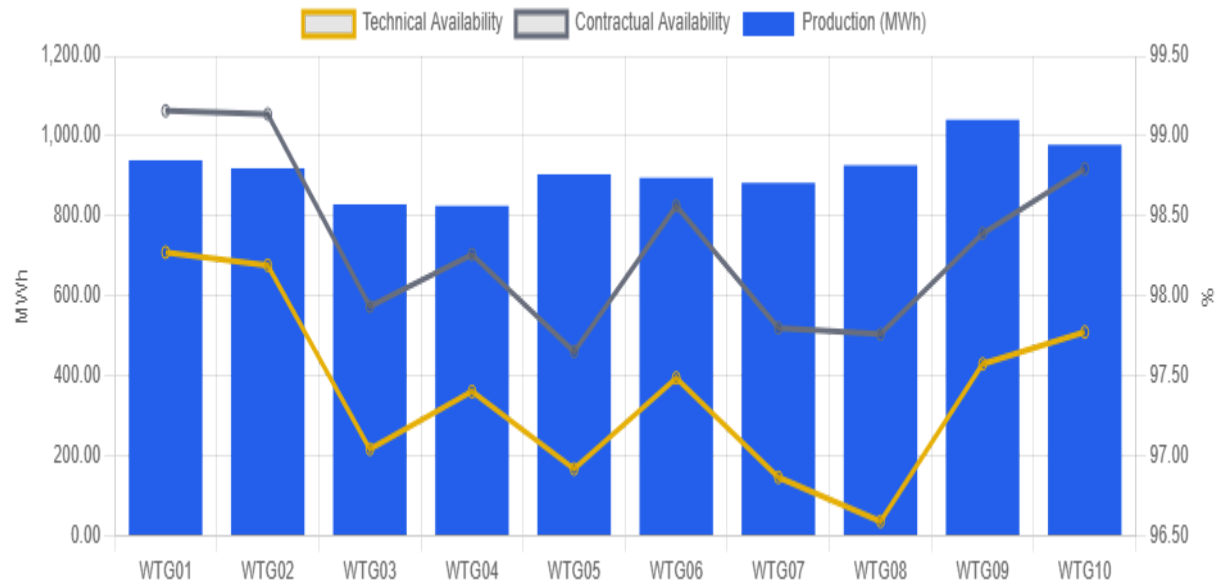

LOSSES BREAKDOWN

