


Grassridge: the plant produced 9.7 GWh, significantly below historical, P50 and P90 targets. Contractual availability averaged 98.2%, while technical availability was lower at 92.4%. The negative delta in production was visible in the wind resource deviation of -17%.


FULL KPI MATRIX

CATEGORY	2022	2023	2024	2025	2026	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	TOTAL
A. Production														
Measured (MWh)	162,374	171,642	160,007	160,758	84,977	13,718	11,001	8,118	11,322	11,569	11,549	7,994	9,708	739,758
Deviation Historical	–	5.7%	-4.2%	-2.4%	-21.9%	11.2%	-4.4%	-31.6%	5.2%	-2.3%	-36.3%	-54.1%	-34.9%	-4.2%
Deviation P50	-7.4%	-10.2%	-16.3%	-15.9%	-31.5%	17.7%	-20.0%	-43.4%	-12.9%	-21.4%	-38.3%	-59.0%	-47.1%	-15.2%
Deviation P90	-2.7%	2.9%	-4.1%	-3.6%	-21.5%	34.8%	-8.4%	-35.1%	-0.2%	-9.9%	-29.4%	-53.0%	-39.4%	-4.6%
Capacity Factor	29.2%	30.7%	28.4%	28.6%	23.0%	29.0%	25.8%	17.3%	24.7%	24.6%	25.3%	17.0%	20.6%	28.3%
Electrical Losses	1.6%	1.2%	0.6%	0.4%	1.7%	1.5%	1.6%	2.0%	1.4%	2.0%	1.6%	1.8%	1.7%	1.1%
B. Consumption														
Measured (MWh)	565	585	584	653	522	57	65	86	60	54	39	95	65	2,910
Ratio to Production	0.4%	0.4%	0.4%	0.4%	0.7%	0.4%	0.6%	1.1%	0.5%	0.5%	0.3%	1.2%	0.7%	0.4%
C. Availability														
TBA - Contractual	97.0%	95.5%	94.9%	97.0%	97.2%	98.1%	96.2%	97.3%	96.4%	96.4%	98.7%	96.2%	98.2%	96.3%
TBA - Technical	96.6%	95.7%	90.2%	92.6%	89.0%	98.1%	90.7%	87.9%	80.9%	82.8%	90.8%	88.5%	92.4%	93.1%
PBA - Technical	97.4%	95.9%	95.3%	97.4%	97.1%	98.0%	95.9%	96.9%	97.1%	95.3%	98.7%	96.7%	98.0%	96.6%
D. OLF - Losses														
Manufacturer	3.0%	4.4%	5.1%	2.7%	2.9%	2.0%	3.8%	3.1%	3.0%	4.7%	1.4%	3.0%	2.1%	3.7%
Owner	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.1%	0.0%	0.0%	0.0%	0.0%	0.1%	0.0%	0.0%
Environmental	0.0%	0.0%	0.0%	0.0%	0.1%	0.3%	0.1%	0.1%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%
Utility	0.4%	0.2%	0.6%	2.7%	12.1%	0.0%	0.0%	13.1%	16.6%	11.6%	22.6%	14.4%	18.5%	2.5%
Bat Curtailment	0.0%	0.0%	0.7%	1.0%	0.3%	0.0%	0.4%	0.6%	0.8%	0.8%	0.0%	0.0%	0.0%	0.4%
E. Wind														
Forecasted WS (m/s)	6.7	6.7	6.7	6.7	6.7	6.5	6.6	6.2	6	6.8	7.3	7.2	7	6.7
Measured WS (m/s)	6.3	6.5	6.4	6.3	5.9	6.2	5.8	5.3	6.2	6.5	6.5	5.2	5.8	6.3
WindSpeed Deviation	-6.6%	-3.1%	-5.0%	-6.4%	-11.3%	-5.3%	-12.0%	-15.3%	3.0%	-4.9%	-10.6%	-28.0%	-17.2%	-6.1%


PLANT PRODUCTION

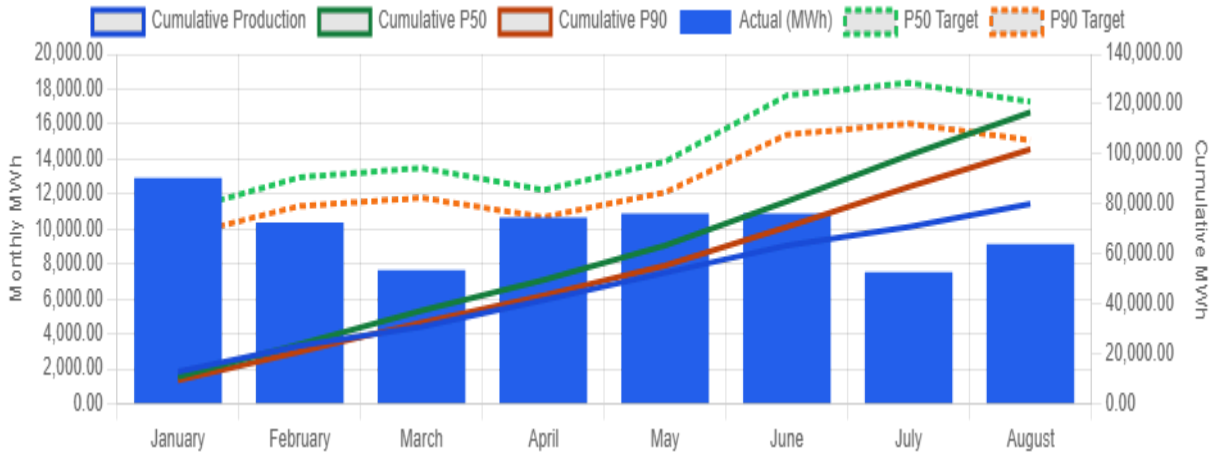


PLANT AVAILABILITY

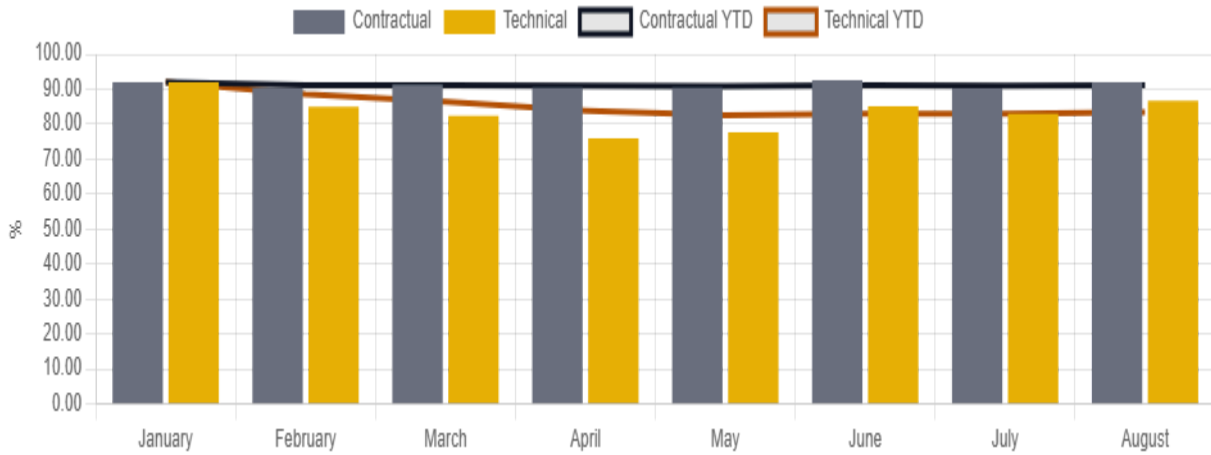

WIND SPEED

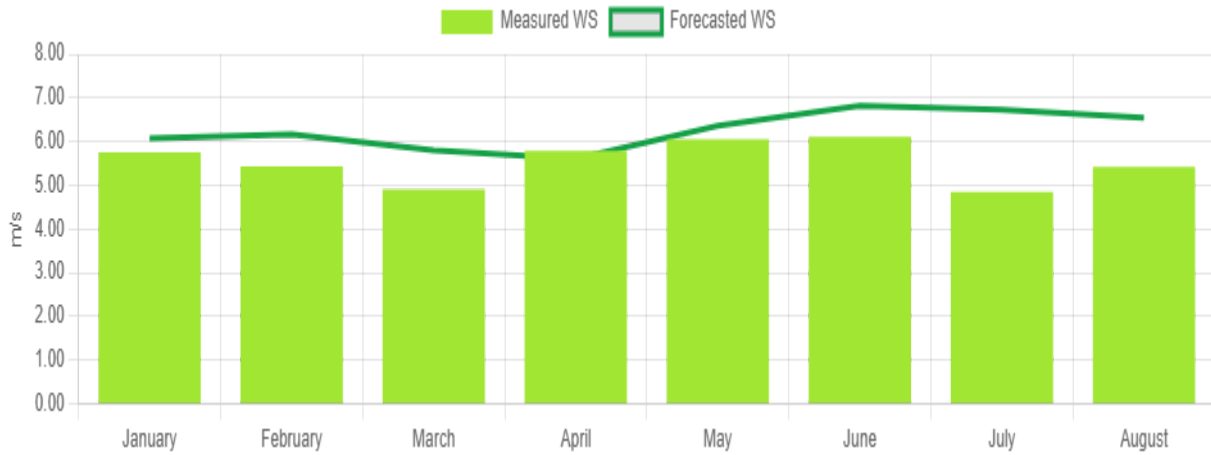

ANNUAL PRODUCTION AND AVAILABILITY PER WT

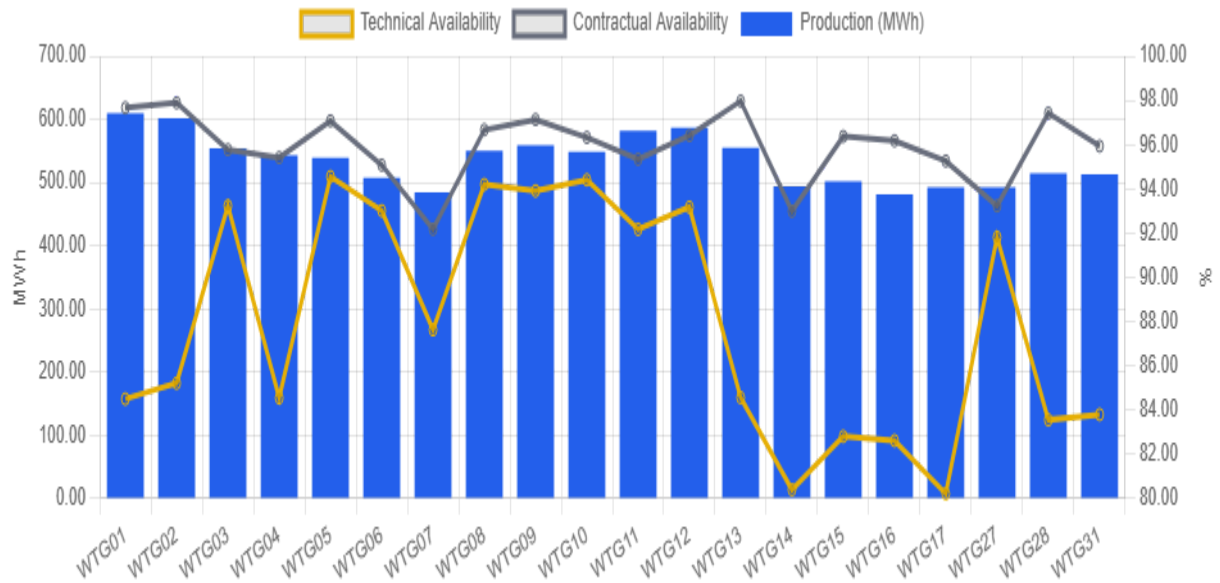

OPERATIONAL LOSS FACTORS

