


San Kraal: the plant produced 26.0 GWh, significantly below P50 and P90 targets. Contractual availability averaged 85.2%, while technical availability was lower at 81.8%. The negative delta in production was visible in the wind resource deviation of -24%.


FULL KPI MATRIX

CATEGORY	2025	2026	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	TOTAL
A. Production											
Measured (MWh)	35,374	300,204	49,138	36,763	35,552	46,951	31,244	37,114	37,409	26,032	335,578
Deviation Historical	-	-	-	-	-	-	-	-	-	-	-
Deviation P50	4.6%	-26.7%	7.8%	-6.8%	-18.7%	5.9%	-41.7%	-37.2%	-38.7%	-58.6%	-24.3%
Deviation P90	17.2%	-17.9%	20.8%	4.5%	-8.9%	18.6%	-34.7%	-29.7%	-31.3%	-53.6%	-15.2%
Capacity Factor	33.1%	35.9%	46.0%	38.1%	33.3%	45.5%	29.0%	35.7%	35.0%	24.3%	35.6%
Electrical Losses	1.4%	1.3%	1.5%	1.4%	1.5%	1.6%	0.7%	0.9%	1.2%	1.3%	1.3%
B. Consumption											
Measured (MWh)	0	228	28	26	34	16	16	42	27	40	228
Ratio to Production	0.0%	0.1%	0.1%	0.1%	0.1%	0.0%	0.1%	0.1%	0.1%	0.2%	0.1%
C. Availability											
TBA - Contractual	98.9%	96.5%	99.8%	98.2%	99.4%	97.1%	94.0%	98.7%	99.5%	85.2%	96.8%
TBA - Technical	95.8%	93.1%	97.8%	94.4%	94.5%	94.8%	90.6%	95.7%	95.6%	81.8%	93.4%
PBA - Technical	97.9%	94.7%	99.3%	97.1%	98.8%	96.1%	91.7%	98.4%	99.4%	76.8%	95.0%
D. OLF - Losses											
Manufacturer	1.6%	2.3%	0.8%	2.7%	1.1%	2.2%	3.6%	1.4%	0.6%	6.1%	2.2%
Owner	0.3%	0.6%	0.1%	0.4%	0.5%	0.3%	1.9%	0.3%	0.6%	0.3%	0.5%
Environmental	0.7%	0.3%	0.1%	0.6%	0.4%	0.2%	0.6%	0.1%	0.1%	0.1%	0.3%
Utility	0.3%	12.9%	0.0%	0.3%	0.8%	3.6%	32.0%	17.6%	21.8%	27.4%	11.5%
Bat Curtailment	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%
E. Wind											
Forecasted WS (m/s)	8.4	8.7	8.1	7.8	7.9	8.1	8.9	9.6	9.4	9.6	8.6
Measured WS (m/s)	8.3	7.7	8	7.3	6.8	8.3	8.5	7.7	7.6	7.3	7.8
WindSpeed Deviation	-1.6%	-10.8%	-0.7%	-5.7%	-14.1%	2.0%	-4.4%	-20.3%	-19.3%	-24.0%	-9.8%


PLANT PRODUCTION

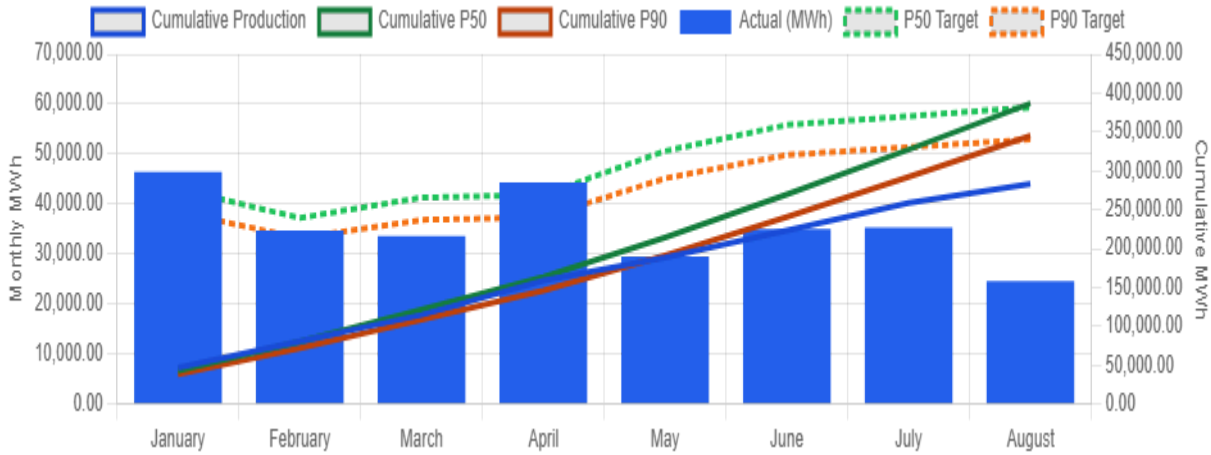


PLANT AVAILABILITY

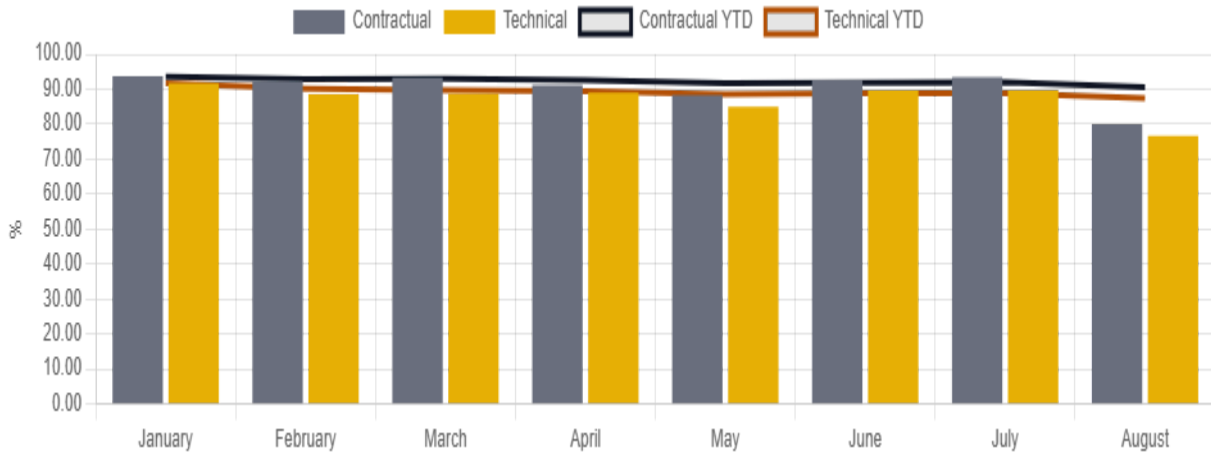

WIND SPEED

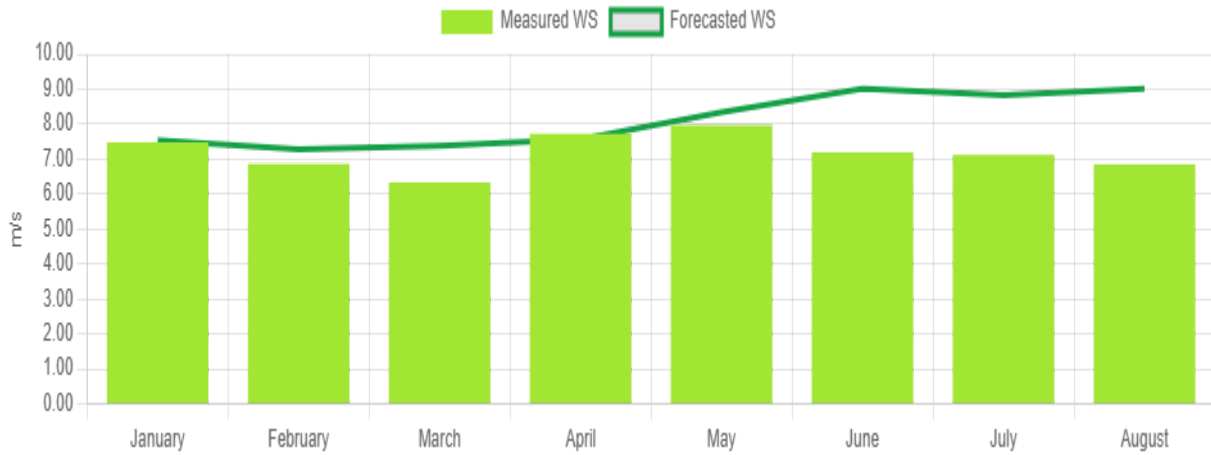

ANNUAL PRODUCTION AND AVAILABILITY PER WT

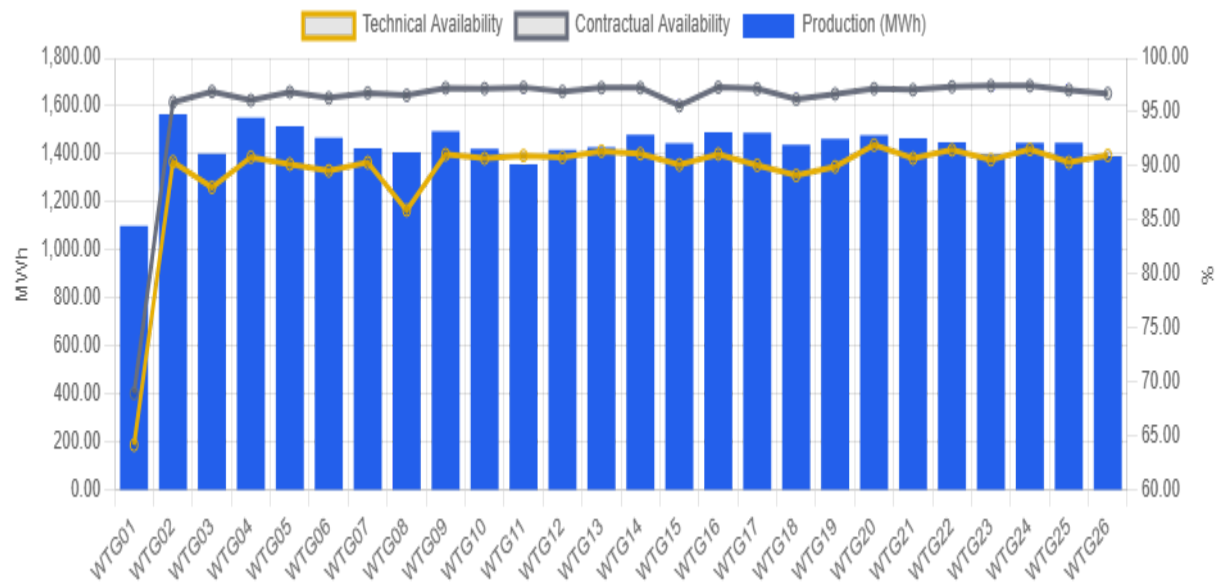

OPERATIONAL LOSS FACTORS

