


Waainek: the plant produced 6.4 GWh, significantly below historical, P50 and P90 targets. Contractual availability averaged 87.1%, while technical availability was 85.1%. The negative delta in production was visible in the wind resource deviation of -16%.


FULL KPI MATRIX

CATEGORY	2022	2023	2024	2025	2026	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	TOTAL
A. Production														
Measured (MWh)	90,260	92,833	92,112	87,117	51,466	6,386	5,427	5,675	7,217	6,864	7,770	5,726	6,403	413,788
Deviation Historical	-	2.9%	0.6%	-5.0%	-16.0%	2.1%	-5.2%	-17.1%	5.3%	1.8%	-20.8%	-44.3%	-26.7%	-3.4%
Deviation P50	-11.7%	-9.2%	-9.9%	-14.8%	-23.2%	-21.0%	-19.6%	-20.7%	-8.4%	-22.9%	-24.8%	-32.5%	-32.0%	-13.1%
Deviation P90	1.4%	4.3%	3.5%	-2.1%	-11.7%	-9.2%	-7.6%	-8.9%	5.3%	-11.4%	-13.6%	-22.5%	-21.8%	-0.2%
Capacity Factor	42.4%	43.4%	43.1%	40.6%	36.3%	35.3%	33.2%	31.4%	41.2%	38.0%	44.4%	31.7%	35.4%	41.5%
Electrical Losses	1.2%	1.0%	1.2%	0.6%	1.2%	1.1%	1.1%	1.2%	1.2%	1.2%	1.1%	1.3%	1.2%	1.0%
B. Consumption														
Measured (MWh)	100	83	117	118	113	15	12	19	19	17	8	9	13	531
Ratio to Production	0.1%	0.1%	0.1%	0.1%	0.2%	0.2%	0.2%	0.3%	0.3%	0.3%	0.1%	0.2%	0.2%	0.1%
C. Availability														
TBA - Contractual	93.9%	88.5%	96.3%	96.9%	95.3%	96.9%	90.2%	92.8%	98.0%	99.5%	99.3%	98.6%	87.1%	94.1%
TBA - Technical	93.7%	88.7%	92.9%	92.3%	89.9%	93.0%	86.8%	86.6%	92.1%	92.6%	97.1%	85.9%	85.1%	91.6%
PBA - Technical	97.2%	95.6%	95.5%	95.4%	95.3%	97.9%	89.5%	92.6%	98.3%	98.7%	99.6%	98.6%	87.2%	95.8%
D. OLF - Losses														
Manufacturer	2.8%	4.4%	2.6%	2.6%	4.7%	2.2%	10.5%	7.4%	1.7%	1.3%	0.4%	1.4%	12.8%	3.3%
Owner	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.1%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%
Environmental	0.0%	0.0%	1.9%	1.9%	0.6%	1.6%	1.1%	1.7%	0.0%	0.0%	0.0%	0.0%	0.0%	0.9%
Utility	0.1%	0.0%	0.4%	1.7%	5.0%	1.5%	0.1%	1.4%	10.0%	8.0%	2.9%	14.9%	1.4%	1.2%
Bat Curtailment	0.0%	0.0%	0.1%	0.4%	0.1%	0.1%	0.2%	0.2%	0.3%	0.3%	0.0%	0.0%	0.0%	0.1%
E. Wind														
Forecasted WS (m/s)	8.2	8.2	8.2	8.2	8.2	7.9	7.8	7.6	7.4	8.4	9.3	8.7	8.8	8.2
Measured WS (m/s)	7.6	8	7.8	7.7	7.3	6.9	7	6.7	7.9	7.9	7.8	7.1	7.4	7.7
WindSpeed Deviation	-7.2%	-3.1%	-4.7%	-6.8%	-10.6%	-12.8%	-10.1%	-11.7%	6.3%	-5.6%	-16.5%	-18.5%	-15.9%	-6.2%


PLANT PRODUCTION

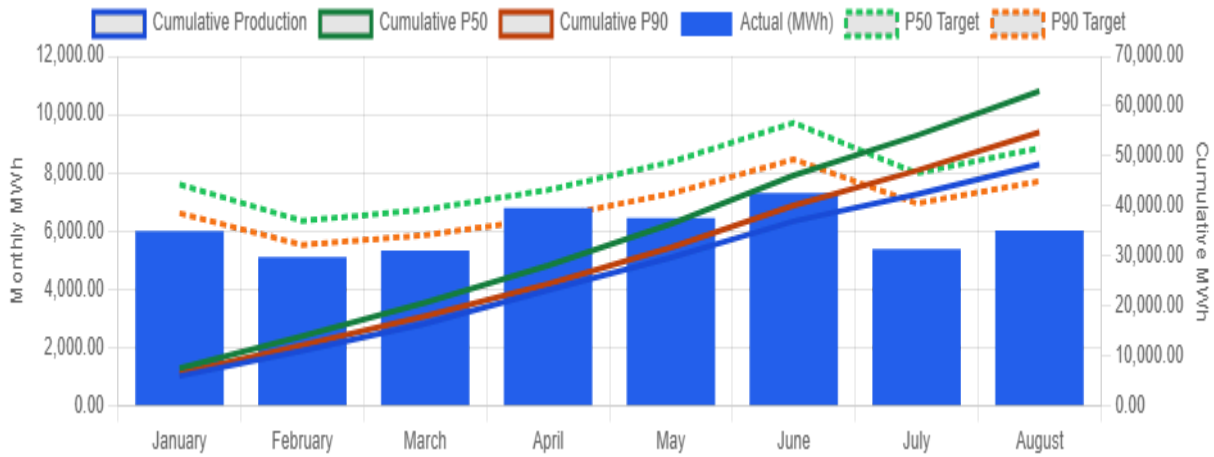


PLANT AVAILABILITY

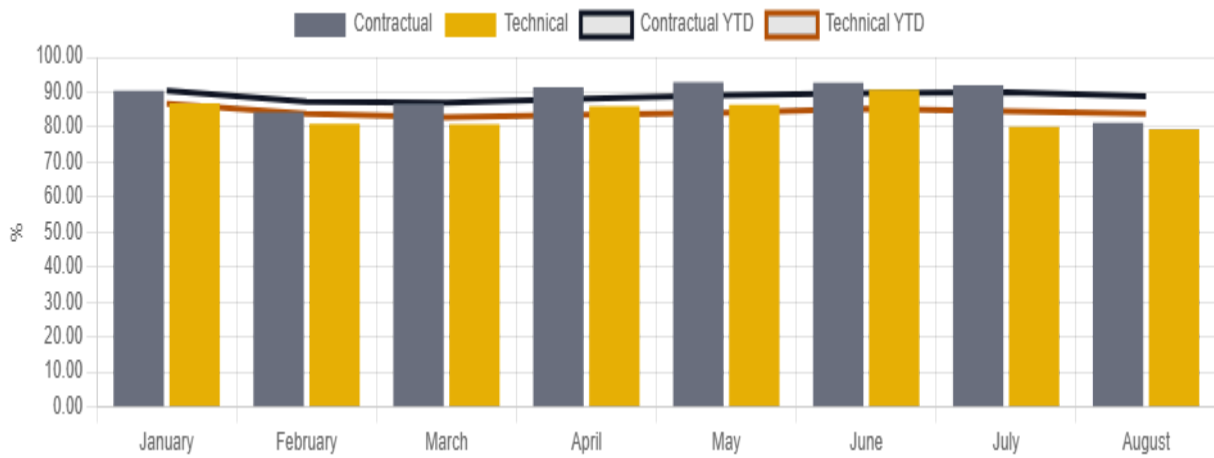

WIND SPEED

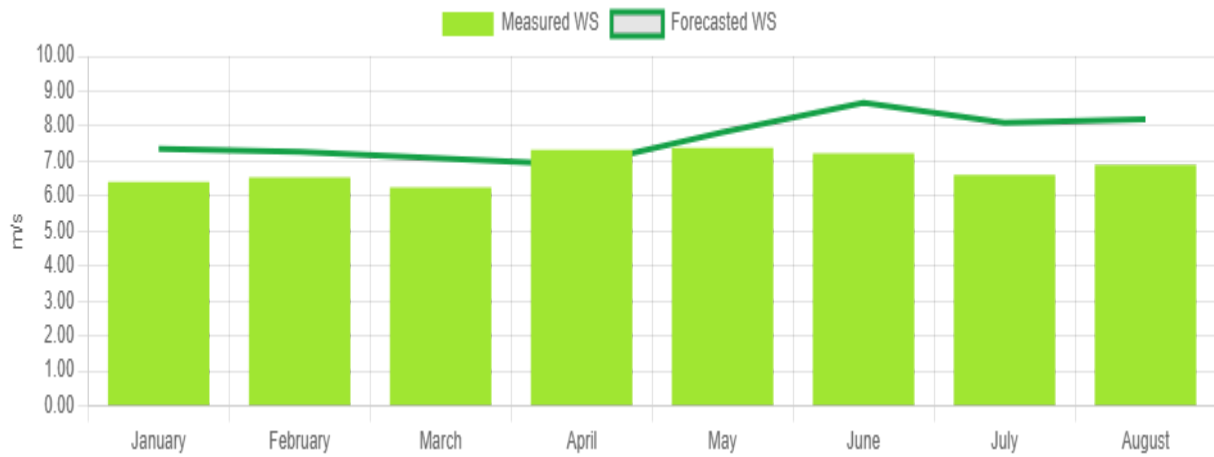

ANNUAL PRODUCTION AND AVAILABILITY PER WT

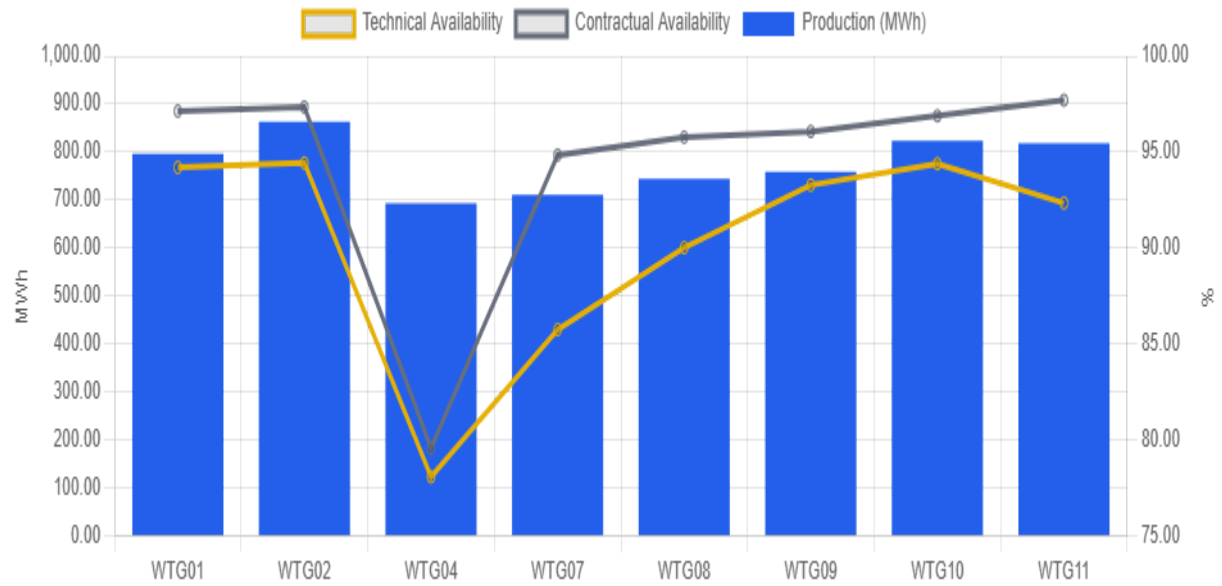

OPERATIONAL LOSS FACTORS

