


Dassiesridge: the plant produced 10.7 GWh, significantly below historical, P50 and P90 targets. Contractual availability averaged 99.2%, while technical availability was lower at 92.4%. The negative delta in production was visible in the wind resource deviation of -28%.


FULL KPI MATRIX

CATEGORY	2025	2026	JAN	FEB	MAR	APR	MAY	JUN	JUL	TOTAL
A. Production										
Measured (MWh)	14,944	87,229	14,780	11,841	10,471	15,782	12,522	11,098	10,735	102,173
Deviation Historical	-	-	-	-	-	-	-	-	-	-
Deviation P50	-	-27.1%	-14.9%	-20.1%	-36.5%	8.2%	-26.3%	-44.7%	-44.5%	-27.1%
Deviation P90	-	-16.3%	-2.2%	-8.2%	-27.1%	24.2%	-15.4%	-36.5%	-36.3%	-16.3%
Capacity Factor	29.5%	27.8%	32.1%	28.5%	22.9%	35.5%	27.3%	25.1%	23.5%	28.0%
Electrical Losses	-7.3%	2.2%	1.8%	2.1%	2.3%	2.1%	2.2%	2.4%	2.5%	1.0%
B. Consumption										
Measured (MWh)	70	443	68	39	43	42	85	94	72	513
Ratio to Production	0.5%	0.5%	0.5%	0.3%	0.4%	0.3%	0.7%	0.8%	0.7%	0.5%
C. Availability										
TBA - Contractual	98.4%	93.2%	98.3%	98.5%	98.1%	98.6%	92.9%	66.7%	99.2%	93.9%
TBA - Technical	95.1%	88.9%	93.7%	95.2%	94.7%	97.5%	80.7%	68.1%	92.4%	89.7%
PBA - Technical	97.9%	93.0%	98.1%	98.2%	98.4%	98.5%	92.7%	66.2%	99.0%	93.6%
D. OLF - Losses										
Manufacturer	2.6%	8.8%	4.6%	7.7%	3.2%	2.1%	6.4%	36.4%	1.0%	8.0%
Owner	0.0%	0.2%	0.0%	0.0%	0.0%	0.0%	1.4%	0.0%	0.2%	0.2%
Environmental	0.1%	0.1%	0.0%	0.1%	0.1%	0.1%	0.1%	0.0%	0.1%	0.1%
Utility	2.0%	2.2%	4.2%	2.1%	0.9%	0.3%	4.4%	0.2%	3.3%	2.2%
Bat Curtailment	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%
E. Wind										
Forecasted WS (m/s)	7.1	7.1	6.9	6.6	6.5	6.5	7.3	8.5	7.8	7.1
Measured WS (m/s)	6.6	6.4	6.6	6.3	5.6	6.7	6.9	7.2	5.6	6.4
WindSpeed Deviation	-5.9%	-9.6%	-3.7%	-4.8%	-14.1%	3.6%	-5.1%	-14.8%	-28.4%	-9.1%


PLANT PRODUCTION

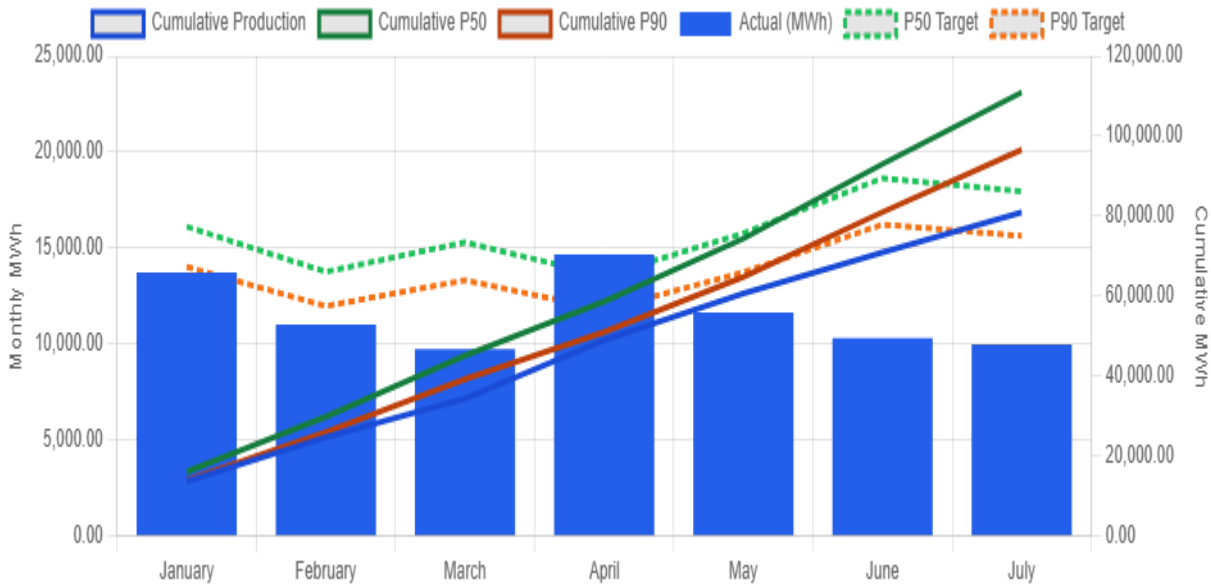


ANNUAL PRODUCTION AND AVAILABILITY PER WT

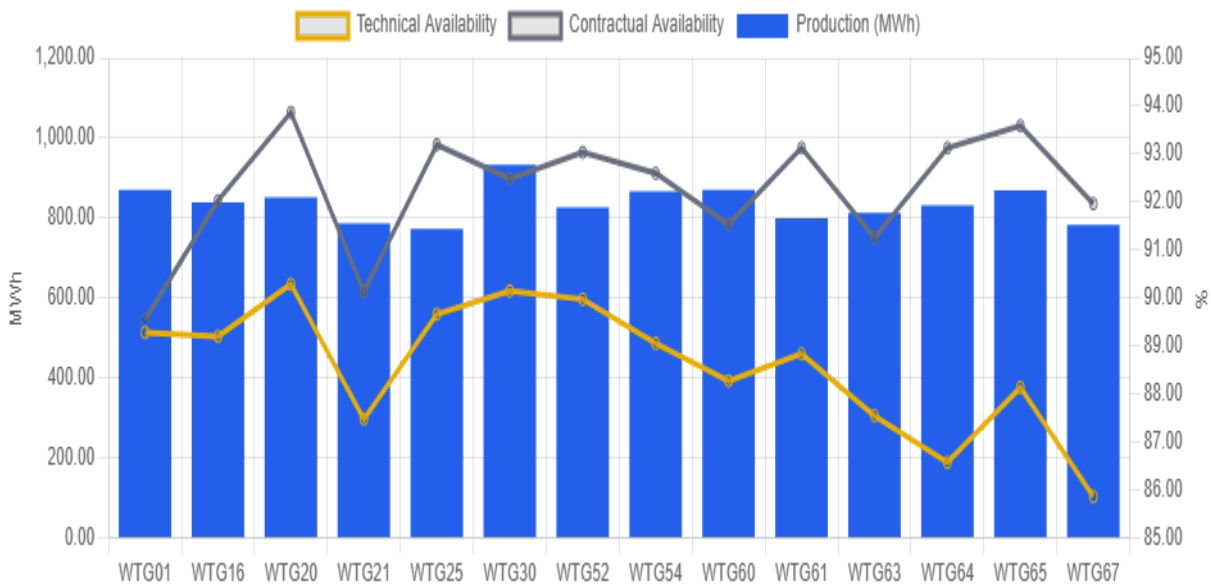

PLANT AVAILABILITY

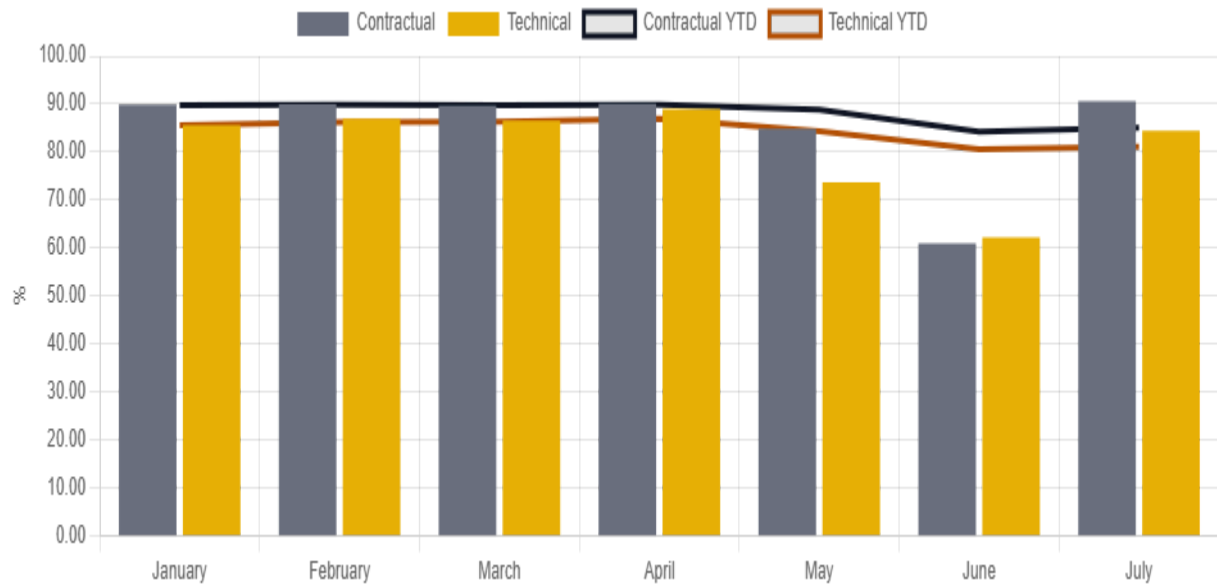

OPERATIONAL LOSS FACTORS

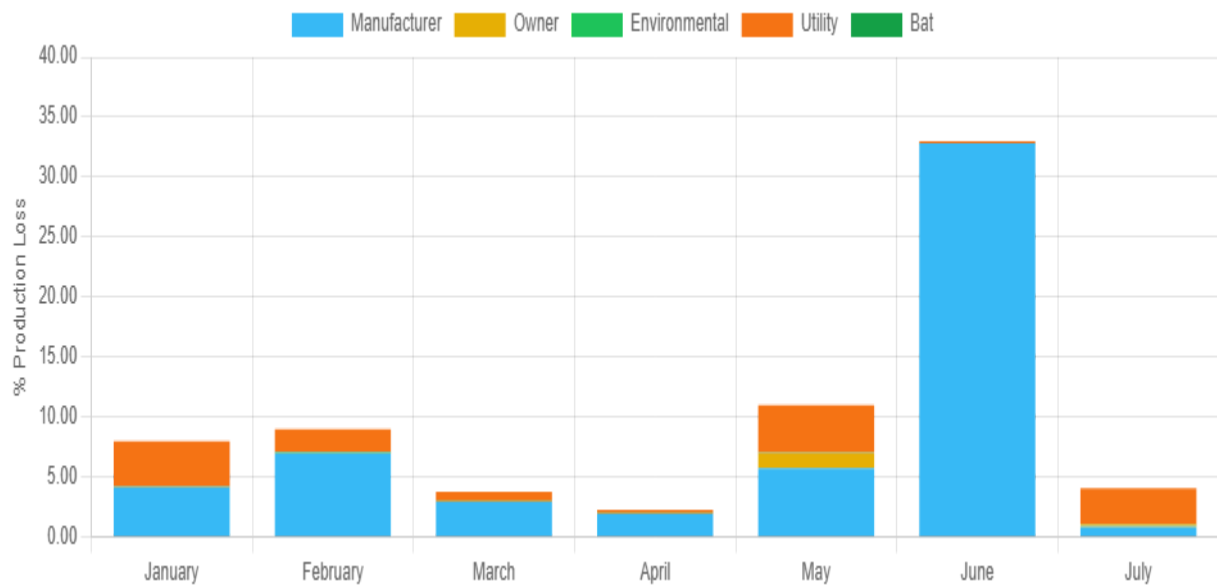

WIND SPEED

