


Chaba: the plant produced 4.7 GWh, significantly below historical, P50 and P90 targets. Contractual availability averaged 96.4%, while technical availability was 95.4%. The negative delta in production was visible in the wind resource deviation of -17%.


FULL KPI MATRIX

CATEGORY	2022	2023	2024	2025	2026	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	TOTAL
A. Production														
Measured (MWh)	56,701	60,160	59,270	55,978	33,162	3,776	3,414	3,876	5,080	4,516	4,295	3,485	4,719	265,271
Deviation Historical	–	6.1%	1.4%	-4.7%	-16.1%	3.7%	1.5%	-7.1%	22.3%	-8.8%	-33.4%	-49.9%	-19.2%	-2.2%
Deviation P50	-5.5%	0.3%	-4.8%	-17.1%	-28.1%	-8.4%	-8.1%	-18.0%	-2.3%	-23.1%	-43.7%	-54.7%	-34.1%	-10.4%
Deviation P90	4.2%	10.6%	8.9%	-5.2%	-17.8%	4.8%	5.1%	-6.3%	11.7%	-12.1%	-35.6%	-48.2%	-24.6%	1.0%
Capacity Factor	30.2%	32.1%	31.6%	28.9%	26.7%	23.9%	23.9%	24.5%	33.1%	28.6%	28.0%	22.1%	29.8%	30.2%
Electrical Losses	0.6%	0.8%	1.0%	-2.1%	1.2%	1.2%	1.2%	1.3%	1.1%	1.2%	1.2%	1.4%	1.1%	0.2%
B. Consumption														
Measured (MWh)	136	131	134	143	136	17	21	19	14	15	10	20	20	679
Ratio to Production	0.3%	0.3%	0.2%	0.3%	0.4%	0.5%	0.6%	0.5%	0.3%	0.3%	0.2%	0.6%	0.4%	0.3%
C. Availability														
TBA - Contractual	96.8%	97.2%	97.0%	97.2%	97.4%	97.7%	96.8%	97.1%	98.5%	96.8%	97.2%	98.9%	96.4%	97.1%
TBA - Technical	96.3%	96.9%	94.2%	94.0%	92.7%	93.1%	90.2%	91.5%	91.7%	88.5%	93.0%	98.2%	95.4%	95.0%
PBA - Technical	96.6%	97.3%	96.9%	95.2%	92.7%	96.7%	96.6%	94.9%	91.4%	88.5%	87.7%	94.4%	91.7%	96.0%
D. Losses Breakdown														
Grid	0.3%	0.3%	1.1%	1.4%	2.9%	1.0%	0.0%	1.4%	4.3%	4.5%	7.1%	2.4%	2.5%	1.4%
Breakdown	1.9%	1.6%	1.2%	1.6%	1.8%	0.8%	1.4%	1.0%	0.8%	4.4%	1.2%	0.4%	4.3%	1.6%
Maintenance	1.0%	0.8%	0.8%	0.9%	0.7%	1.0%	1.2%	1.4%	0.3%	0.1%	1.0%	0.4%	0.1%	0.9%
Partial Perf.	0.4%	0.3%	0.4%	0.4%	2.0%	–	–	0.8%	2.9%	1.7%	2.9%	2.2%	1.4%	0.7%
Environmental	0.0%	0.0%	0.0%	0.1%	0.1%	0.0%	–	–	–	0.1%	–	–	–	0.1%
Data Quality	–	0.1%	0.3%	–	–	–	–	–	–	–	–	–	–	0.3%
Requested Shutdown	0.1%	0.0%	0.0%	0.0%	0.0%	0.1%	0.0%	0.0%	–	0.1%	0.0%	–	0.0%	0.0%
BoP	0.0%	0.0%	0.0%	0.1%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.1%	0.1%
Bat	0.1%	0.1%	0.6%	2.0%	0.5%	0.4%	0.8%	0.5%	0.4%	0.7%	–	–	–	0.8%
E. Wind														
Forecasted WS (m/s)	7.2	7.2	7.2	7.2	7.2	6.5	6.5	6.6	6.7	7.5	8.1	7.9	8	7.2
Measured WS (m/s)	6.4	6.6	6.6	6.5	6.2	5.8	5.8	5.9	6.9	6.9	6.5	5.6	6.6	6.5
WindSpeed Deviation	-11.3%	-8.6%	-8.0%	-10.1%	-13.0%	-11.3%	-11.0%	-10.4%	3.3%	-7.9%	-19.9%	-29.6%	-17.5%	-10.0%


PLANT PRODUCTION

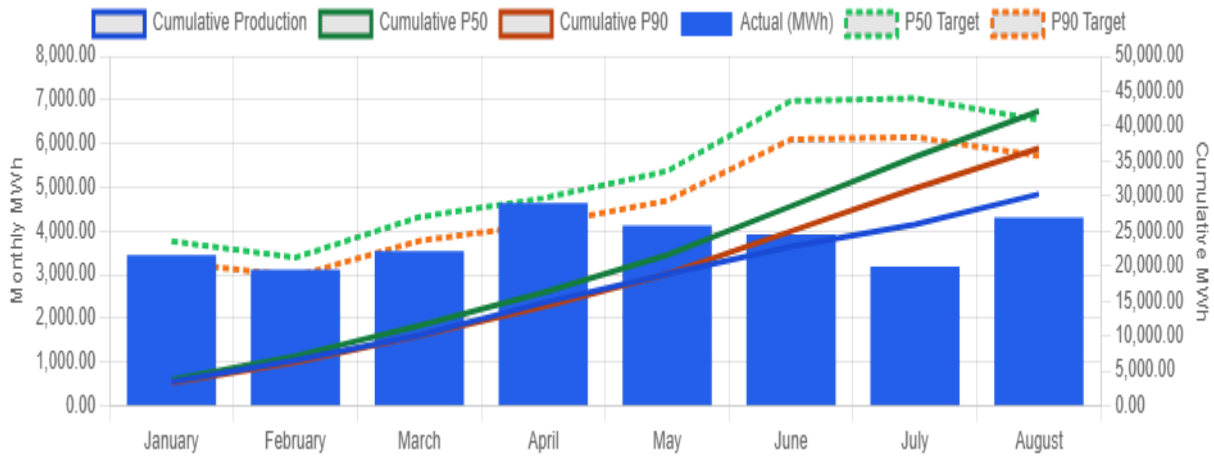


PLANT AVAILABILITY

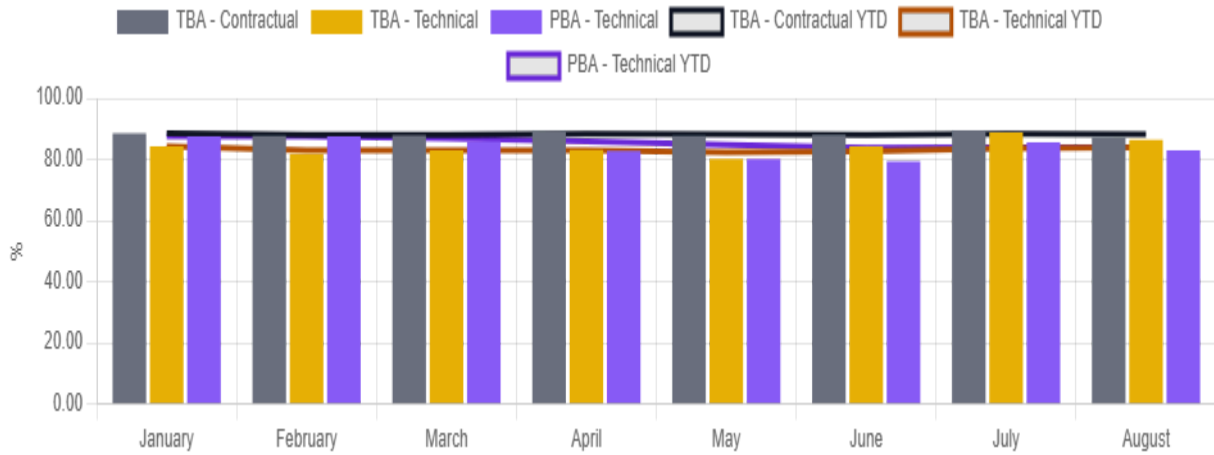

WIND SPEED

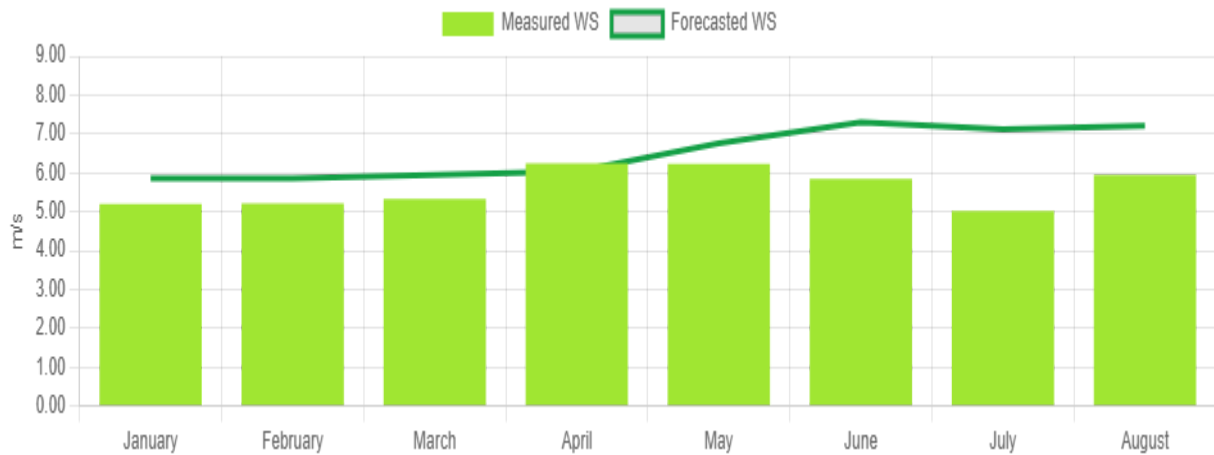

ANNUAL PRODUCTION AND AVAILABILITY PER WT

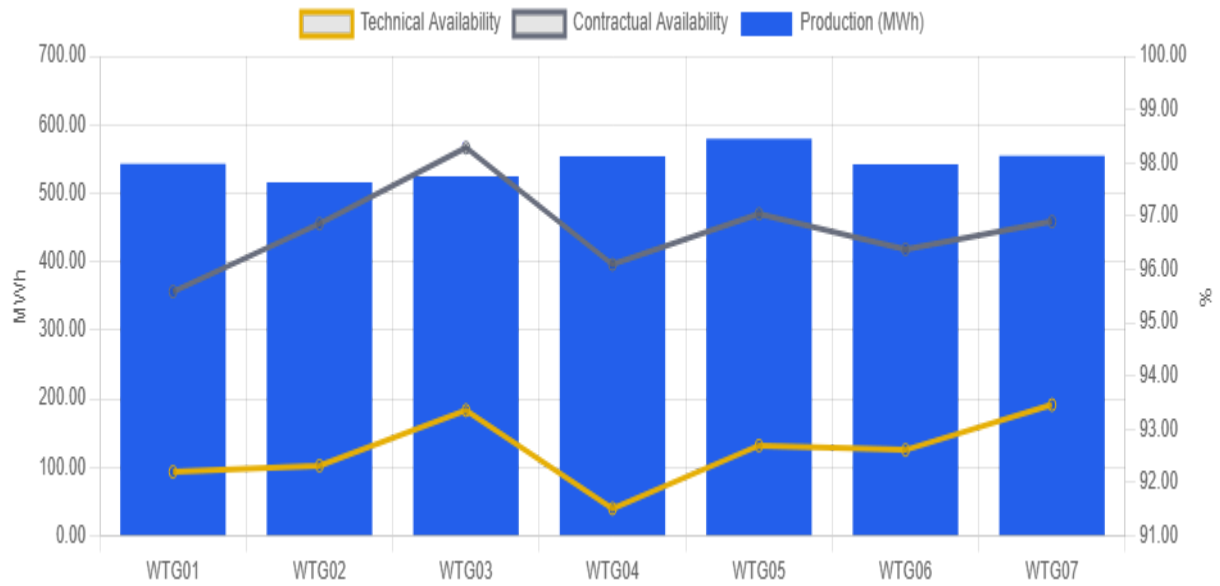

LOSSES BREAKDOWN

