


**Grassridge:** the plant produced 9.7 GWh, significantly below historical, P50 and P90 targets. Contractual availability averaged 98.2%, while technical availability was lower at 92.4%. The negative delta in production was visible in the wind resource deviation of -17%.


FULL KPI MATRIX

| CATEGORY             | 2022    | 2023    | 2024    | 2025    | 2026   | JAN    | FEB    | MAR    | APR    | MAY    | JUN    | JUL    | AUG    | TOTAL   |
|----------------------|---------|---------|---------|---------|--------|--------|--------|--------|--------|--------|--------|--------|--------|---------|
| A. Production        |         |         |         |         |        |        |        |        |        |        |        |        |        |         |
| Measured (MWh)       | 162,374 | 171,642 | 160,007 | 160,758 | 84,977 | 13,718 | 11,001 | 8,118  | 11,322 | 11,569 | 11,549 | 7,994  | 9,708  | 739,758 |
| Deviation Historical | –       | 5.7%    | -4.2%   | -2.4%   | -21.9% | 11.2%  | -4.4%  | -31.6% | 5.2%   | -2.3%  | -36.3% | -54.1% | -34.9% | -4.2%   |
| Deviation P50        | -7.4%   | -10.2%  | -16.3%  | -15.9%  | -31.5% | 17.7%  | -20.0% | -43.4% | -12.9% | -21.4% | -38.3% | -59.0% | -47.1% | -15.2%  |
| Deviation P90        | -2.7%   | 2.9%    | -4.1%   | -3.6%   | -21.5% | 34.8%  | -8.4%  | -35.1% | -0.2%  | -9.9%  | -29.4% | -53.0% | -39.4% | -4.6%   |
| Capacity Factor      | 29.2%   | 30.7%   | 28.4%   | 28.6%   | 23.0%  | 29.0%  | 25.8%  | 17.3%  | 24.7%  | 24.6%  | 25.3%  | 17.0%  | 20.6%  | 28.3%   |
| Electrical Losses    | 1.6%    | 1.2%    | 0.6%    | 0.4%    | 1.7%   | 1.5%   | 1.6%   | 2.0%   | 1.4%   | 2.0%   | 1.6%   | 1.8%   | 1.7%   | 1.1%    |
| B. Consumption       |         |         |         |         |        |        |        |        |        |        |        |        |        |         |
| Measured (MWh)       | 565     | 585     | 584     | 653     | 522    | 57     | 65     | 86     | 60     | 54     | 39     | 95     | 65     | 2,910   |
| Ratio to Production  | 0.4%    | 0.4%    | 0.4%    | 0.4%    | 0.7%   | 0.4%   | 0.6%   | 1.1%   | 0.5%   | 0.5%   | 0.3%   | 1.2%   | 0.7%   | 0.4%    |
| C. Availability      |         |         |         |         |        |        |        |        |        |        |        |        |        |         |
| TBA - Contractual    | 97.0%   | 95.5%   | 94.9%   | 97.0%   | 97.2%  | 98.1%  | 96.2%  | 97.3%  | 96.4%  | 96.4%  | 98.7%  | 96.2%  | 98.2%  | 96.3%   |
| TBA - Technical      | 96.6%   | 95.7%   | 90.2%   | 92.6%   | 89.0%  | 98.1%  | 90.7%  | 87.9%  | 80.9%  | 82.8%  | 90.8%  | 88.5%  | 92.4%  | 93.1%   |
| PBA - Technical      | 96.5%   | 95.4%   | 93.6%   | 93.6%   | 83.5%  | 97.7%  | 95.4%  | 82.4%  | 79.0%  | 82.2%  | 75.1%  | 79.3%  | 77.2%  | 93.2%   |
| D. Losses Breakdown  |         |         |         |         |        |        |        |        |        |        |        |        |        |         |
| Grid                 | 0.6%    | 0.4%    | 2.4%    | 2.8%    | 13.2%  | 0.0%   | 0.0%   | 13.7%  | 17.2%  | 12.3%  | 23.6%  | 17.6%  | 20.9%  | 4.3%    |
| Breakdown            | 1.7%    | 2.5%    | 3.1%    | 1.5%    | 1.8%   | 1.3%   | 1.1%   | 1.5%   | 1.5%   | 3.9%   | 1.1%   | 2.9%   | 1.4%   | 2.1%    |
| Maintenance          | 0.8%    | 1.5%    | 1.5%    | 0.9%    | 0.6%   | 0.5%   | 0.7%   | 0.7%   | 1.3%   | 0.6%   | 0.2%   | 0.2%   | 0.5%   | 1.1%    |
| Partial Perf.        | 0.4%    | 0.3%    | 0.4%    | 0.2%    | 0.1%   | 0.2%   | 0.2%   | 0.1%   | 0.1%   | 0.3%   | 0.0%   | 0.0%   | 0.1%   | 0.3%    |
| Environmental        | 0.0%    | 0.0%    | 0.1%    | 0.0%    | 0.1%   | 0.3%   | 0.1%   | 0.0%   | 0.0%   | 0.1%   | –      | –      | 0.0%   | 0.0%    |
| Data Quality         | 0.1%    | 0.0%    | –       | 0.2%    | 0.1%   | –      | –      | –      | –      | –      | –      | 0.2%   | 0.0%   | 0.1%    |
| Requested Shutdown   | 0.0%    | 0.1%    | 0.0%    | 0.1%    | 0.5%   | 0.0%   | 2.1%   | 0.9%   | –      | 0.0%   | –      | 0.1%   | 0.0%   | 0.1%    |
| BoP                  | 0.0%    | 0.0%    | 0.0%    | 0.0%    | 0.0%   | –      | –      | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%   | 0.0%    |
| Bat                  | 0.3%    | –       | 2.8%    | 2.9%    | 0.6%   | –      | 0.4%   | 0.6%   | 0.8%   | 0.8%   | –      | –      | –      | 1.8%    |
| MCR                  | –       | –       | –       | 0.4%    | –      | –      | –      | –      | –      | –      | –      | –      | –      | 0.4%    |
| E. Wind              |         |         |         |         |        |        |        |        |        |        |        |        |        |         |
| Forecasted WS (m/s)  | 6.7     | 6.7     | 6.7     | 6.7     | 6.7    | 6.5    | 6.6    | 6.2    | 6      | 6.8    | 7.3    | 7.2    | 7      | 6.7     |
| Measured WS (m/s)    | 6.3     | 6.5     | 6.4     | 6.3     | 5.9    | 6.2    | 5.8    | 5.3    | 6.2    | 6.5    | 6.5    | 5.2    | 5.8    | 6.3     |
| WindSpeed Deviation  | -6.6%   | -3.1%   | -5.0%   | -6.4%   | -11.3% | -5.3%  | -12.0% | -15.3% | 3.0%   | -4.9%  | -10.6% | -28.0% | -17.2% | -6.1%   |


PLANT PRODUCTION

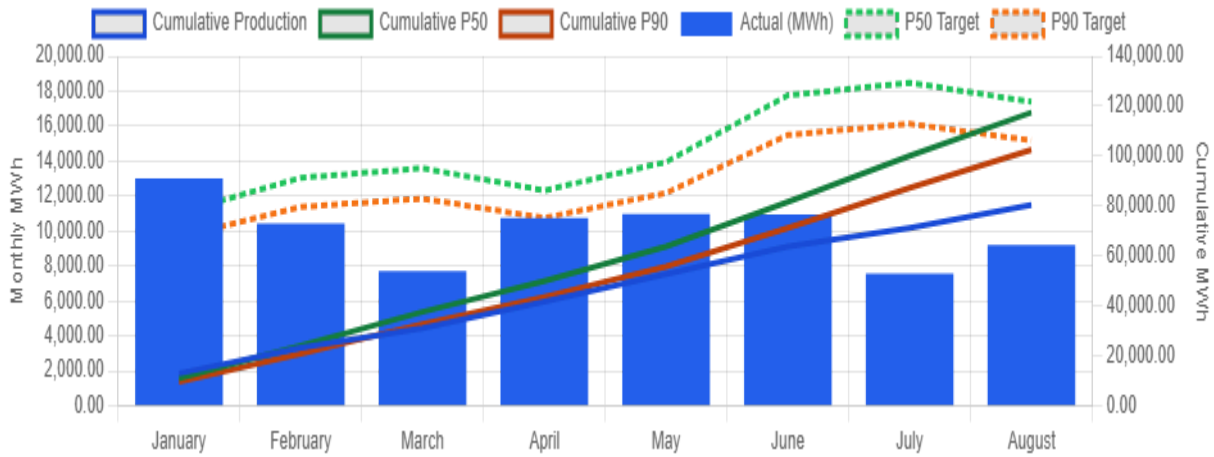


PLANT AVAILABILITY

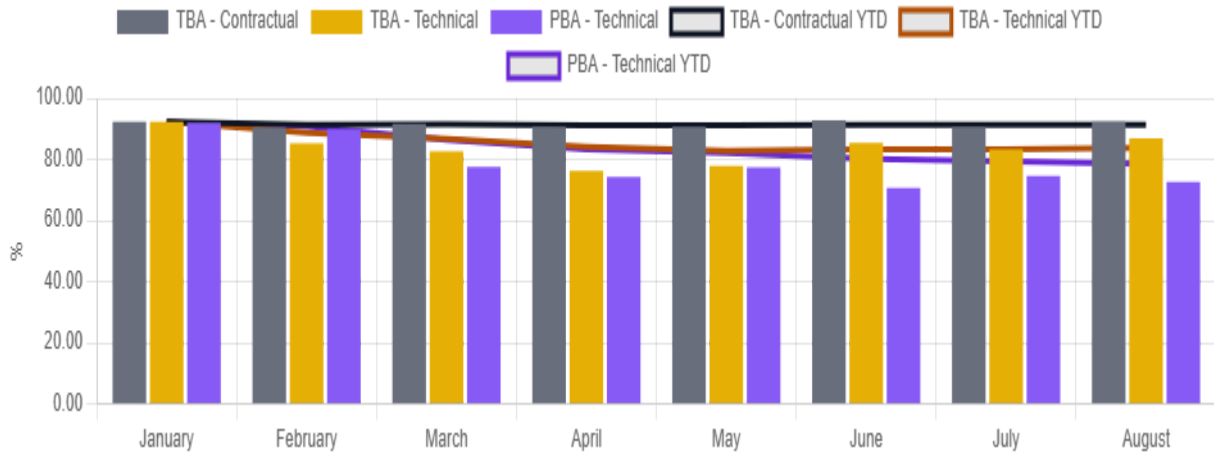

WIND SPEED

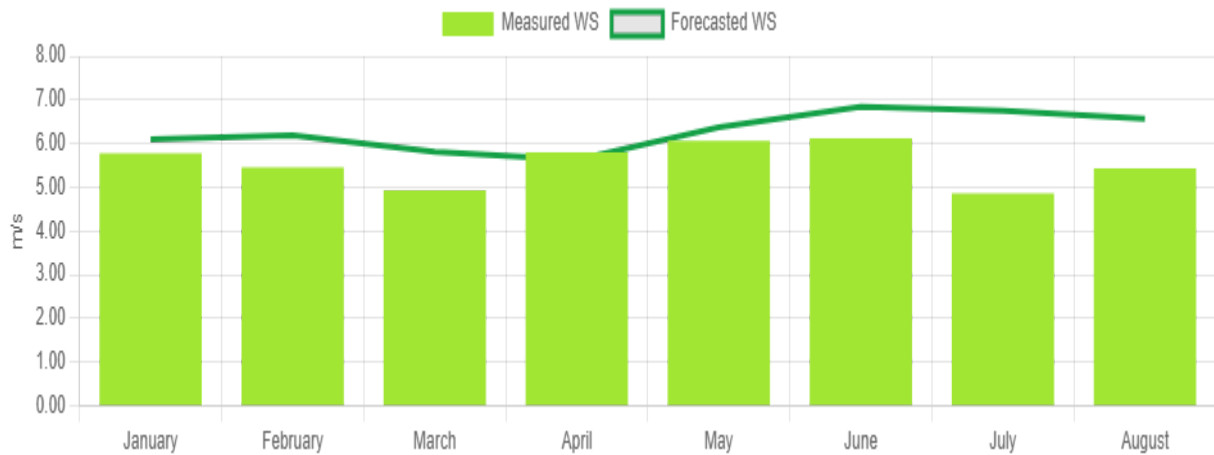

## ANNUAL PRODUCTION AND AVAILABILITY PER WT

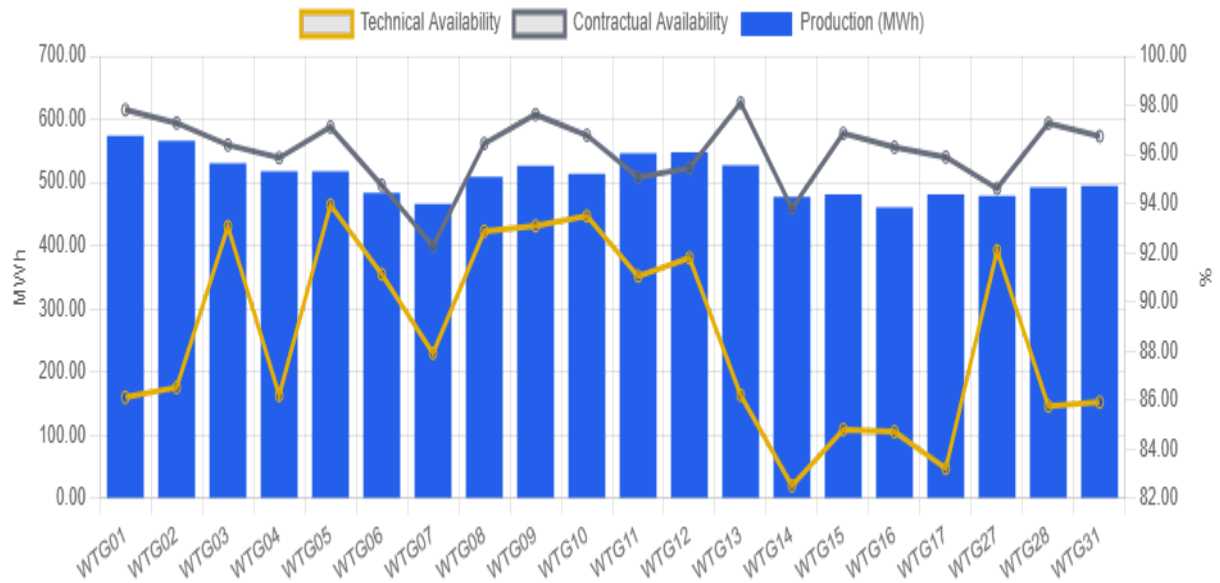

## LOSSES BREAKDOWN

