


Coleskop: the plant produced 38.7 GWh, significantly below historical, P50 and P90 targets. Contractual availability averaged 99.4%, while technical availability was lower at 96.0%. Losses were dominated by grid curtailments (recoverable losses).


FULL KPI MATRIX

CATEGORY	2026	FEB	MAR	APR	MAY	JUN	JUL	TOTAL
A. Production								
Measured (MWh)	197,370	8,096	36,822	44,460	33,537	35,741	38,713	197,370
Deviation Historical	–	–	–	–	–	–	–	–
Deviation P50	-31.0%	-33.2%	-22.6%	-6.6%	-40.1%	-40.9%	-37.9%	-31.0%
Deviation P90	-22.2%	-24.7%	-12.7%	5.4%	-32.4%	-33.3%	-30.0%	-22.2%
Capacity Factor	31.1%	8.1%	34.3%	42.4%	31.1%	34.4%	36.2%	31.1%
Electrical Losses	0.3%	-1.8%	0.9%	-0.1%	0.5%	0.9%	1.4%	0.3%
B. Consumption								
Measured (MWh)	78	0	28	9	12	29	0	78
Ratio to Production	0.0%	0.0%	0.1%	0.0%	0.0%	0.1%	0.0%	0.0%
C. Availability								
TBA - Contractual	99.0%	96.7%	99.8%	99.3%	99.7%	99.4%	99.4%	99.0%
TBA - Technical	96.0%	95.0%	95.5%	95.6%	97.2%	96.5%	96.0%	96.0%
PBA - Technical	96.7%	88.2%	98.8%	98.4%	97.6%	98.9%	98.6%	96.7%
D. OLF - Losses								
Manufacturer	6.4%	10.8%	3.2%	4.1%	10.7%	5.4%	4.5%	6.4%
Owner	0.5%	0.3%	0.7%	0.8%	0.2%	0.2%	0.9%	0.5%
Environmental	1.0%	0.8%	0.4%	2.0%	0.8%	1.0%	1.2%	1.0%
Utility	13.0%	0.2%	5.5%	9.1%	25.1%	20.7%	17.3%	13.0%
Bat Curtailment	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%
E. Wind								
Forecasted WS (m/s)	8	7.5	7.5	7.5	8.1	8.7	8.5	8
Measured WS (m/s)	7.9	6.9	7.1	8.6	8.9	8	7.8	7.9
WindSpeed Deviation	-0.8%	-9.0%	-4.6%	14.2%	10.1%	-7.8%	-7.6%	-0.8%


PLANT PRODUCTION

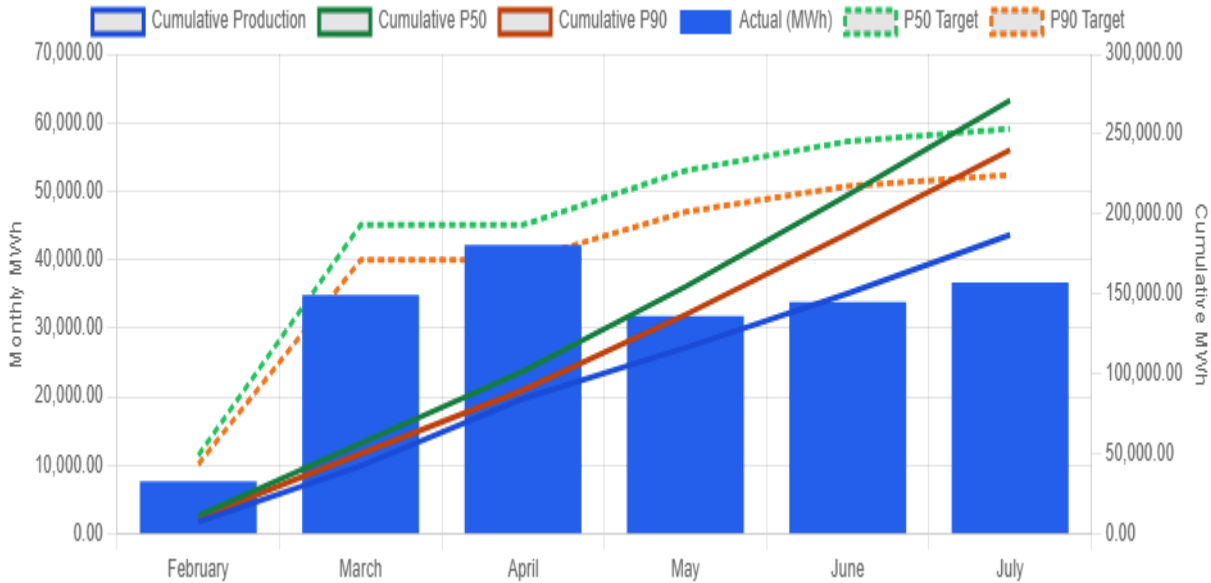


ANNUAL PRODUCTION AND AVAILABILITY PER WT

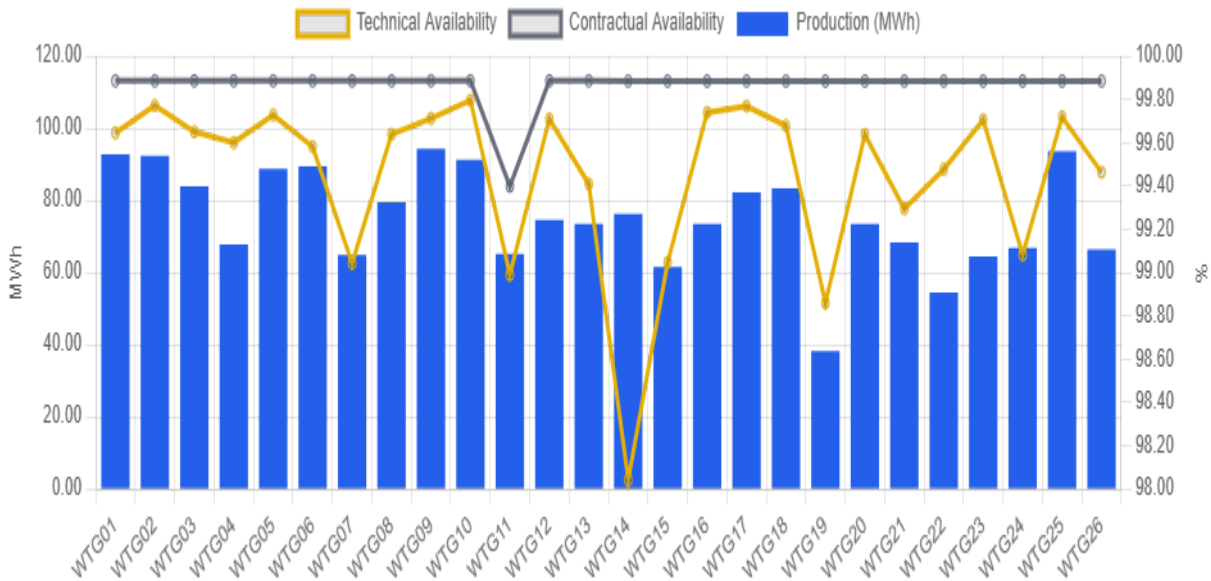


PLANT AVAILABILITY

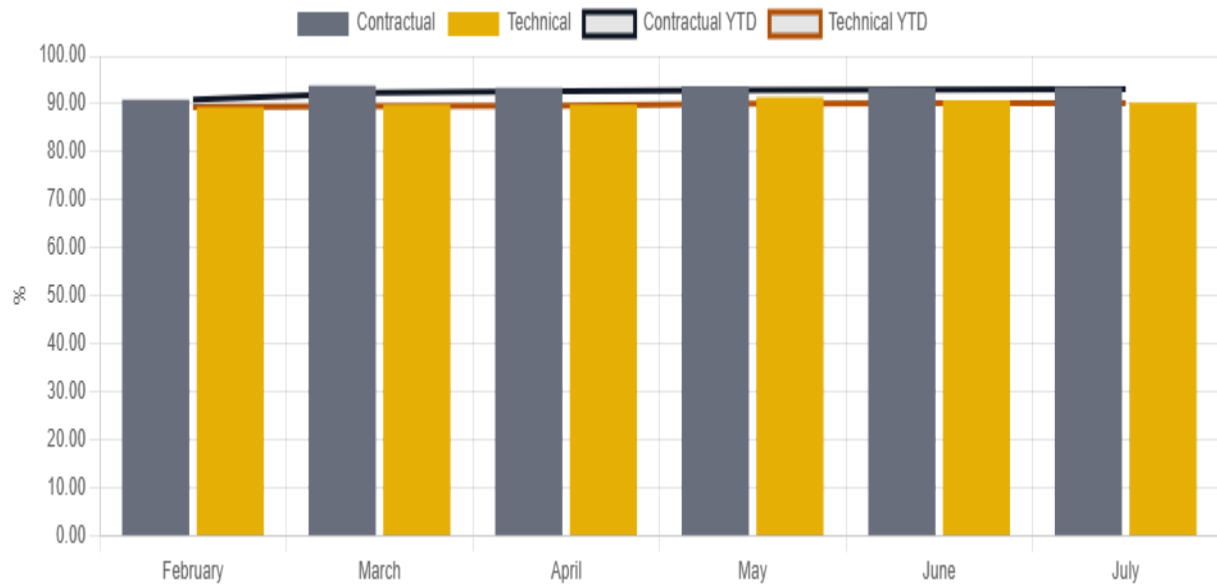

OPERATIONAL LOSS FACTORS

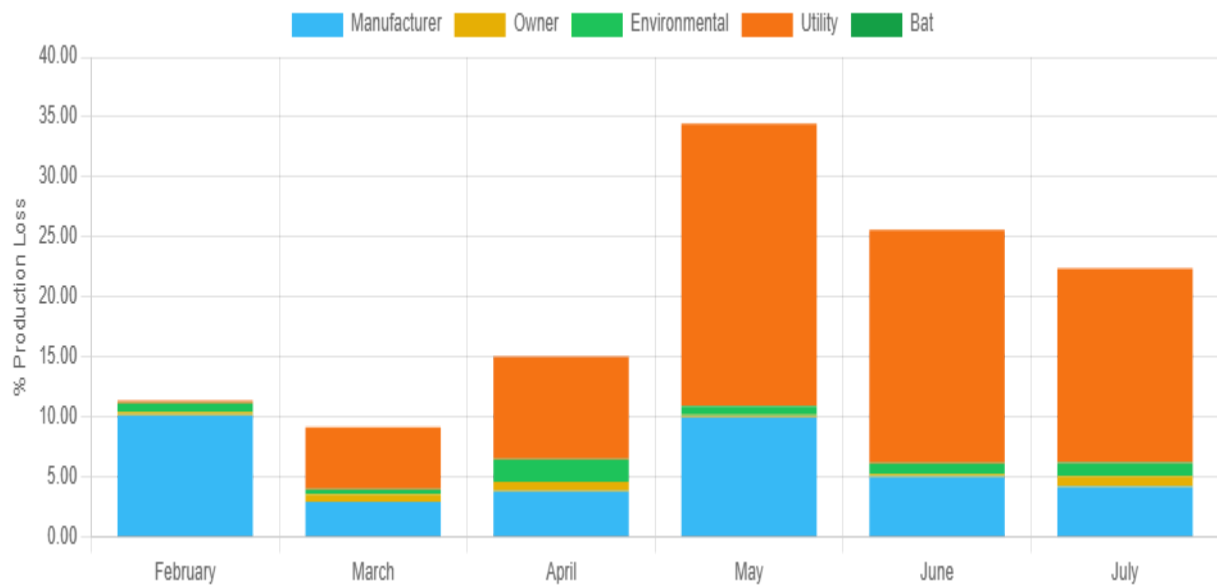

WIND SPEED

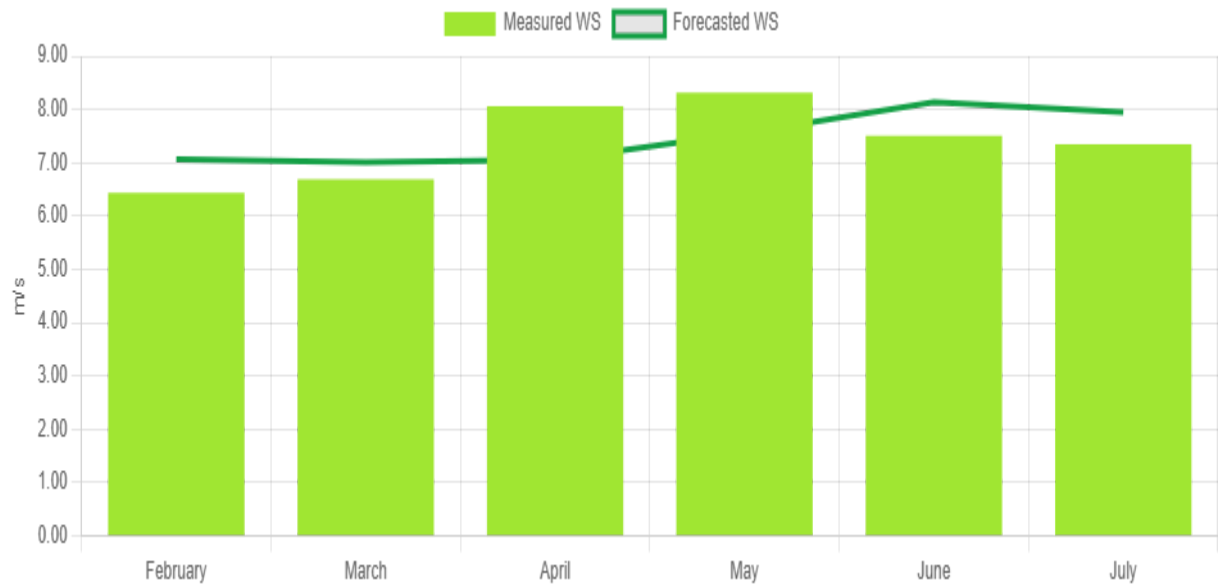

Plant Analysis Reports · Coleskop · Full history table, 2026 dashboard · Source: P&O_Custom_Semantic_Model (PowerBI)
