

Phezukomoya

PHEZ · 145.6 MW installed


Full History

Phezukomoya: the plant produced 35.0 GWh, significantly below historical, P50 and P90 targets. Contractual availability averaged 99.5%, while technical availability was lower at 94.2%. Losses were dominated by grid curtailments (recoverable losses).


FULL KPI MATRIX

CATEGORY	2026	FEB	MAR	APR	MAY	JUN	JUL	TOTAL
A. Production								
Measured (MWh)	203,288	31,758	34,015	41,027	29,164	32,348	34,975	203,288
Deviation Historical	–	–	–	–	–	–	–	–
Deviation P50	-33.8%	-18.7%	-29.5%	-13.8%	-46.7%	-44.7%	-40.9%	-33.8%
Deviation P90	-26.7%	-9.9%	-21.9%	-4.5%	-40.9%	-38.8%	-34.5%	-26.7%
Capacity Factor	32.6%	32.8%	31.9%	39.7%	27.3%	31.3%	32.8%	32.6%
Electrical Losses	1.4%	1.2%	1.5%	1.5%	1.3%	1.4%	1.4%	1.4%
B. Consumption								
Measured (MWh)	138	38	15	15	14	31	25	138
Ratio to Production	0.1%	0.1%	0.0%	0.0%	0.0%	0.1%	0.1%	0.1%
C. Availability								
TBA - Contractual	99.8%	–	100.0%	100.0%	99.8%	99.9%	99.5%	99.8%
TBA - Technical	97.3%	97.3%	99.1%	98.7%	97.1%	97.3%	94.2%	97.3%
PBA - Technical	97.7%	94.5%	98.8%	97.9%	96.5%	99.0%	99.4%	97.7%
D. OLF - Losses								
Manufacturer	13.2%	5.9%	5.2%	14.0%	33.5%	15.0%	5.3%	13.2%
Owner	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.2%	0.0%
Environmental	1.3%	0.0%	0.0%	1.1%	3.7%	1.2%	1.9%	1.3%
Utility	4.5%	0.0%	0.0%	0.1%	0.3%	9.6%	17.0%	4.5%
Bat Curtailment	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%
E. Wind								
Forecasted WS (m/s)	8.5	8	8	8	8.7	9.3	9.1	8.5
Measured WS (m/s)	7.5	7.3	6.8	8	8.1	7.4	7.4	7.5
WindSpeed Deviation	-11.4%	-8.3%	-15.1%	0.4%	-6.2%	-20.6%	-18.4%	-11.4%


PLANT PRODUCTION

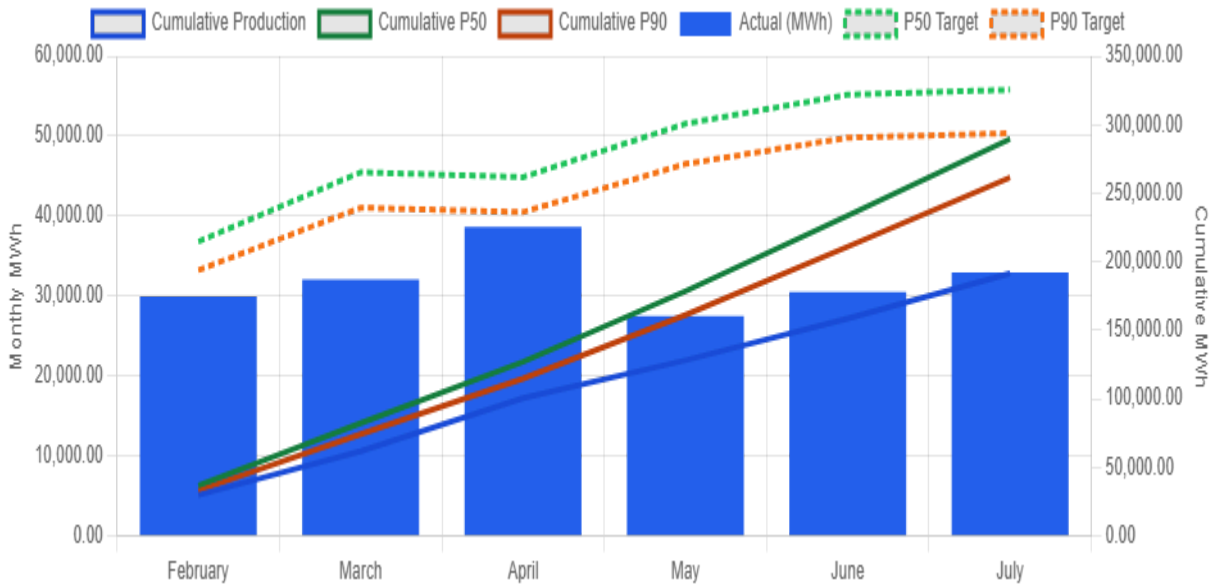


ANNUAL PRODUCTION AND AVAILABILITY PER WT

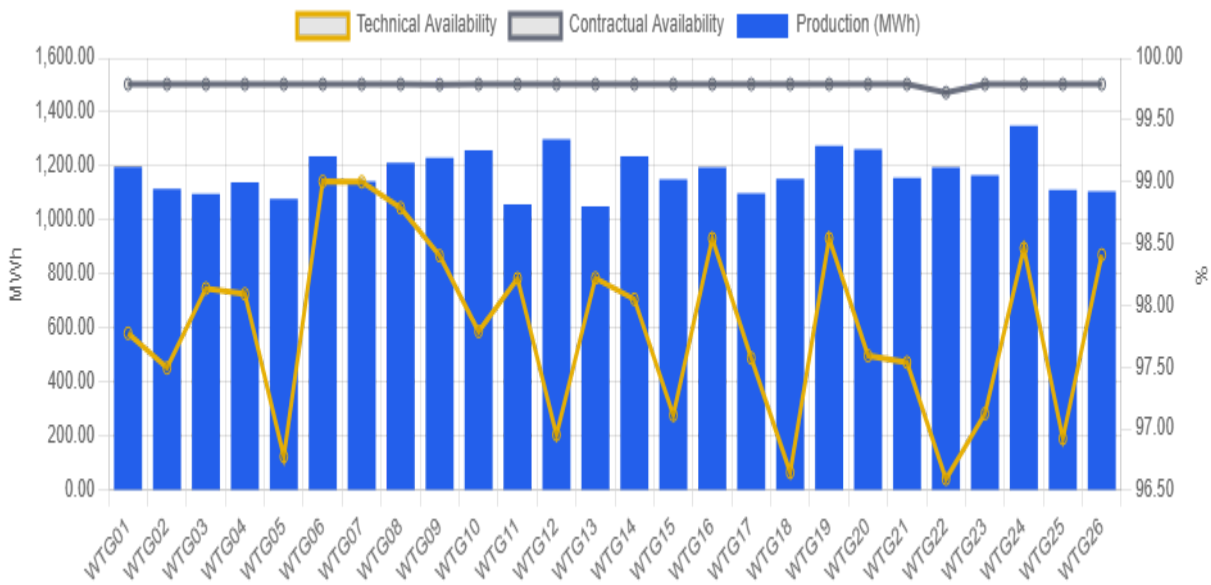

PLANT AVAILABILITY

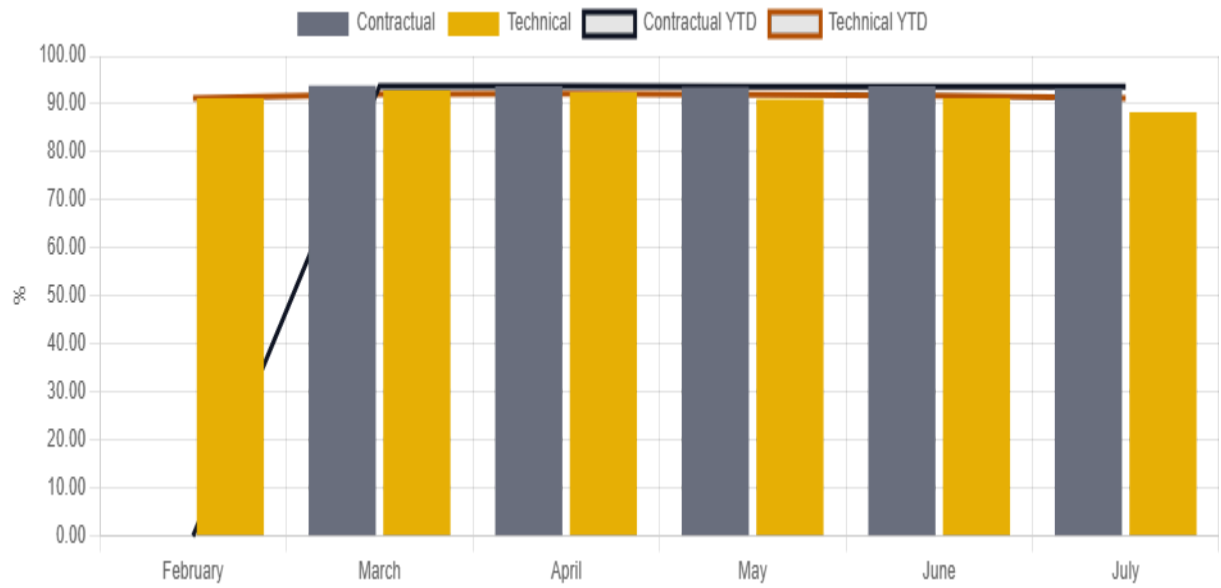

OPERATIONAL LOSS FACTORS

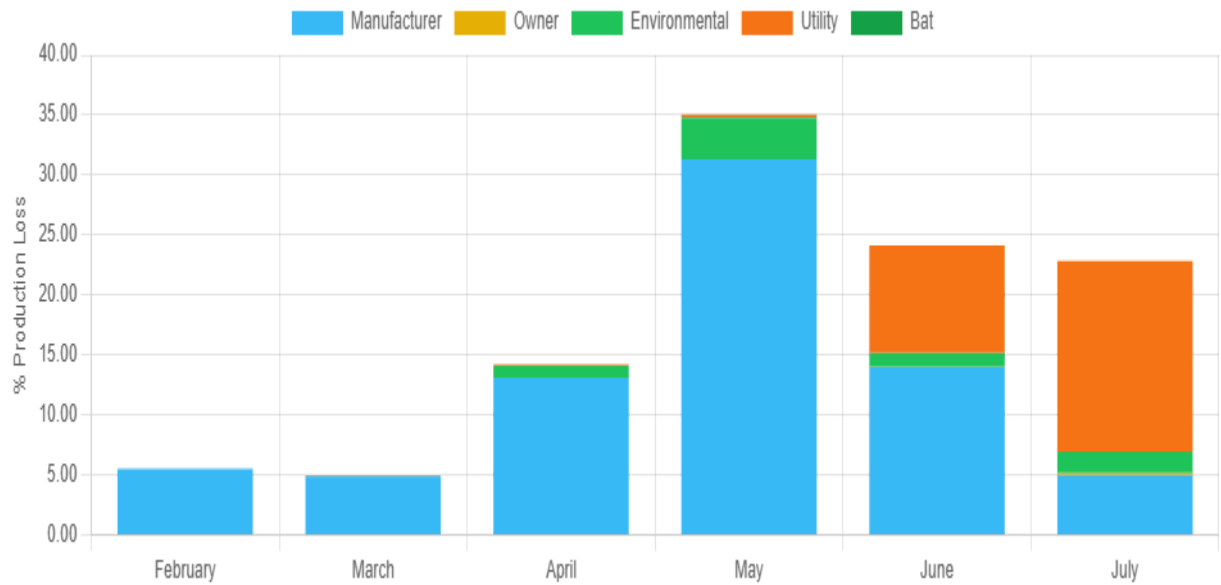

WIND SPEED

