


San Kraal: the plant produced 37.4 GWh, significantly below historical, P50 and P90 targets. Contractual availability averaged 99.5%, while technical availability was lower at 95.6%. Losses were dominated by grid curtailments (recoverable losses).


FULL KPI MATRIX

CATEGORY	2025	2026	JAN	FEB	MAR	APR	MAY	JUN	JUL	TOTAL
A. Production										
Measured (MWh)	35,374	274,172	49,138	36,763	35,552	46,951	31,244	37,114	37,409	309,546
Deviation Historical	–	–	–	–	–	–	–	–	–	–
Deviation P50	4.6%	-20.9%	7.8%	-6.8%	-18.7%	5.9%	-41.7%	-37.2%	-38.7%	-18.7%
Deviation P90	17.2%	-11.4%	20.8%	4.5%	-8.9%	18.6%	-34.7%	-29.7%	-31.3%	-8.9%
Capacity Factor	33.1%	37.5%	46.0%	38.1%	33.3%	45.5%	29.0%	35.7%	35.0%	37.0%
Electrical Losses	1.4%	1.2%	1.5%	1.4%	1.5%	1.6%	0.7%	0.9%	1.2%	1.3%
B. Consumption										
Measured (MWh)	0	189	28	26	34	16	16	42	27	189
Ratio to Production	0.0%	0.1%	0.1%	0.1%	0.1%	0.0%	0.1%	0.1%	0.1%	0.1%
C. Availability										
TBA - Contractual	98.9%	98.1%	99.8%	98.2%	99.4%	97.1%	94.0%	98.7%	99.5%	98.2%
TBA - Technical	95.8%	94.8%	97.8%	94.4%	94.5%	94.8%	90.6%	95.7%	95.6%	94.9%
PBA - Technical	97.9%	97.2%	99.3%	97.1%	98.8%	96.1%	91.7%	98.4%	99.4%	97.3%
D. OLF - Losses										
Manufacturer	1.6%	1.8%	0.8%	2.7%	1.1%	2.2%	3.6%	1.4%	0.6%	1.8%
Owner	0.3%	0.6%	0.1%	0.4%	0.5%	0.3%	1.9%	0.3%	0.6%	0.6%
Environmental	0.7%	0.3%	0.1%	0.6%	0.4%	0.2%	0.6%	0.1%	0.1%	0.4%
Utility	0.3%	10.9%	0.0%	0.3%	0.8%	3.6%	32.0%	17.6%	21.8%	9.6%
Bat Curtailment	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%	0.0%
E. Wind										
Forecasted WS (m/s)	8.4	8.5	8.1	7.8	7.9	8.1	8.9	9.6	9.4	8.5
Measured WS (m/s)	8.3	7.7	8	7.3	6.8	8.3	8.5	7.7	7.6	7.8
WindSpeed Deviation	-1.6%	-8.9%	-0.7%	-5.7%	-14.1%	2.0%	-4.4%	-20.3%	-19.3%	-8.0%


PLANT PRODUCTION

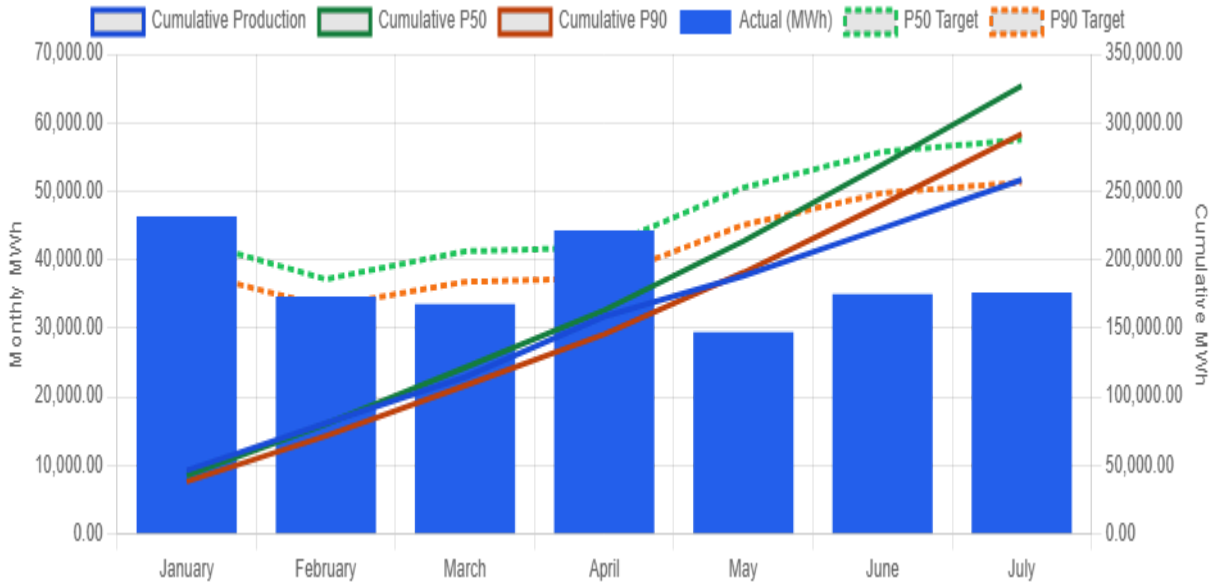


ANNUAL PRODUCTION AND AVAILABILITY PER WT

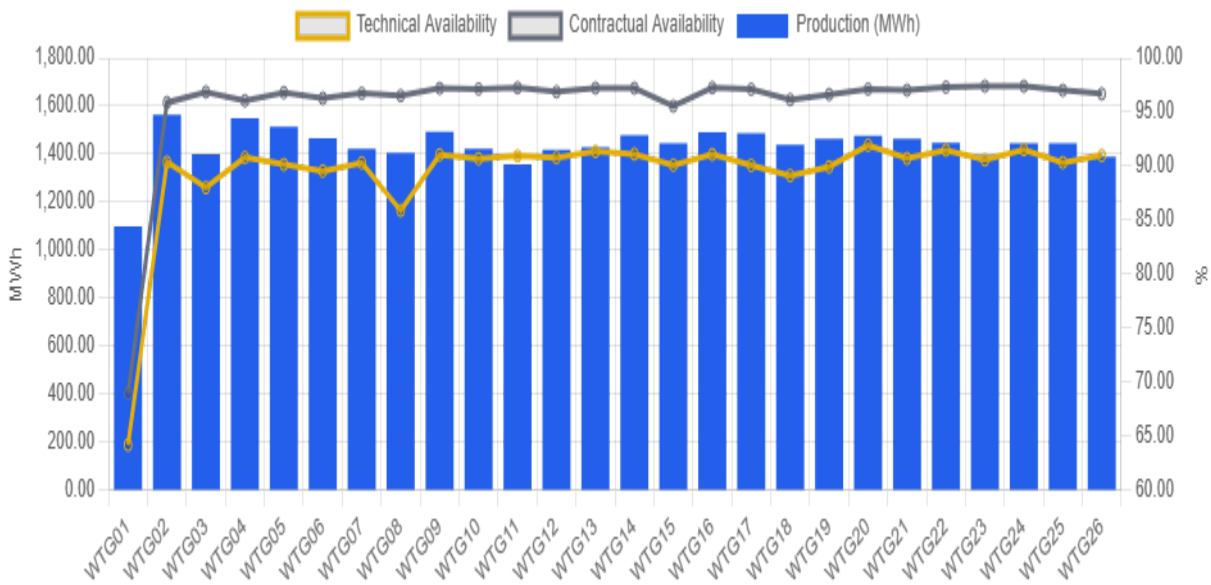

PLANT AVAILABILITY

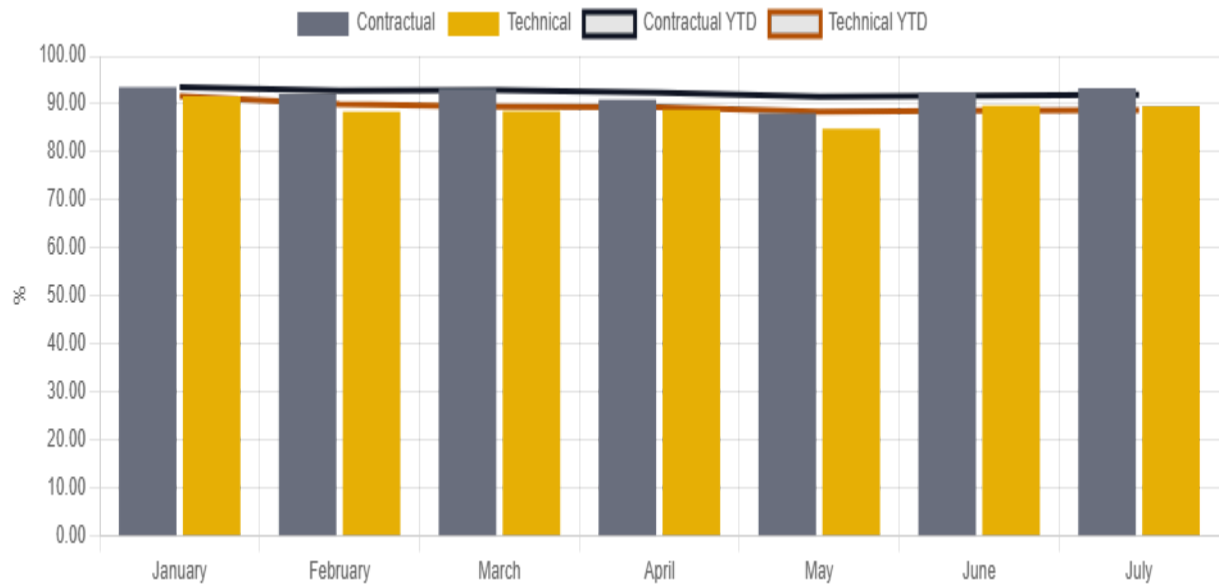

OPERATIONAL LOSS FACTORS

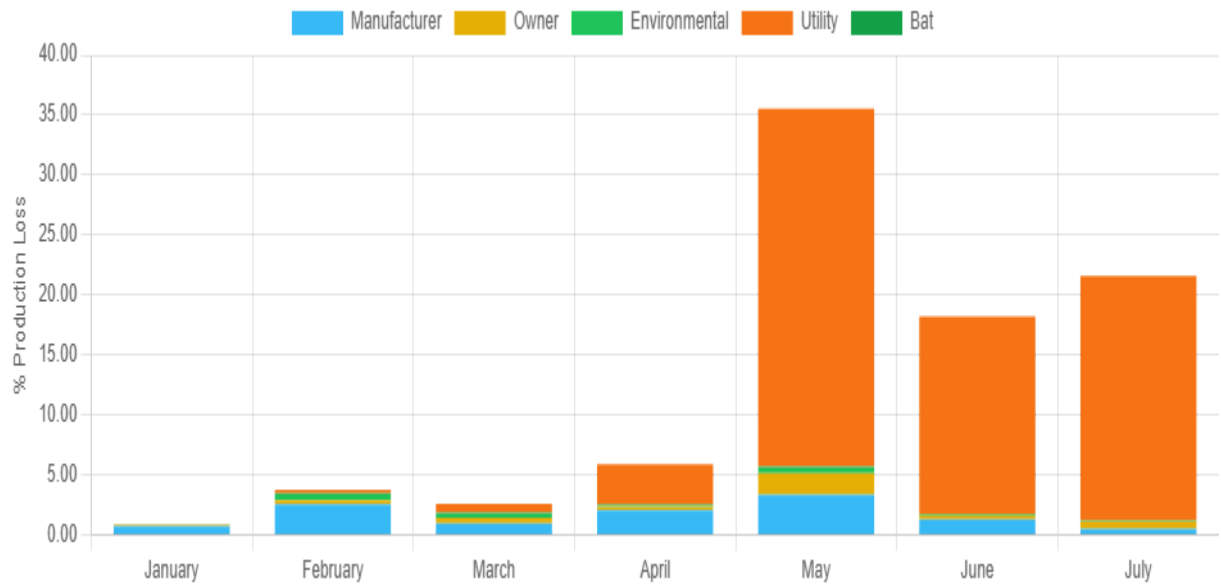

WIND SPEED

